

Job Name: 26-1899 - Gateway 65 Industrial Road  
Job Location: Franklin, KY  
Contractor: RD Sitework LLC

Plant: 100

6/4/2026 4:39:09 PM

Tech: Jared - F  
PC: E. Bardley



## Structure ID: 11 ST-CI

### P2 MH048LD12-24X36RECT


### MH FLAT TOP w/24"x36" Hole F/G

- P3) 24" x 36" - CASTING HEIGHT - 6"  
P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12"  
P1) 48" - MH BASE T/n - 42"  
1) CASTING - HOE 525 SET FLAT GRATE (F/G/H)  
1) 48" - Conseal CS-102 1.00"  
1) 24" x 36" - Conseal CS-102 1.00"  
1) Hole - 22"

Structure Total: 5842 lb

#### Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
  2. CONCRETE = 4,000 PSI AT 28 DAYS.
  3. NO STEPS AND NO INVERT CHANNEL.
  4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)).
  5. CITY OF BGKY-CBI TYPE F.
- REINFORCING PER ASTM A615 (GRADE 60).  
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..  
- RISER/WALLS (As .12)  
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

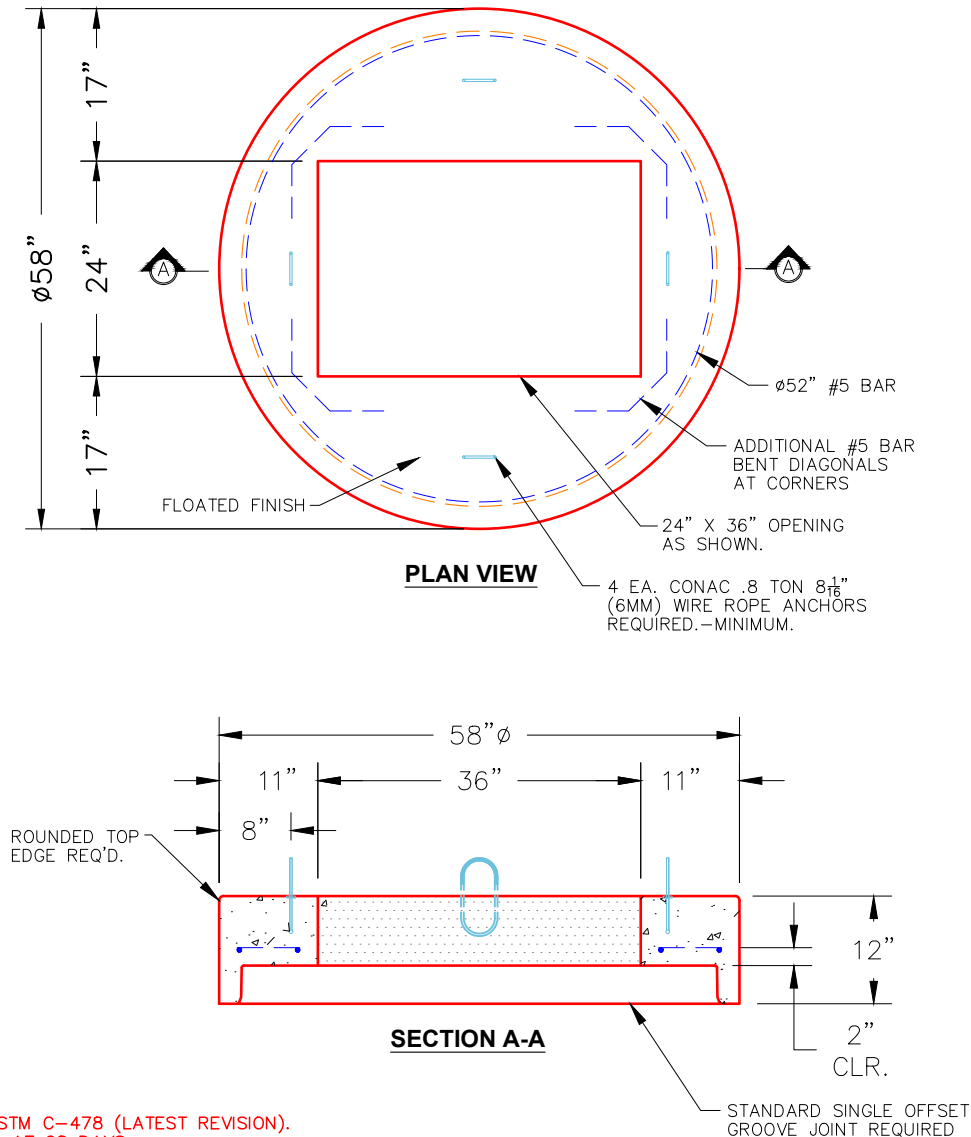

#### NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1300 lb  
Volume (Net): 0.46cu.yd
