

Contractor: RD Sitework LLC

Plant: 100



Size: 48"

Rim to Invert: 5.22'

Floor Height: 6"

Slack: 0.64"



REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

2) Hole - 22


0 lb

Structure Total: 5817 lb

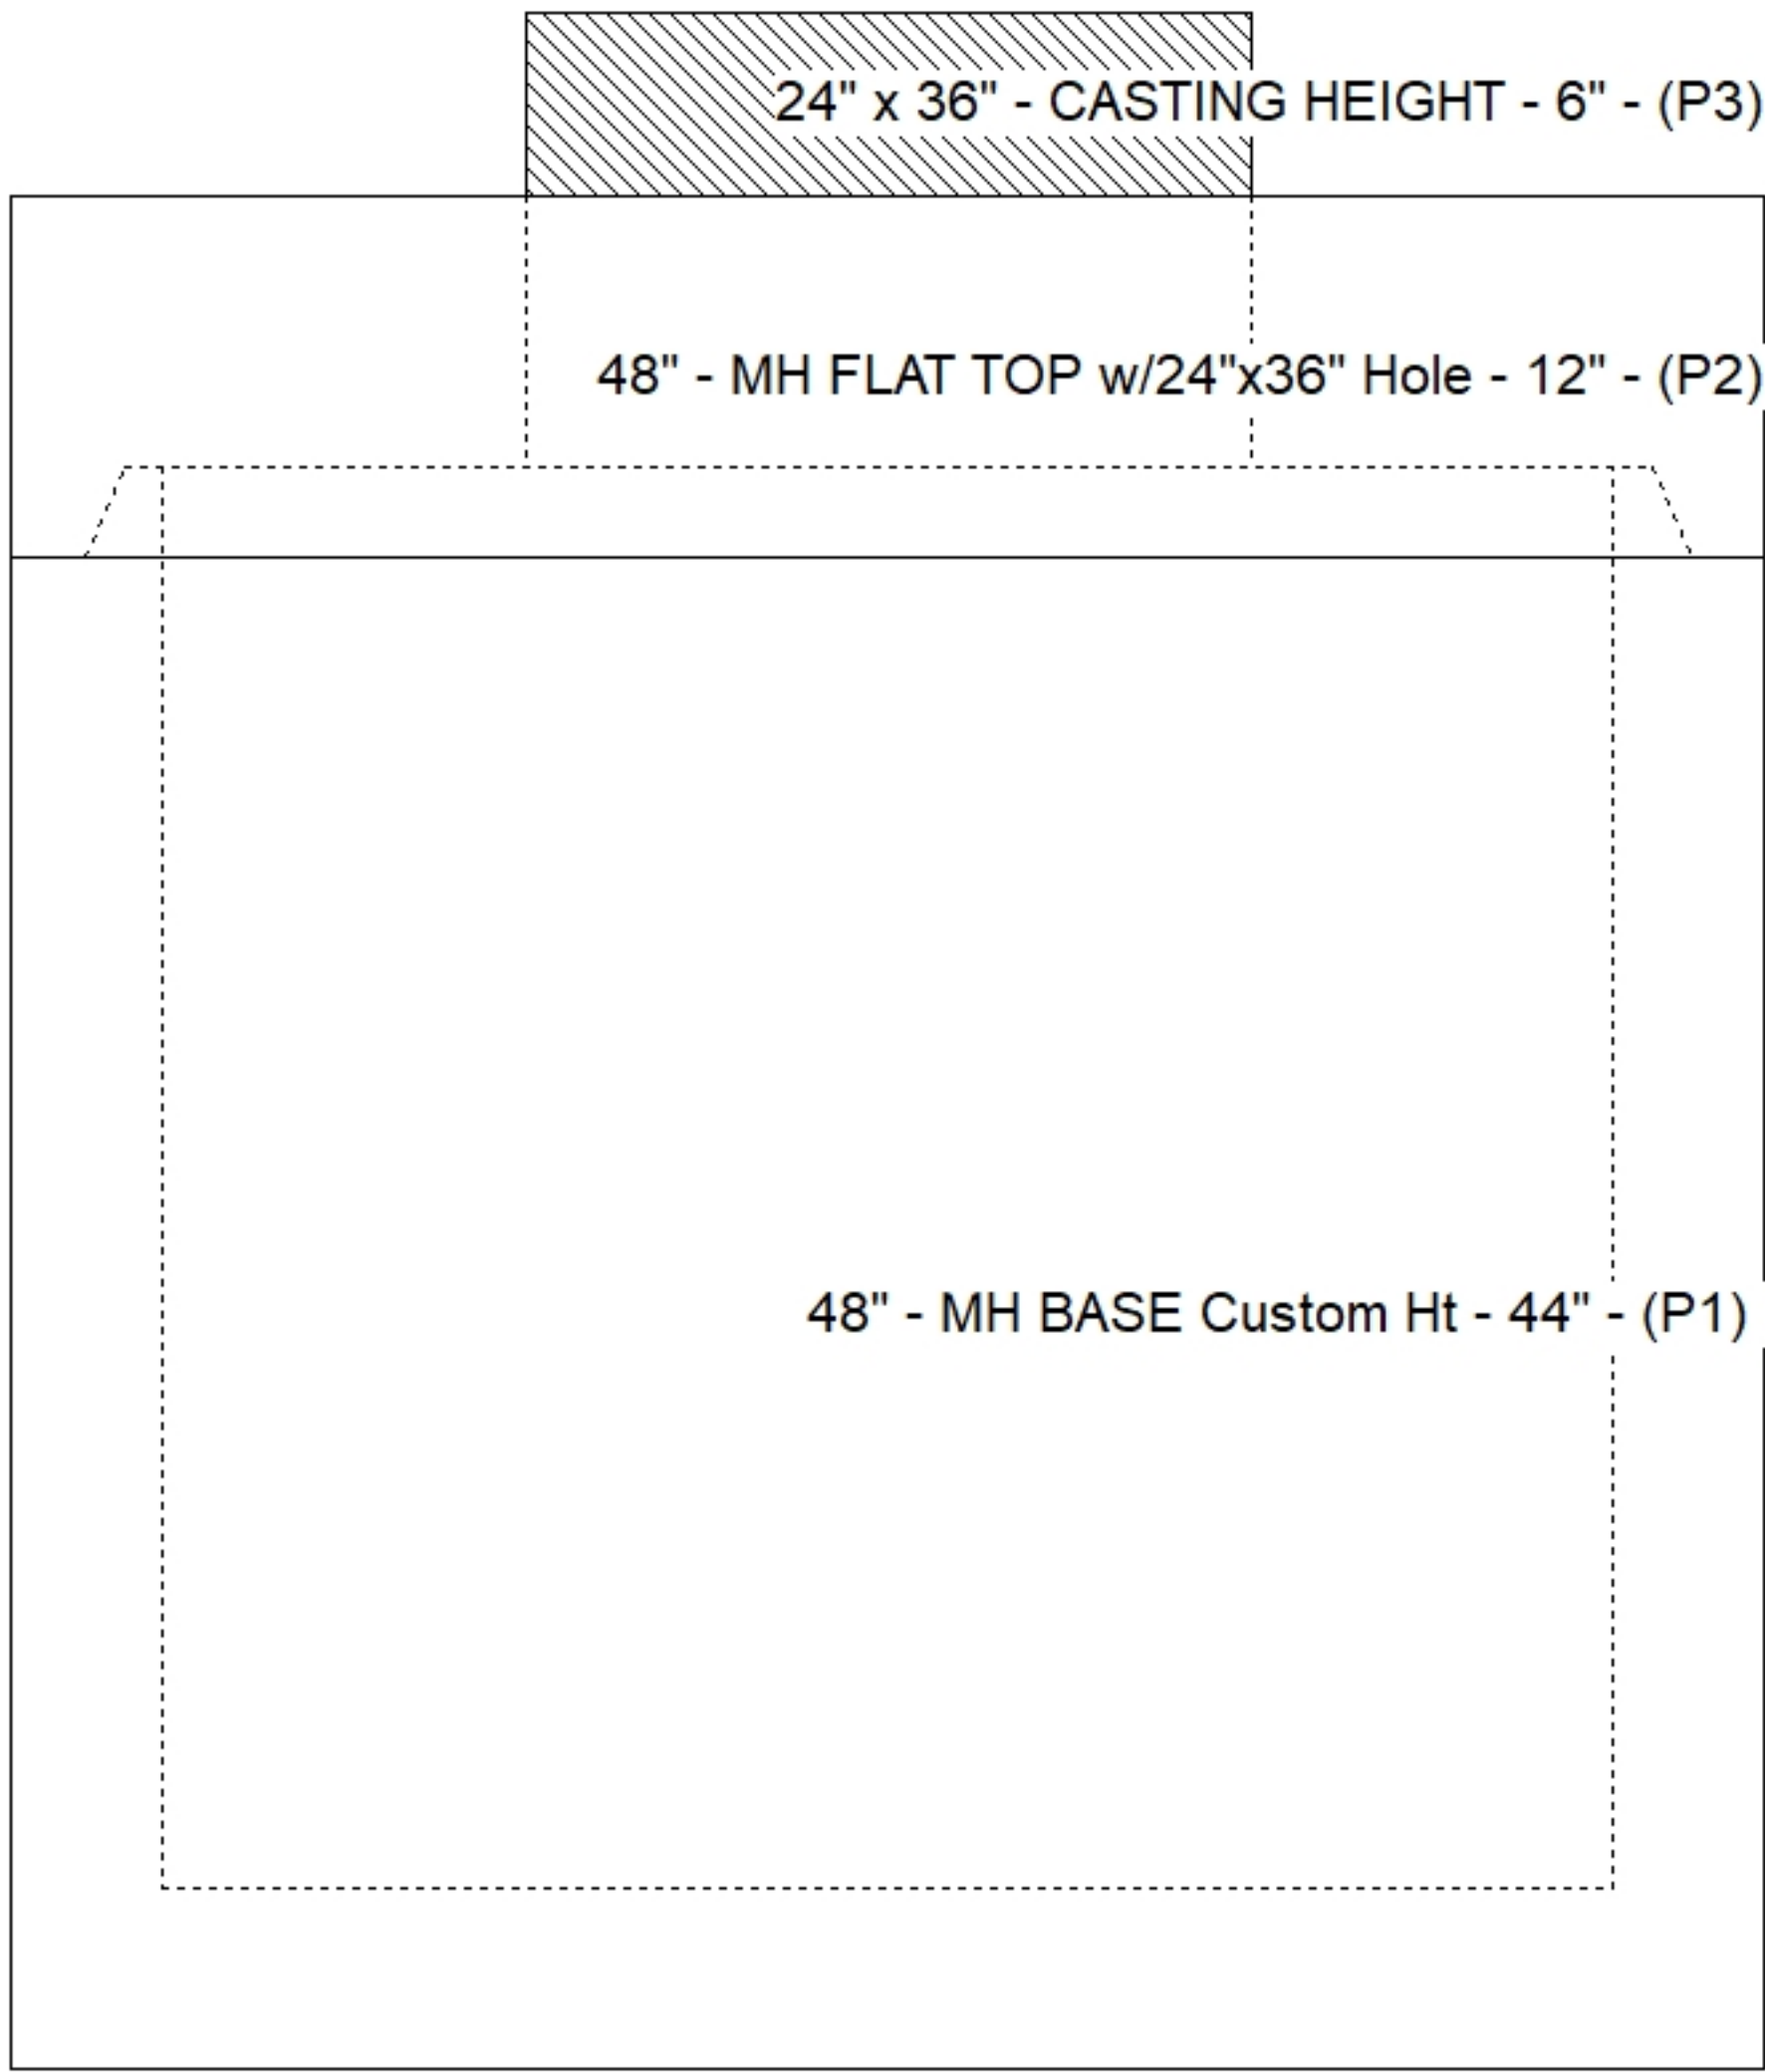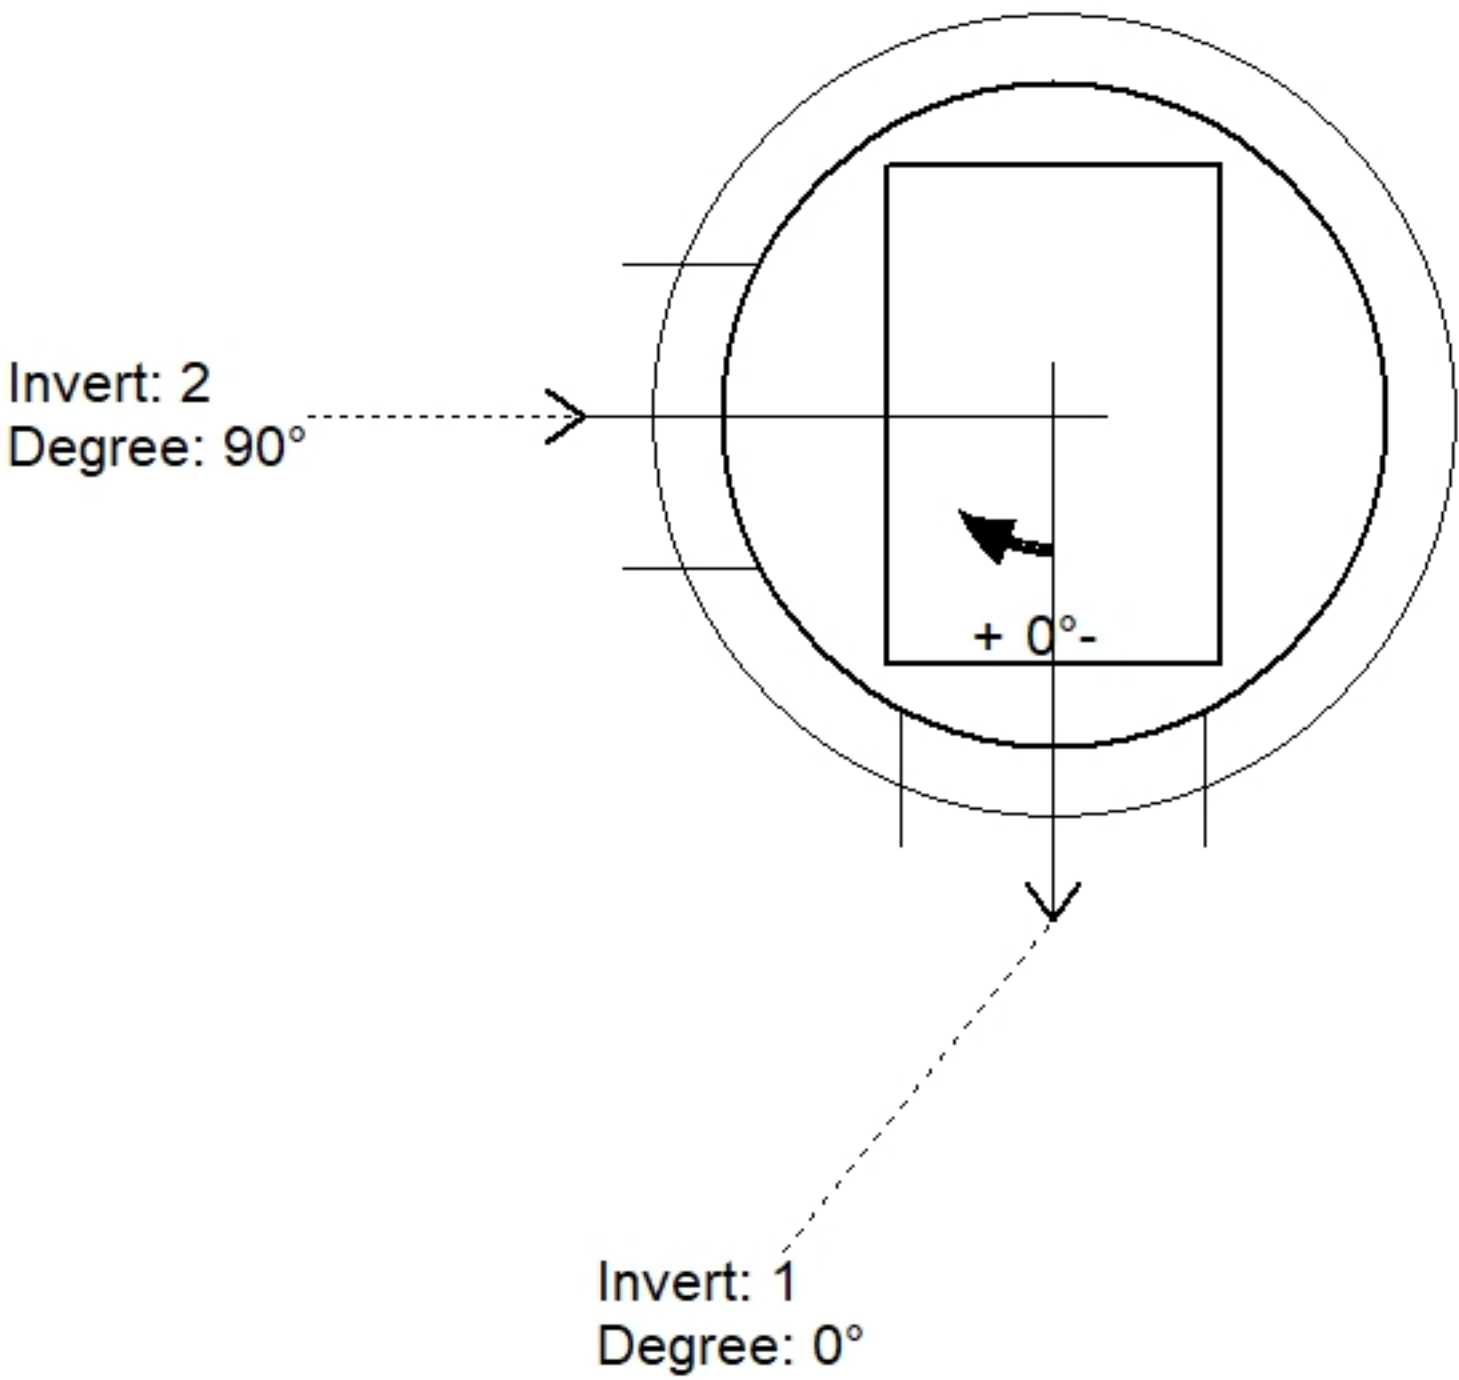

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	691.37'							
Reducer								
Invert 1	686.15'	0°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 2	686.15'	90°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

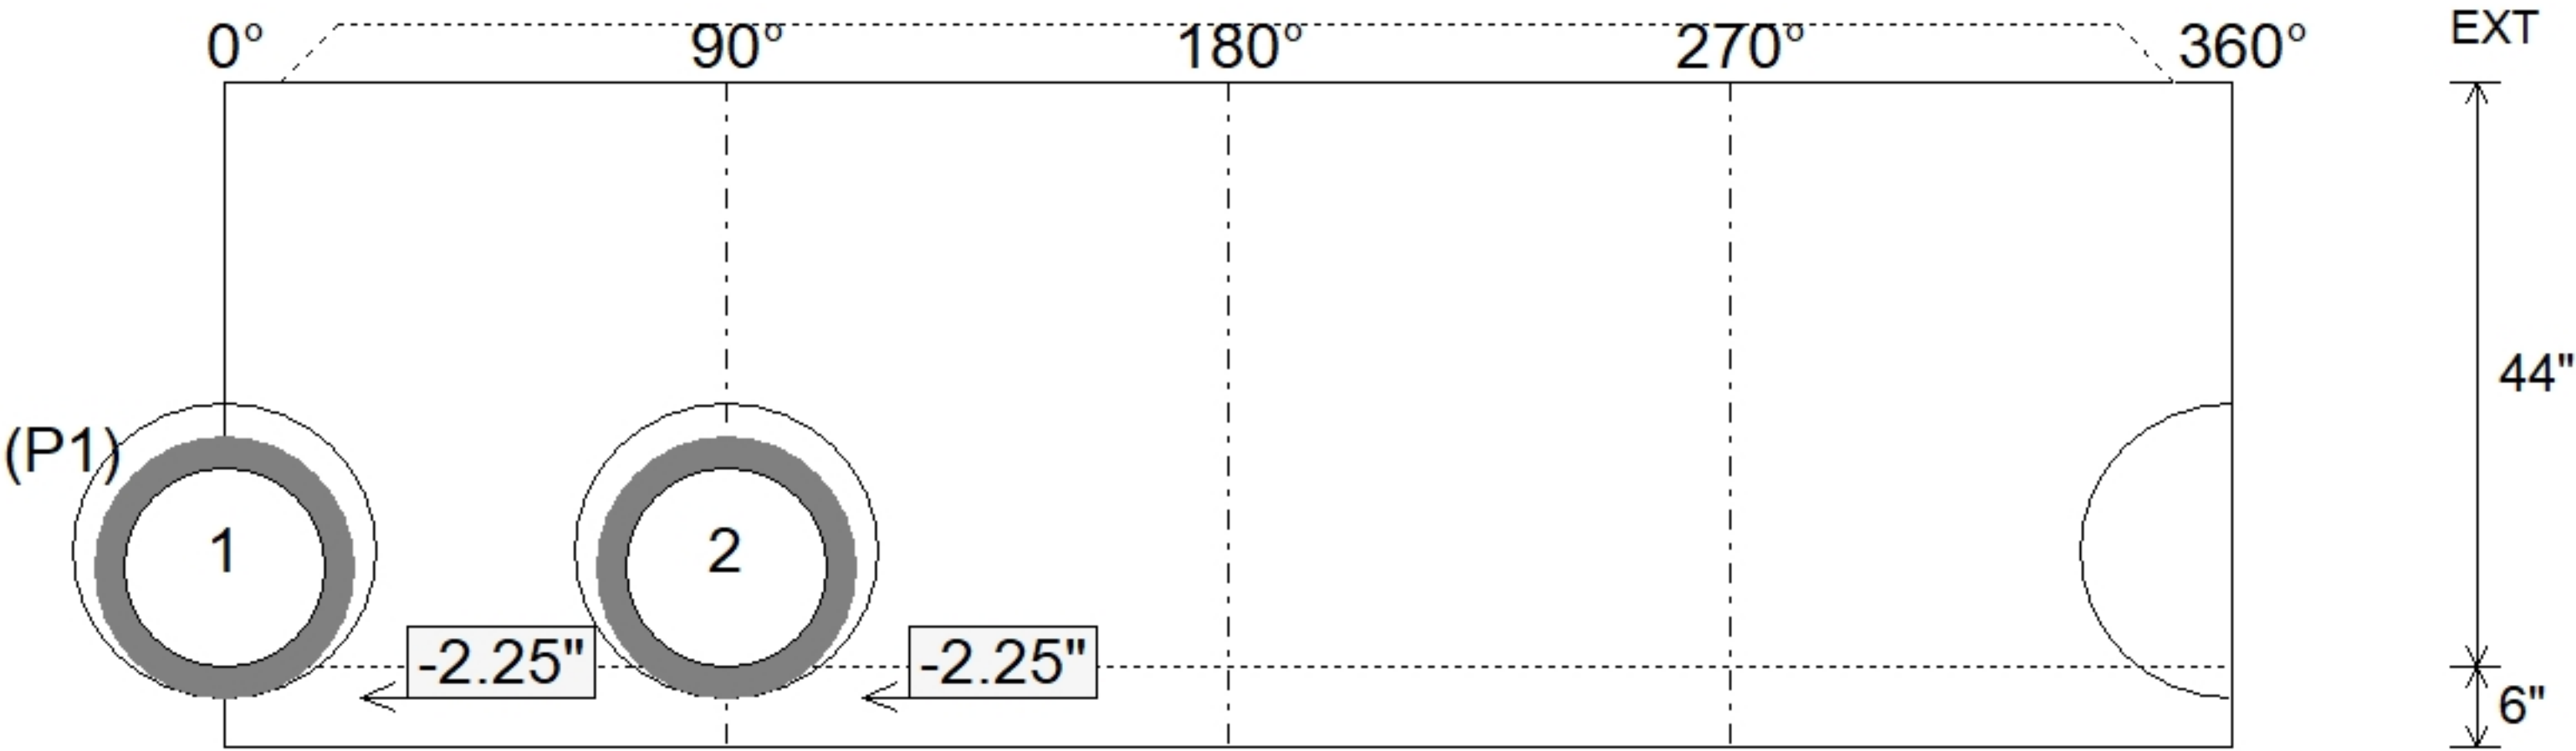

SUBMITTAL
APPROVED BY:
