

Contractor: RD Sitework LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 6.68'

Floor Height: 6"

Slack: 0.16"

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)).
5. CITY OF BGKY-CBI TYPE F.

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

0 lb

1300 lb

5195 lb


442 lb

0 lb

0 lb


0 lb

Structure Total: 6937 lb

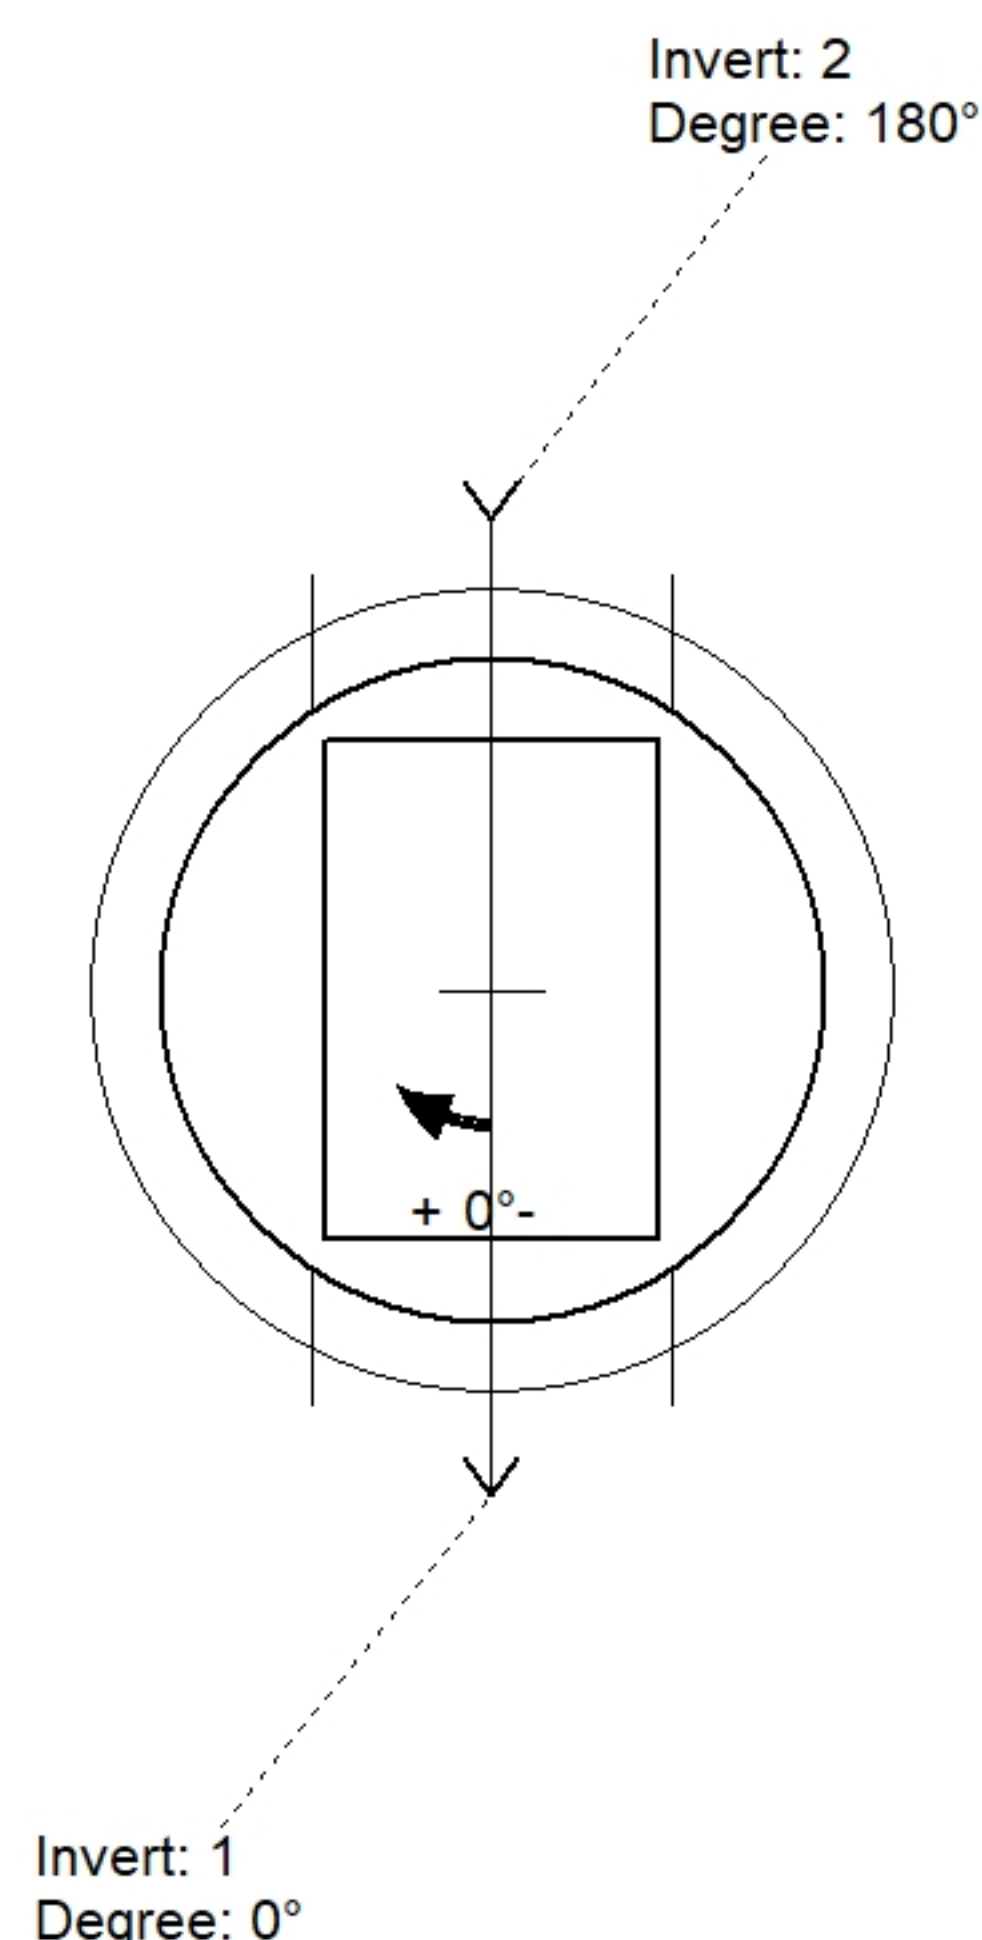

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	676.82'							
Reducer								
Invert 1	670.14'	0°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	670.14'	180°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

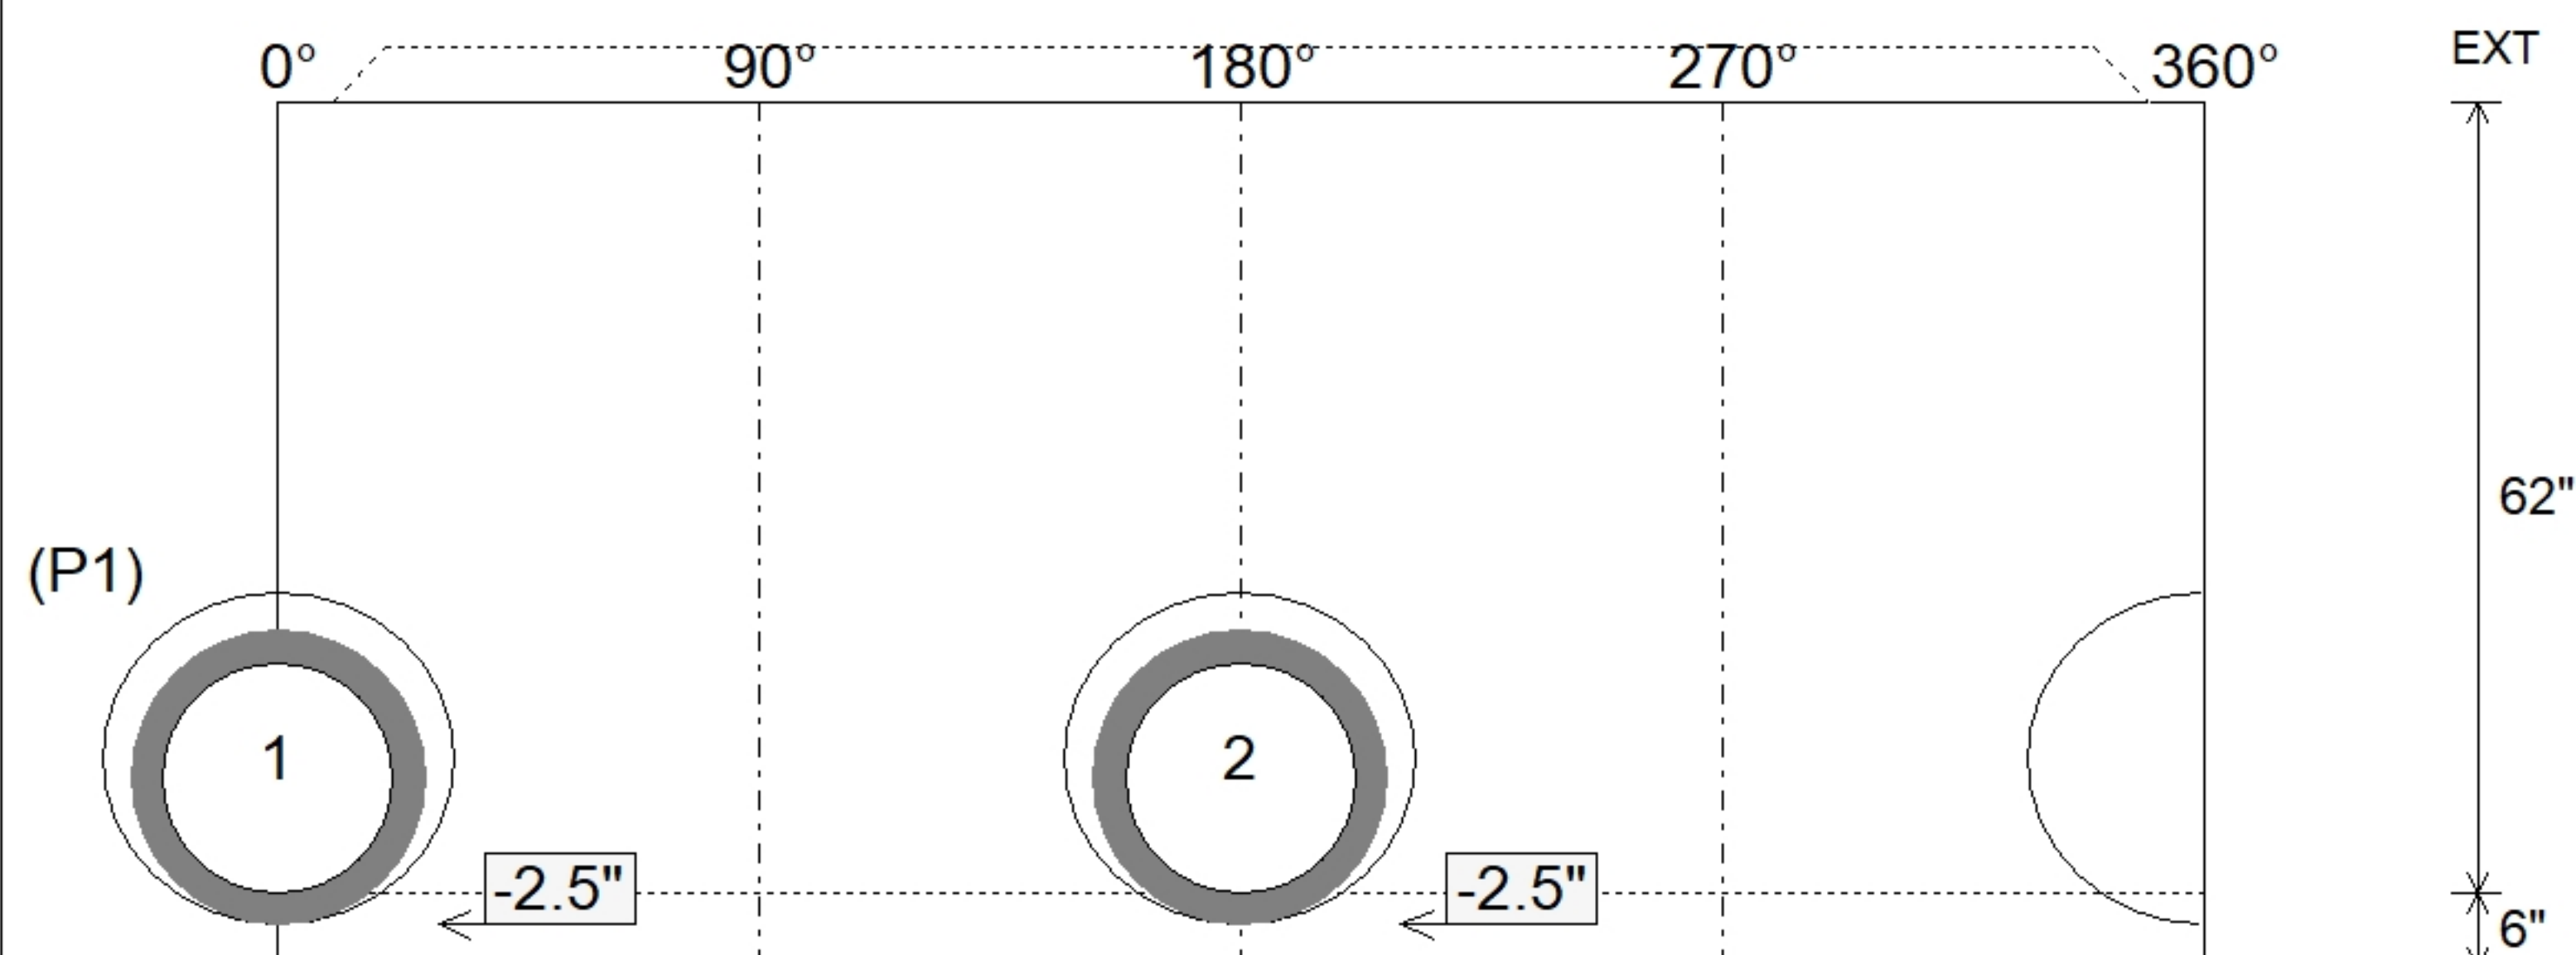

Submittal Drawing
6/8/2026 12:38:52 PM

SUBMITTAL
APPROVED BY:
