



Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC					Plant: 100 6/4/2026 4:33:55 PM		Tech: Jared - F PC: E. Bardley				
Structure ID: 2 ST-MH											
P1 MH048BAVF		MH BASE Custom Ht T/n									
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" Center Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 47" 1) CASTING - HOE MC-375 F/C Storm 1) 48" - Conseal CS-102 1.00" 2) Hole - 26 1) Hole - 22 4) MH Step ML-10-TDS-NCR - 10"					0 lb 1580 lb 3983 lb 271 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 5834 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE MC-375 F/C STORM). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 679.3' Rim to Invert: 5.53' Slack: 0.36" Sump: 0" Step Position: 270											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	673.77'	0°	0"	18" RCP B WALL	23"	Hole 26	26"	27.476"	-2.5"	0"	
Invert 2	673.77'	107°	54.125"	15" RCP B WALL	19.5"	Hole 22	22"	22.854"	-2.25"	0"	
Invert 3	673.77'	173°	87.625"	18" RCP B WALL	23"	Hole 26	26"	27.476"	-2.5"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

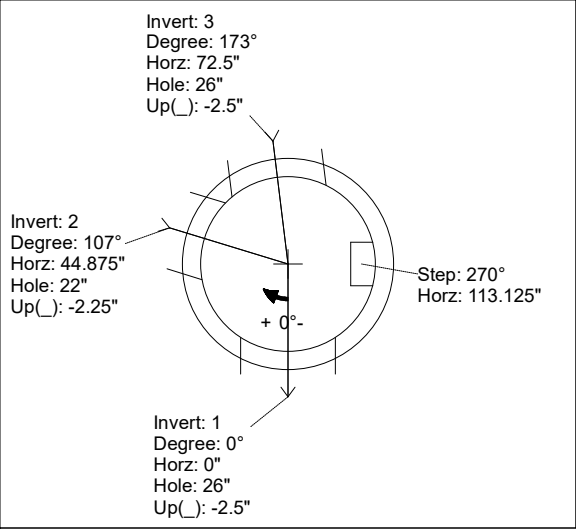

RIGHT-SIDE UP VIEW (int. dimensions)

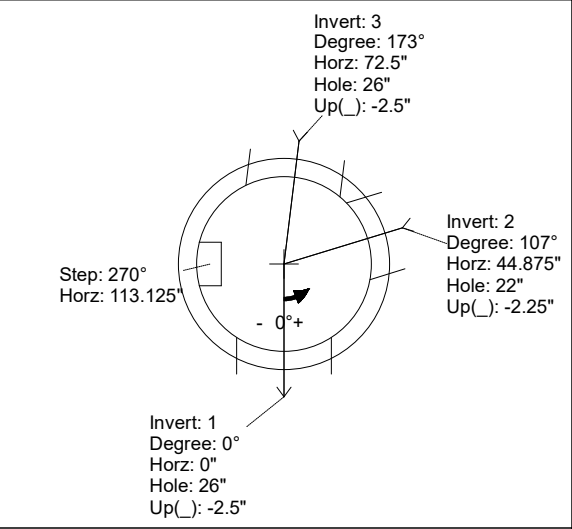

UPSIDE-DOWN VIEW (int. dimensions)


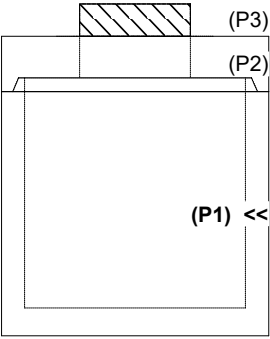


Diagram showing the structure components (P1, P2, P3) and their relative positions.

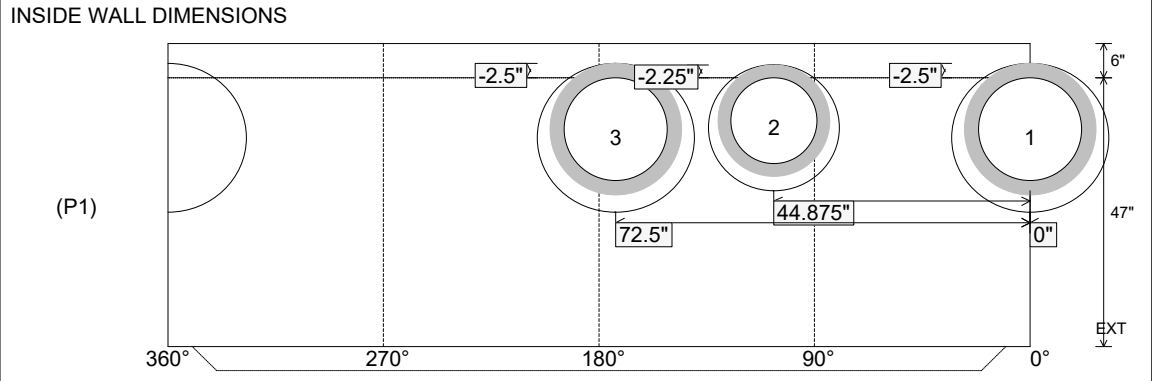

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 47" Height (Ext): 53"	Weight (Net): 3983 lb Volume (Net): 1.02cu.yd
----------------------------------	---------------------------------	--	--	--
