

Contractor: RD Sitework LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 5'

Floor Height: 6"

Slack: 0"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

1) 48" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 26
1) Hole - 22



0 lb
1300 lb
3866 lb
442 lb
0 lb
0 lb
0 lb
0 lb

Structure Total: 5608 lb

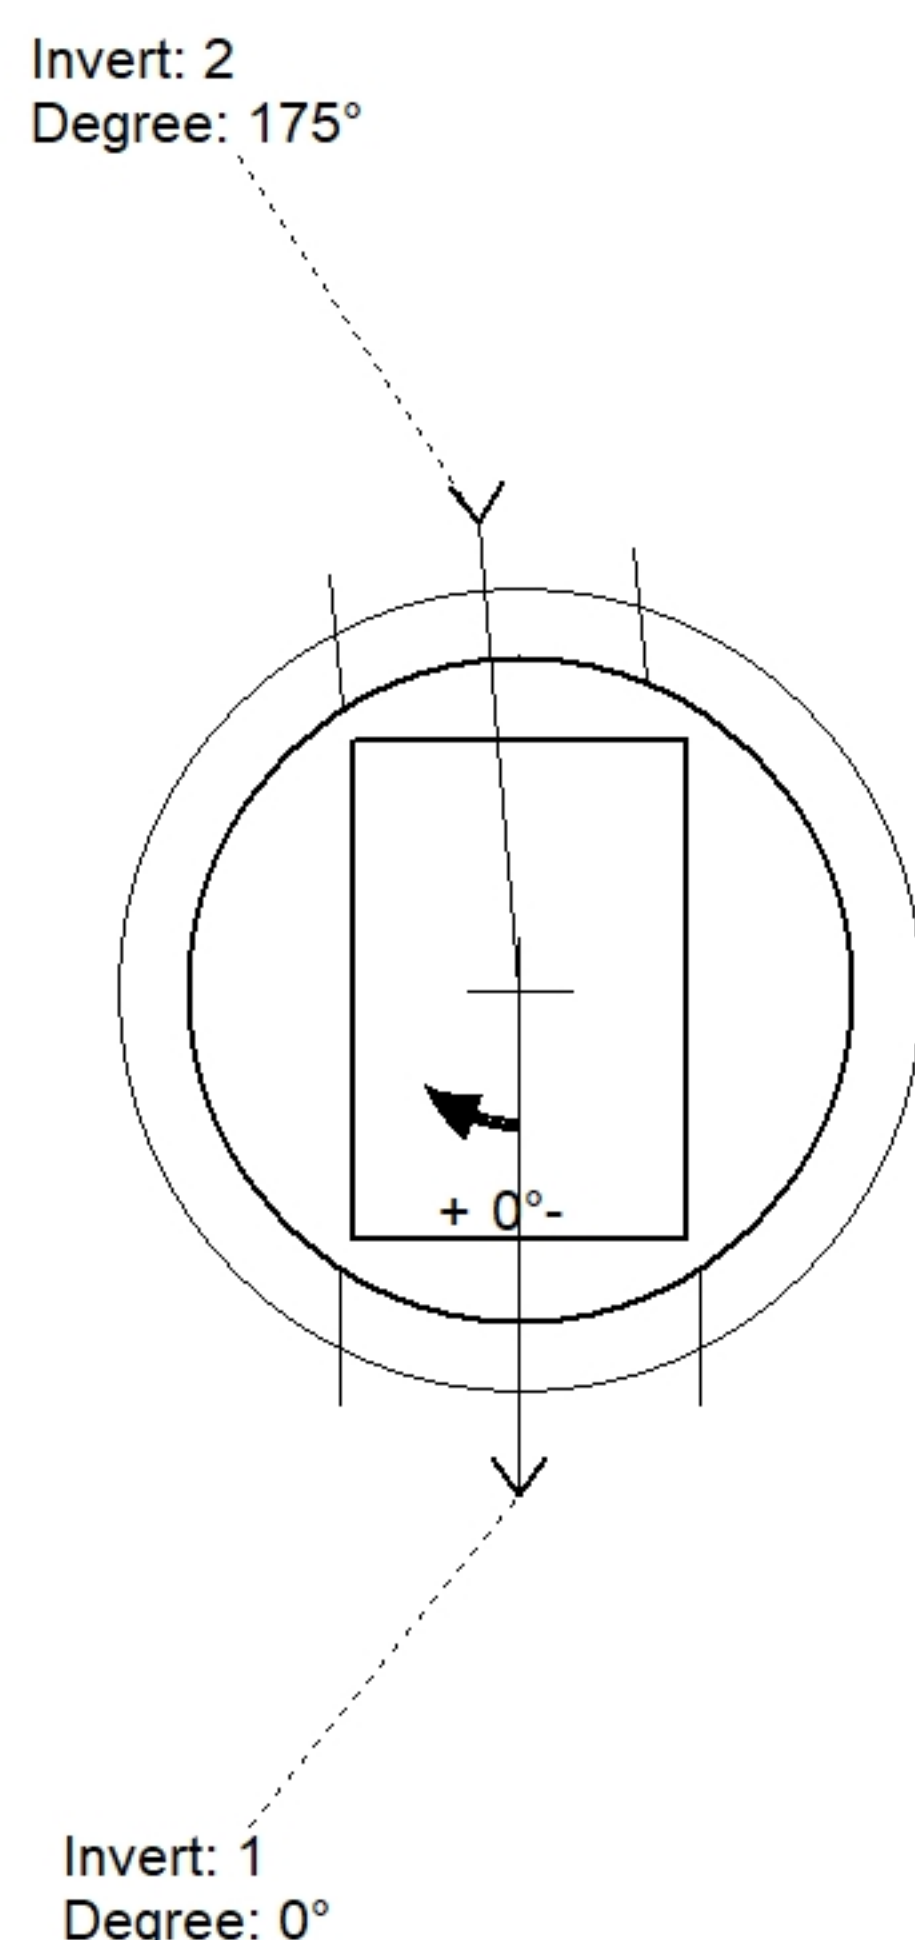

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	677.14'							
Reducer								
Invert 1	672.14'	0°	18" RCP B WALL	23"	26"	Hole 26	-2.5"	P1
Invert 2	672.14'	175°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

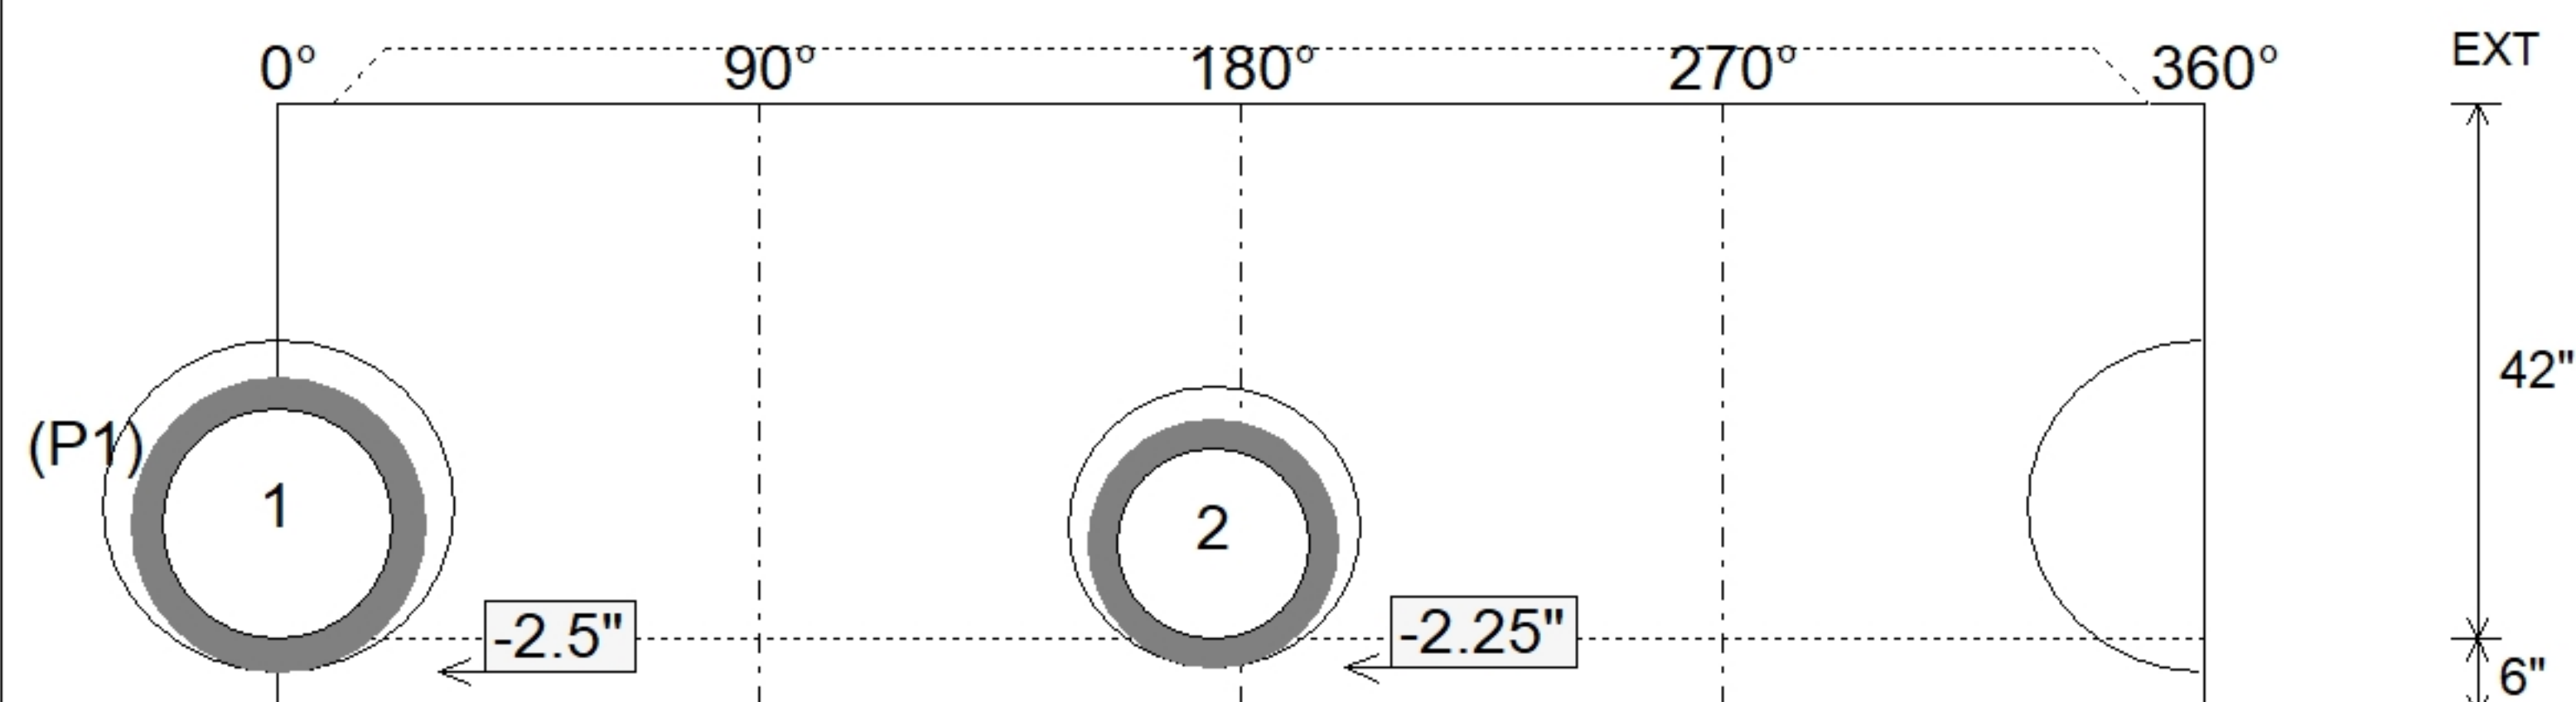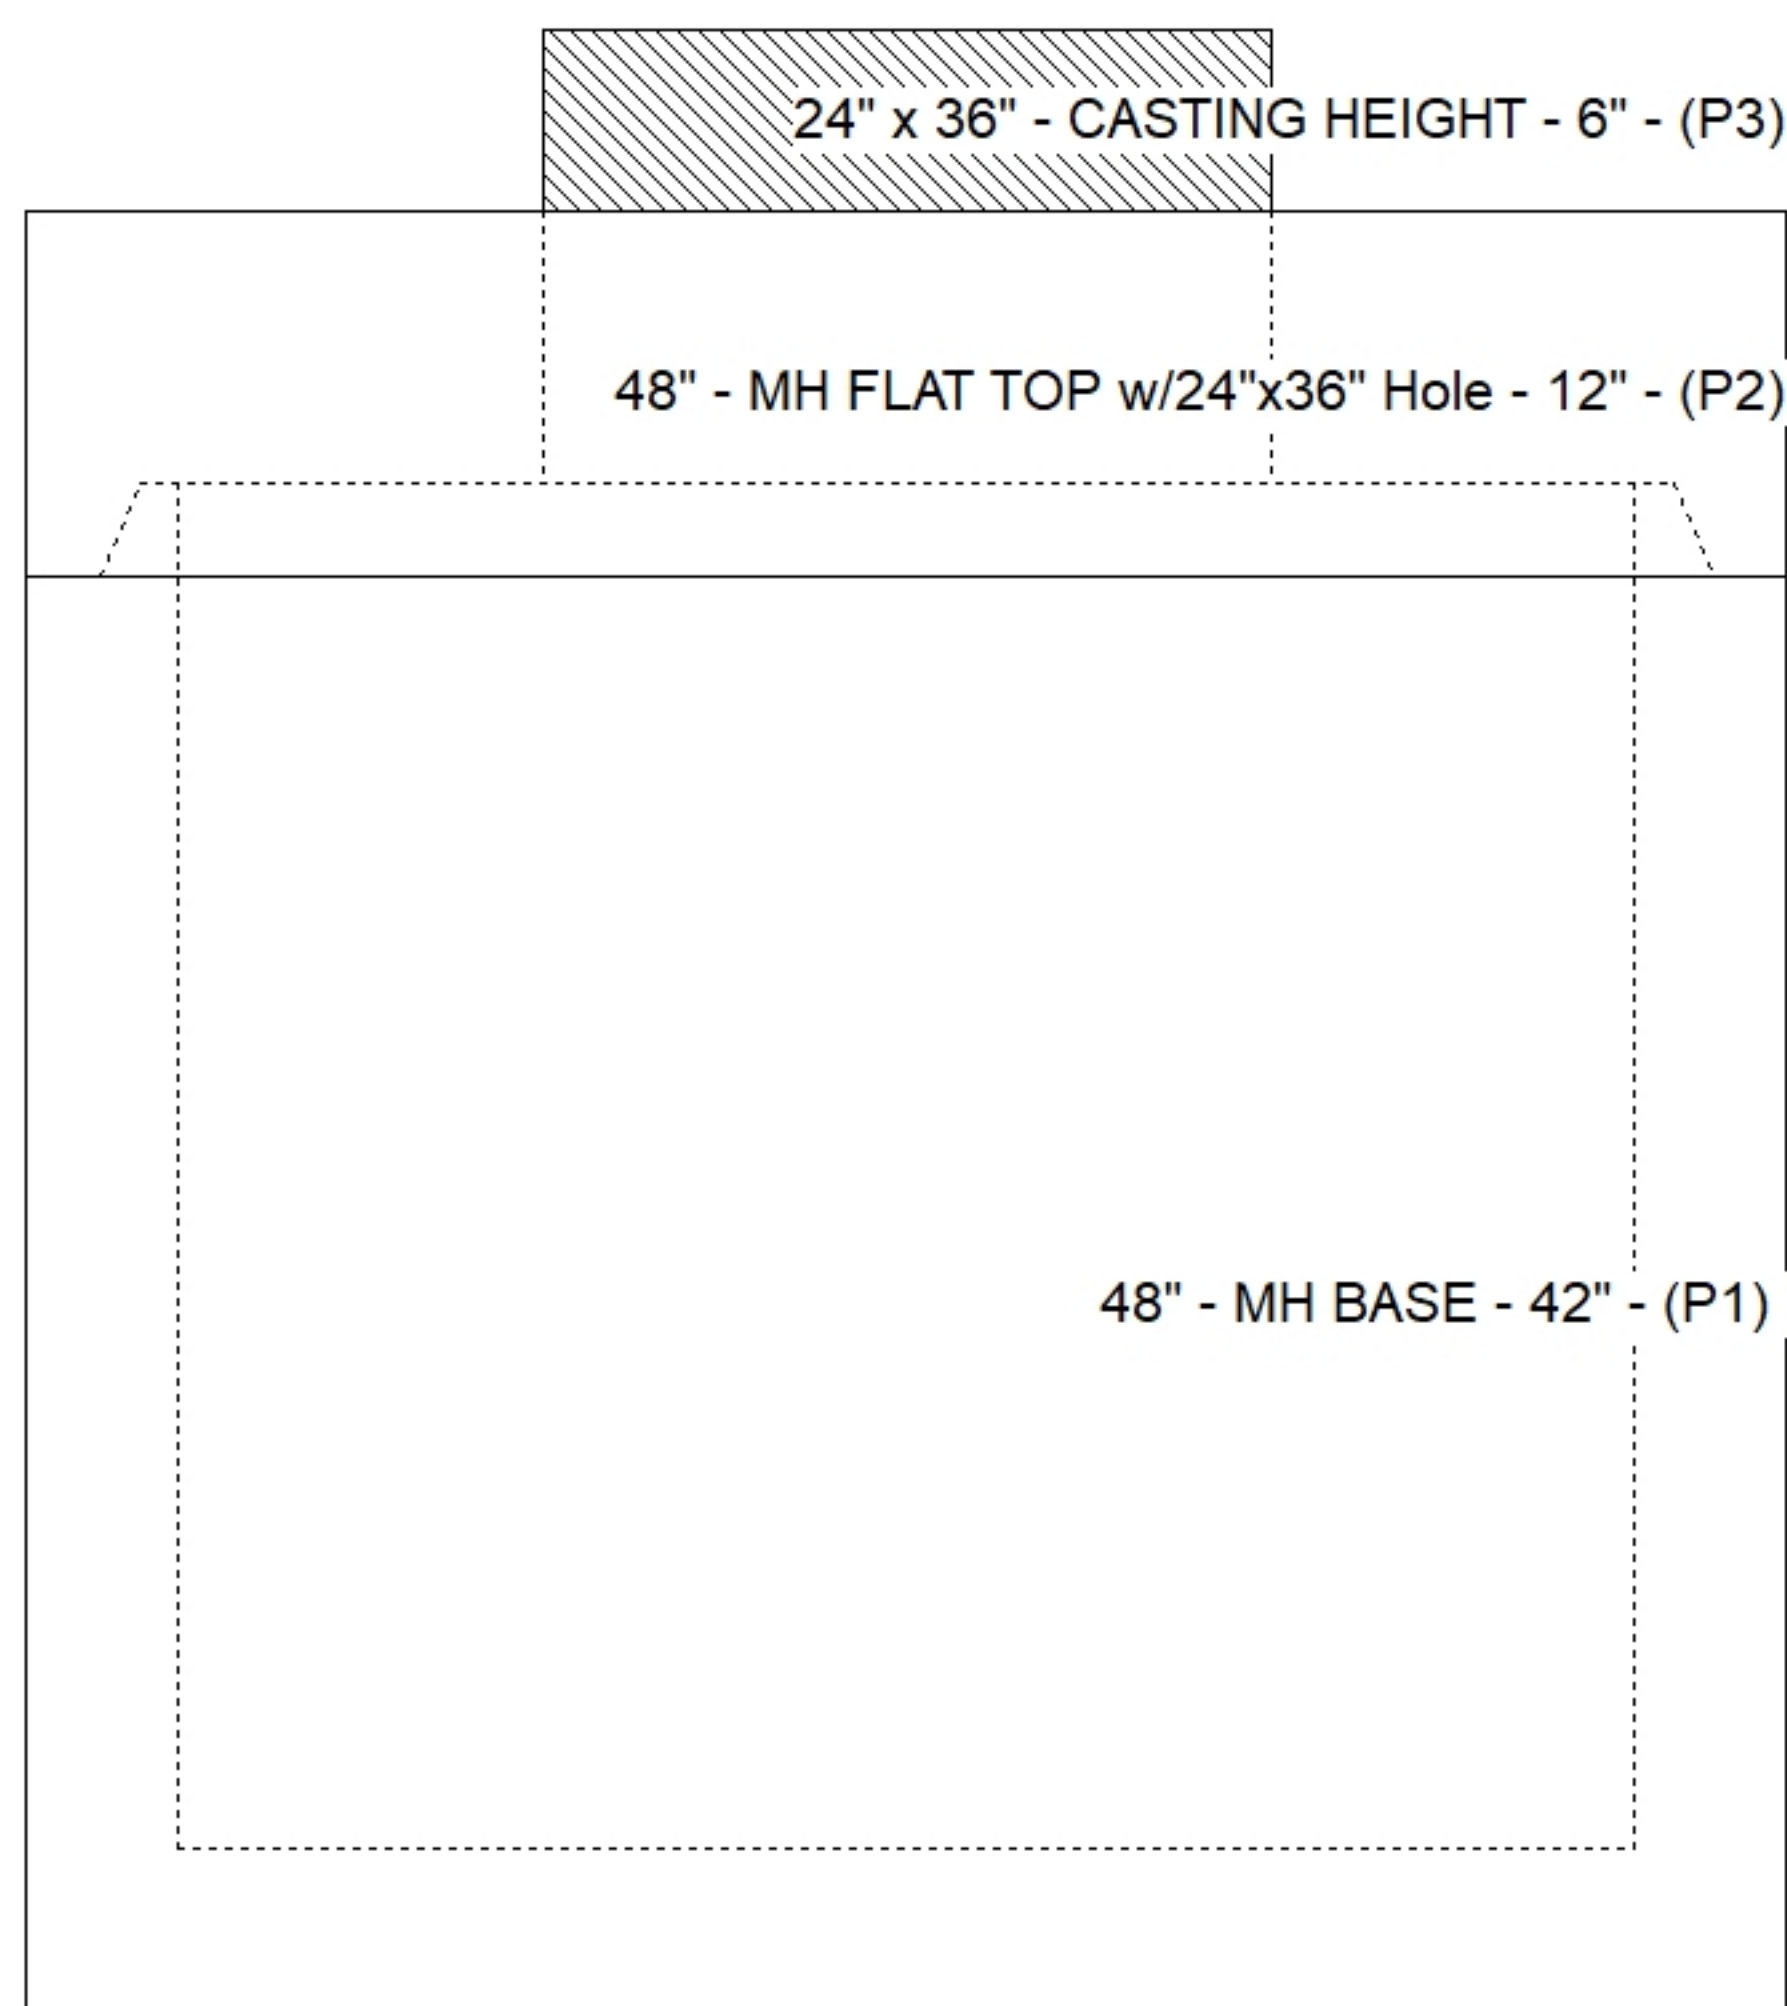

Submittal Drawing
6/8/2026 12:38:52 PM

SUBMITTAL
APPROVED BY:
