



Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC					Plant: 100 6/4/2026 4:34:07 PM		Tech: Jared - F PC: E. Bardley				
Structure ID: 25 ST-DCI											
P1 BX036084-08BAVF					BOX BASE 8inW, 8inF, Variable Ht F/n						
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F - 8" P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58" 1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H) 1) 36" x 84" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 46 2) Hole - 22 1) Hole - 40					0 lb 2911 lb 11612 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 14964 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 DBL SET FLAT GRATE (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .47) #5 BARS AT 8" C.C.E.W. - FLOOR (As .47) #5 BARS AT 8" C.C.E.W.				
Rim: 687.19' Rim to Invert: 6' Slack: 0" Sump: 0" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	681.19'	90°	50"	36" RCP B WALL	44"	Hole 46	46"	46"	-4"	0"	
Invert 2	681.19'	180°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"	
Invert 3	681.19'	270°	50"	30" RCP B WALL	37"	Hole 40	40"	40"	-3.5"	0"	
Invert 4	681.19'	0°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

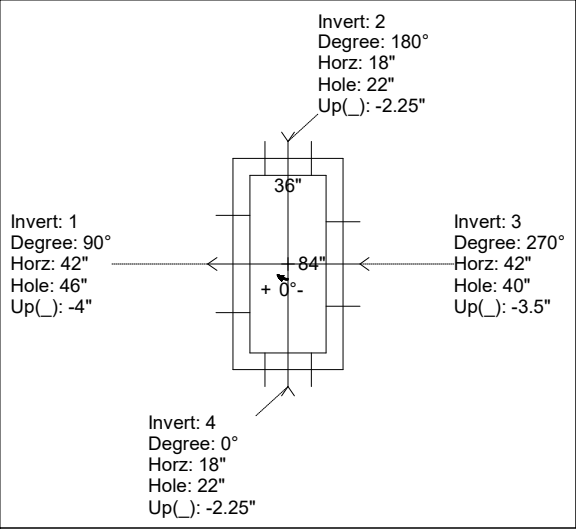


UPSIDE-DOWN VIEW (int. dimensions)

1ST POUR (FLOOR) = 3,490 LBS
2ND POUR (WALLS) = 8,122 LBS

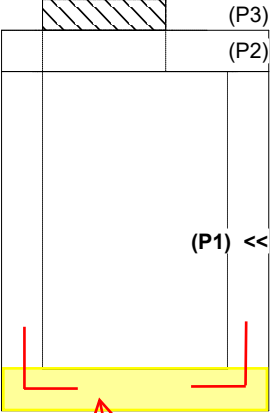

1ST POUR (FLOOR)
STUB #5 L BARS OUT
TOP FLOOR, SPA AT
12" C/C FOR
CONNECTING WALLS

INSIDE WALL DIMENSIONS

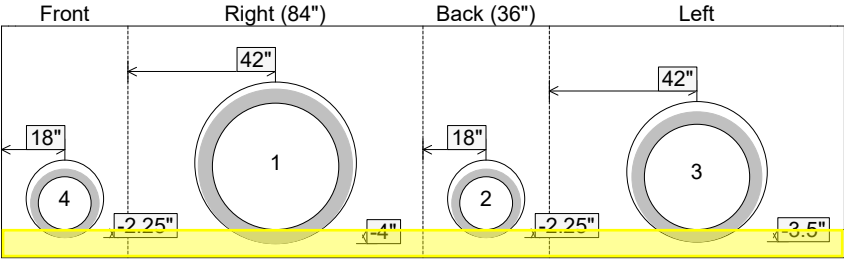

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 58" Height (Ext): 66"	Weight (Net): 11612 lb Volume (Net): 2.97cu.yd
----------------------------------	-------------------------------	--	--	---

Job Name: 26-1899 - Gateway 65 Industrial Road

Job Location: Franklin, KY

Contractor: RD Sitework LLC

Plant: 100

6/4/2026 4:34:07 PM

Tech: Jared - F

PC: E. Bardley



Structure ID: 25 ST-DCI

P1 BX036084-08BAVF

BOX BASE 8inW, 8inF, Variable Ht F/n

P3) 24" x 36" - CASTING HEIGHT - 6"

P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F - 8"

P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht F/n - 58"

1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H)

1) 36" x 84" - Conseal CS-102 1.00"

1) 24" x 36" - Conseal CS-102 1.00"

1) Hole - 46

2) Hole - 22

1) Hole - 40

0 lb

2911 lb

11612 lb

442 lb

0 lb

0 lb

0 lb

0 lb

0 lb

Structure Total: 14964 lb

Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.

2. CONCRETE = 4,000 PSI AT 28 DAYS.

3. NO STEPS AND NO INVERT CHANNEL.

4. CASTING BY ICAST (HOE 525 DBL SET FLAT GRATE (F/G/H)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.

- WALLS (As .47) #5 BARS AT 8" C.C.E.W.

- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Rim: 687.19'

Rim to Invert: 6'


Slack: 0"

Sump: 0"

Step Position:

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	681.19'	90°	50"	36" RCP B WALL	44"	Hole 46	46"	46"	-4"	0"
Invert 2	681.19'	180°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"
Invert 3	681.19'	270°	50"	30" RCP B WALL	37"	Hole 40	40"	40"	-3.5"	0"
Invert 4	681.19'	0°	26"	15" RCP B WALL	19.5"	Hole 22	22"	22"	-2.25"	0"
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

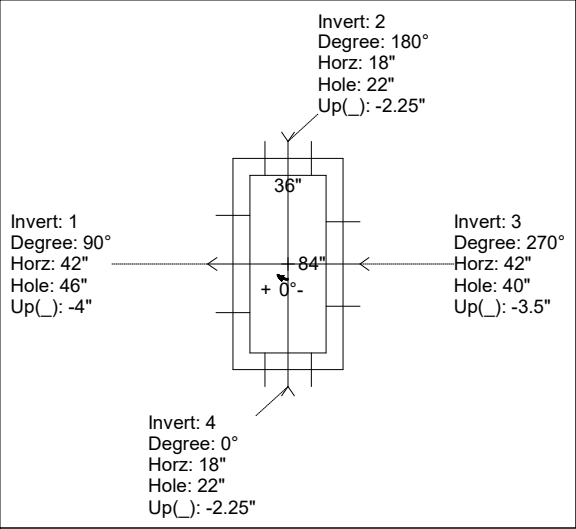

UPSIDE-DOWN VIEW (int. dimensions)


1ST POUR (FLOOR) = 3,490 LBS

2ND POUR (WALLS) = 8,122 LBS

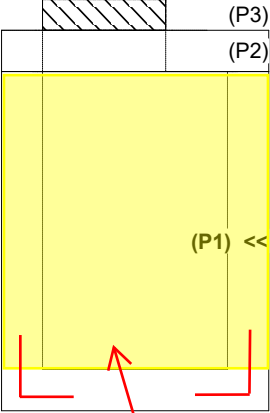

2ND POUR (WALLS)

INSIDE WALL DIMENSIONS

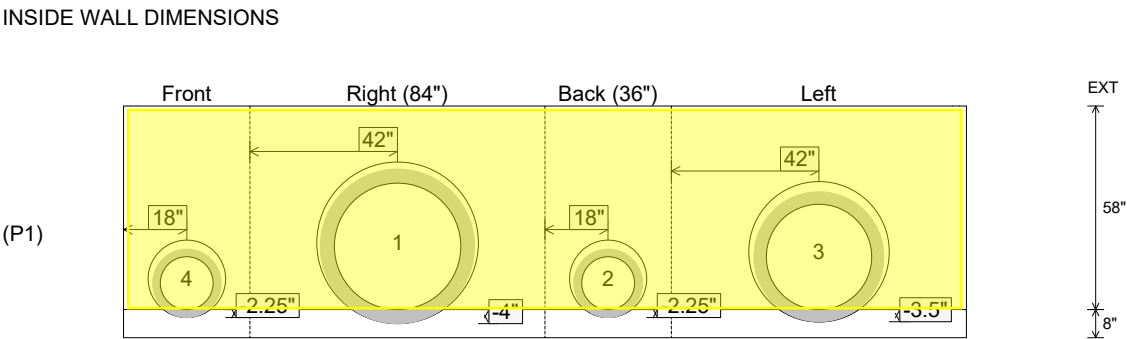

Coating (Int):

Coating (Ext):

Seam Up: Flat

Seam Dn: n/a

Wall Thickness: 8"

Floor Height: 8"

Height (Int): 58"

Height (Ext): 66"

Weight (Net): 11612 lb

Volume (Net): 2.97cu.yd
