

Job Name: 26-1899 - Gateway 65 Industrial Road
Job Location: Franklin, KY
Contractor: RD Sitework LLC

Plant: 100

6/4/2026 4:39:20 PM

Tech: Jared - F
PC: E. Bardley



Structure ID: 49 ST-DCI

P2 BX036084-08LD08SP

CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F

P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 36" x 84" - CB FLAT TOP 8"W SPEC. (2 - 24x36 HOLES) F/F - 8"
P1) 36" x 84" - BOX BASE 8inW, 8inF, Variable Ht F/n - 37"
1) CASTING - HOE 525 DBL SET FLAT GRATE (F/G/H)
1) 36" x 84" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 22


0 lb
2911 lb
9991 lb
442 lb
0 lb
0 lb
0 lb

Structure Total: 13344 lb


Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 525 DBL SET FLAT GRATE (F/G/H)).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .47) #5 BARS AT 8" C.C.E.W.
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

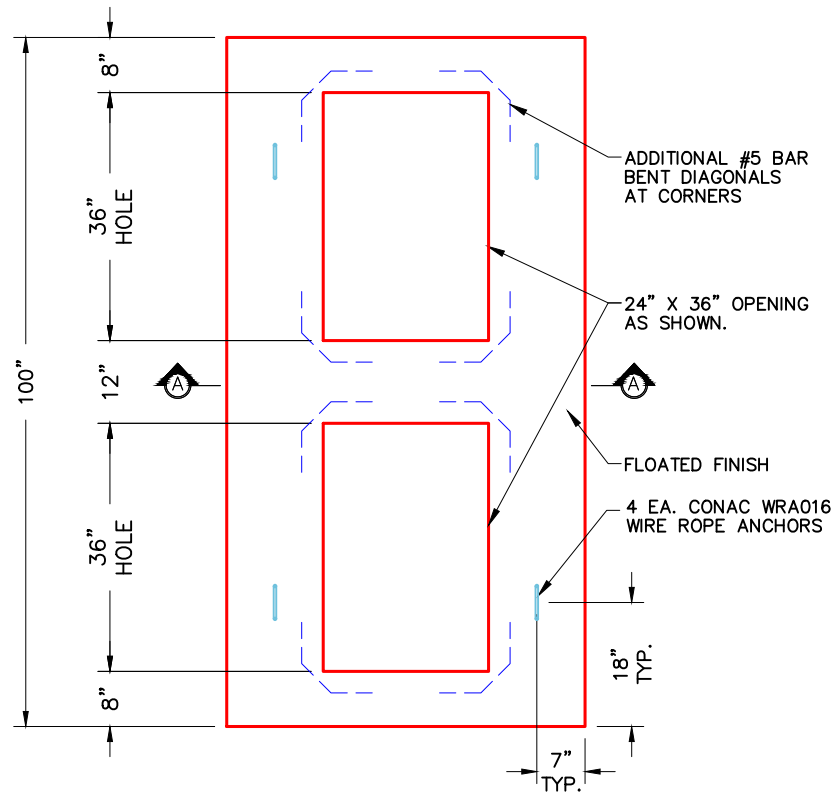

PLAN VIEW

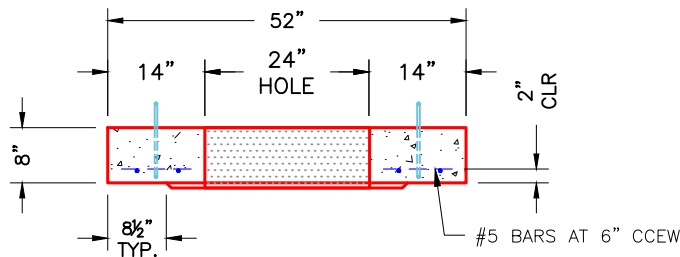

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 2911 lb
Volume (Net): 0.74cu.yd
