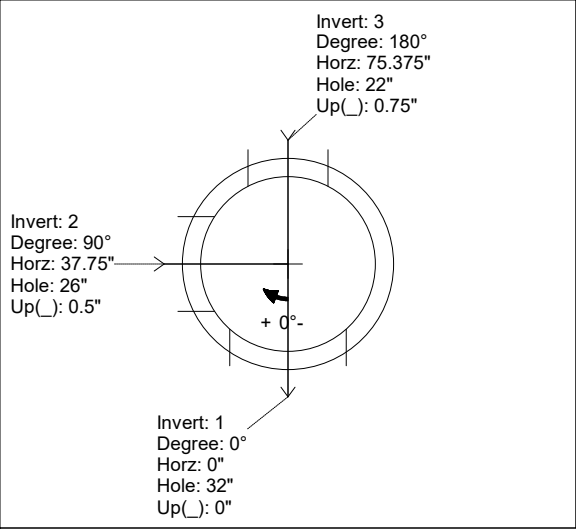
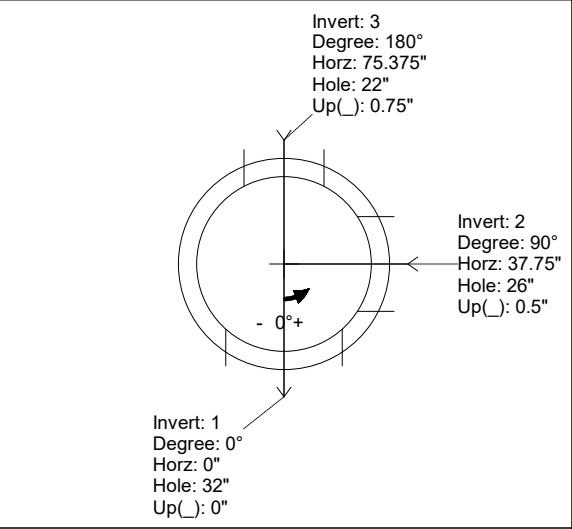
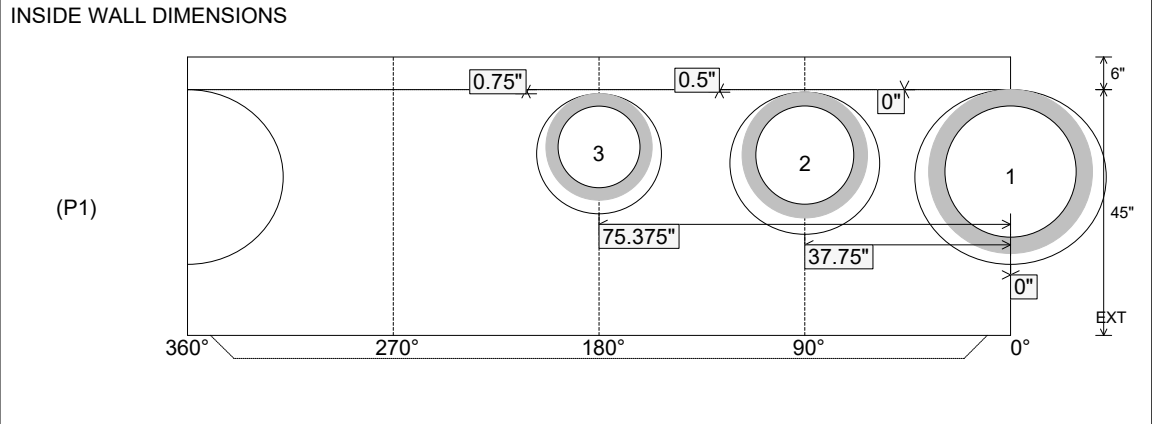


Job Name: 26-1899 - Gateway 65 Industrial Road Job Location: Franklin, KY Contractor: RD Sitework LLC					Plant: 100 6/4/2026 4:34:23 PM		Tech: Jared - F PC: E. Bardley						
Structure ID: 59 ST-CI													
P1 MH048BAVF		MH BASE Custom Ht T/n											
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole F/G - 12" P1) 48" - MH BASE Custom Ht T/n - 45" 1) CASTING - HOE 525 SET FLAT GRATE (F/G/H) 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 32 1) Hole - 26 1) Hole - 22						0 lb 1300 lb 3713 lb 442 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 5455 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 525 SET FLAT GRATE (F/G/H)). 5. CITY OF BGKY-CBI TYPE F. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 706.61'		Rim to Invert: 5'		Slack: 0"		Sump: 3"		Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset			
Invert 1	701.61'	0°	0"	24" RCP B WALL	30"	Hole 32	32"	35.027"	0"	0"			
Invert 2	701.61'	90°	45.5"	18" RCP B WALL	23"	Hole 26	26"	27.476"	0.5"	0"			
Invert 3	701.61'	180°	91.125"	15" RCP B WALL	19.5"	Hole 22	22"	22.854"	0.75"	0"			
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimensions)  INSIDE WALL DIMENSIONS  Coating (Int): Coating (Ext): Seam Up: Tongue Seam Dn: n/a Wall Thickness: 5" Floor Height: 6" Height (Int): 45" Height (Ext): 51" Weight (Net): 3713 lb Volume (Net): 0.95cu.yd													
