


Contractor: RD Sitework LLC

Plant: 100



Slack: 0.12"

Structure Total: 5632 lb

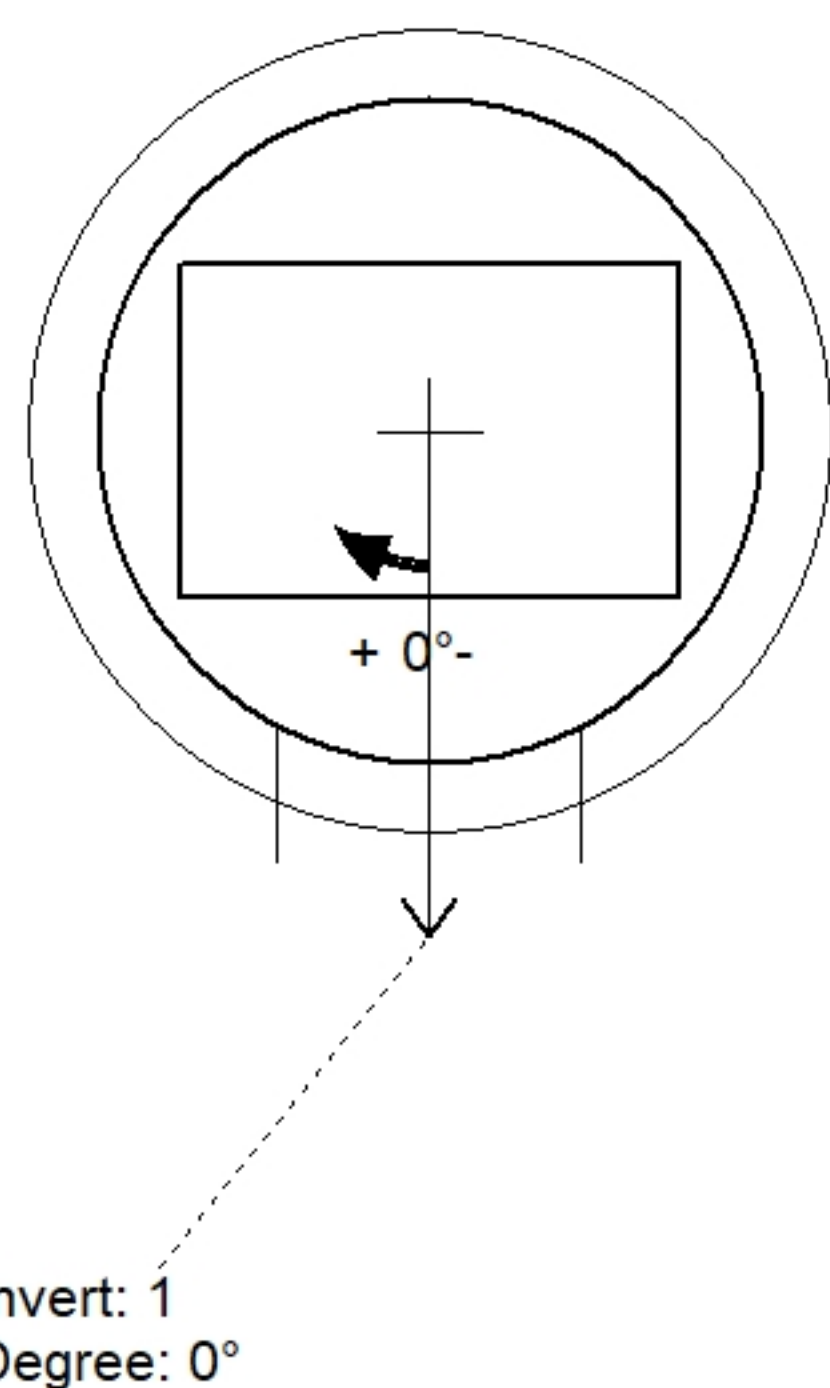


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	680.77'							
Reducer								
Invert 1	676.01'	0°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P3)

48" - MH FLAT TOP w/24"x36" Hole - 12" - (P2)

48" - MH BASE Custom Ht - 39" - (P1)

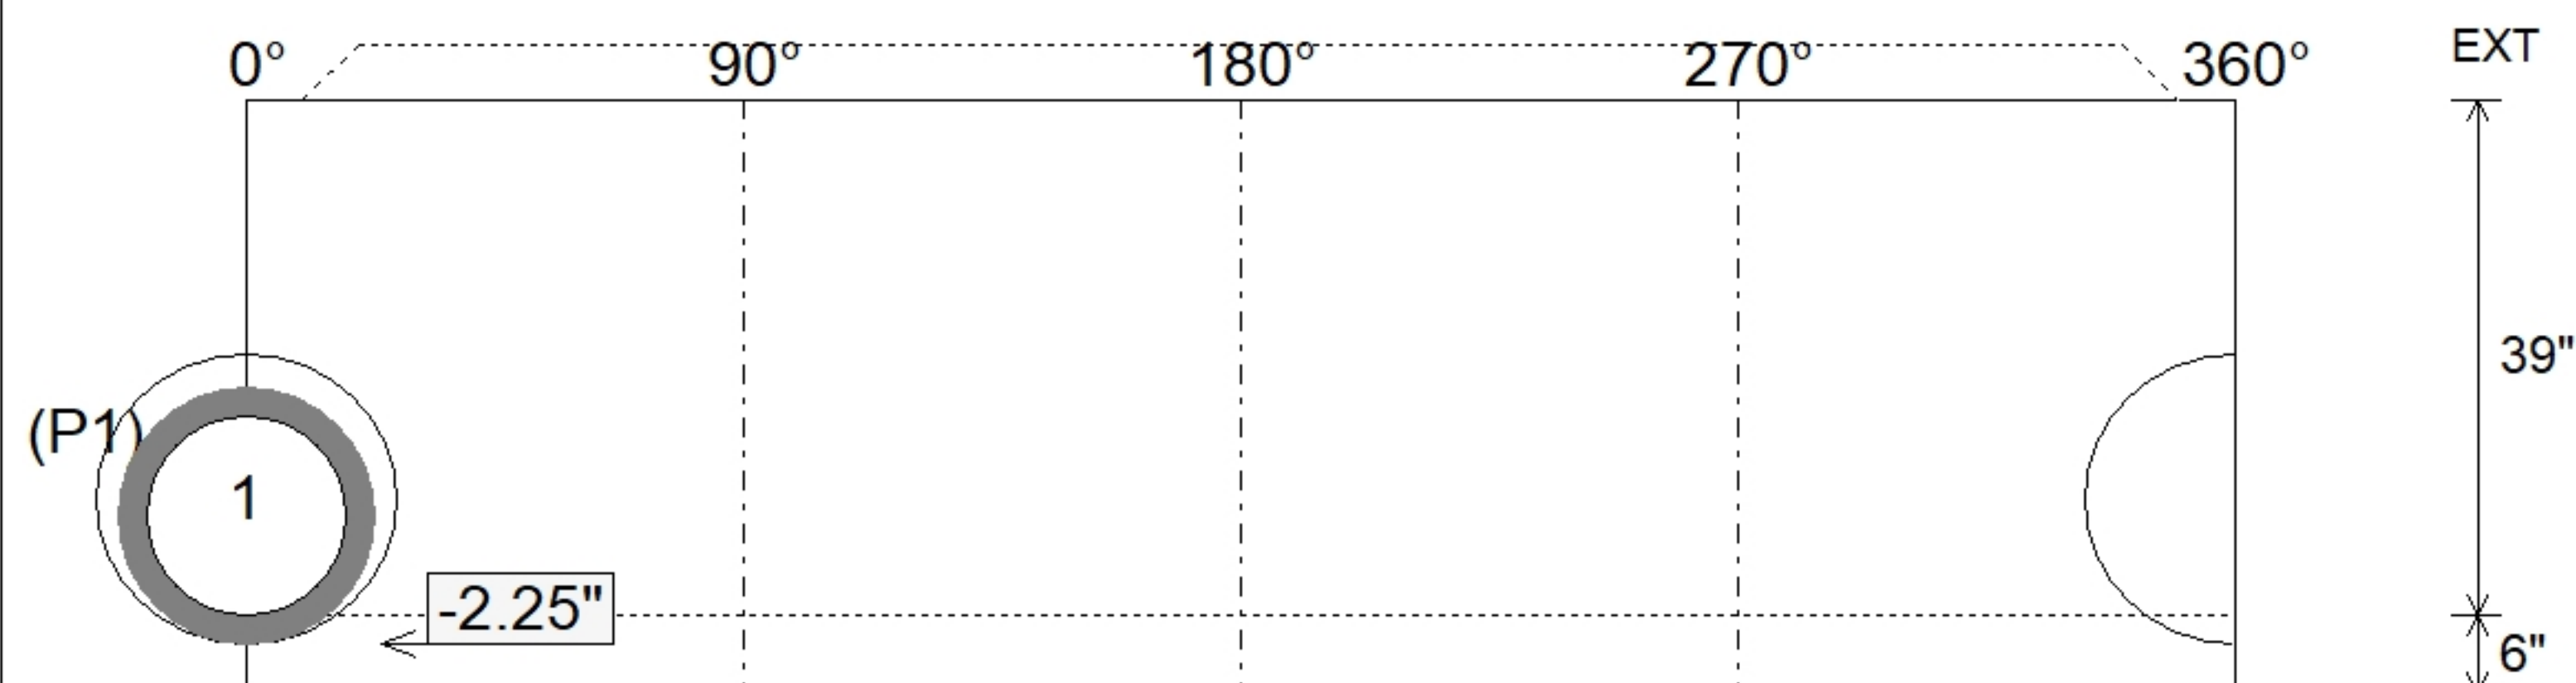

SUBMITTAL
APPROVED BY:
