

Contractor: RD Sitework LLC

TECH: Jared - F

Plant: 100



Size: 36" x 84"

Rim to Invert: 4.68'

Floor Height: 8"


Slack: 0.16"

- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

2) Hole - 22



0 lb

Structure Total: 14002 lb

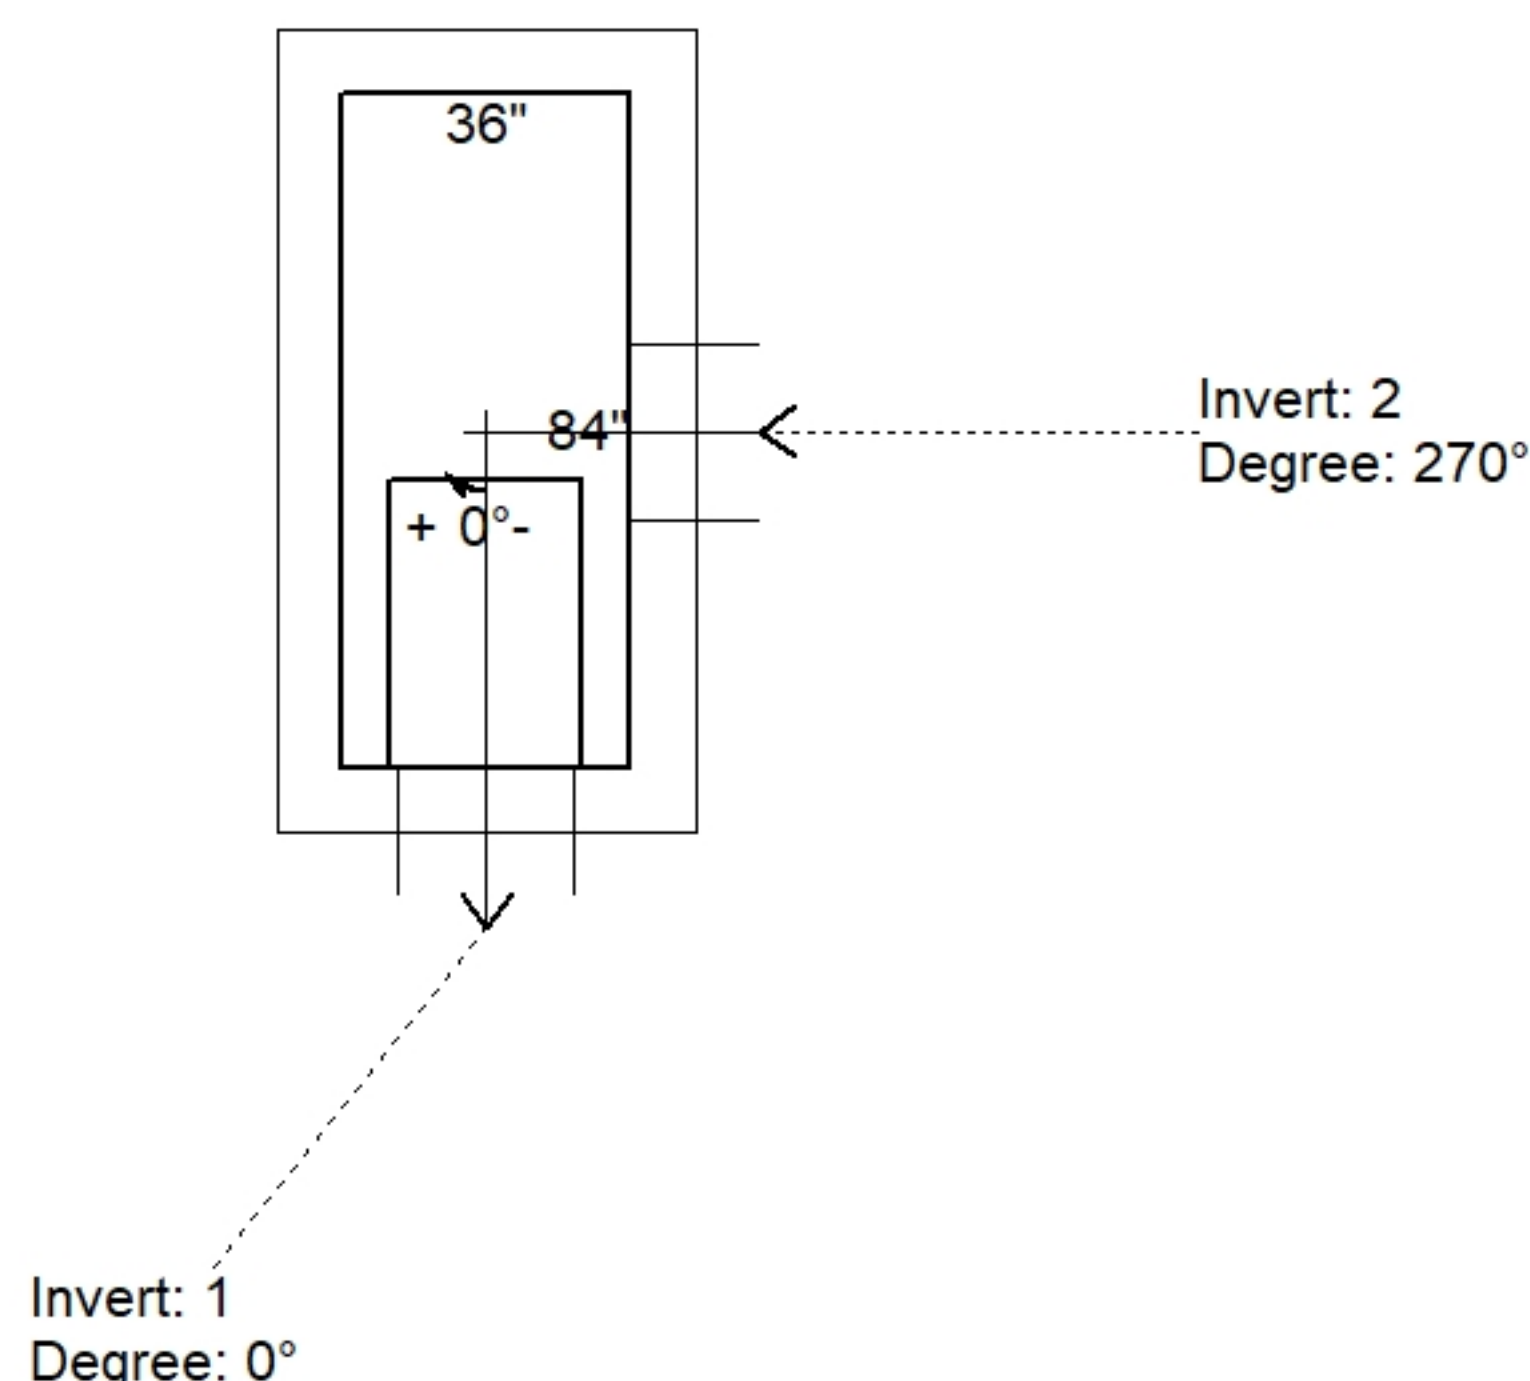

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	717.47'							
Reducer								
Invert 1	712.79'	0°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 2	712.79'	270°	15" RCP B WALL	19.5"	22"	Hole 22	-2.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

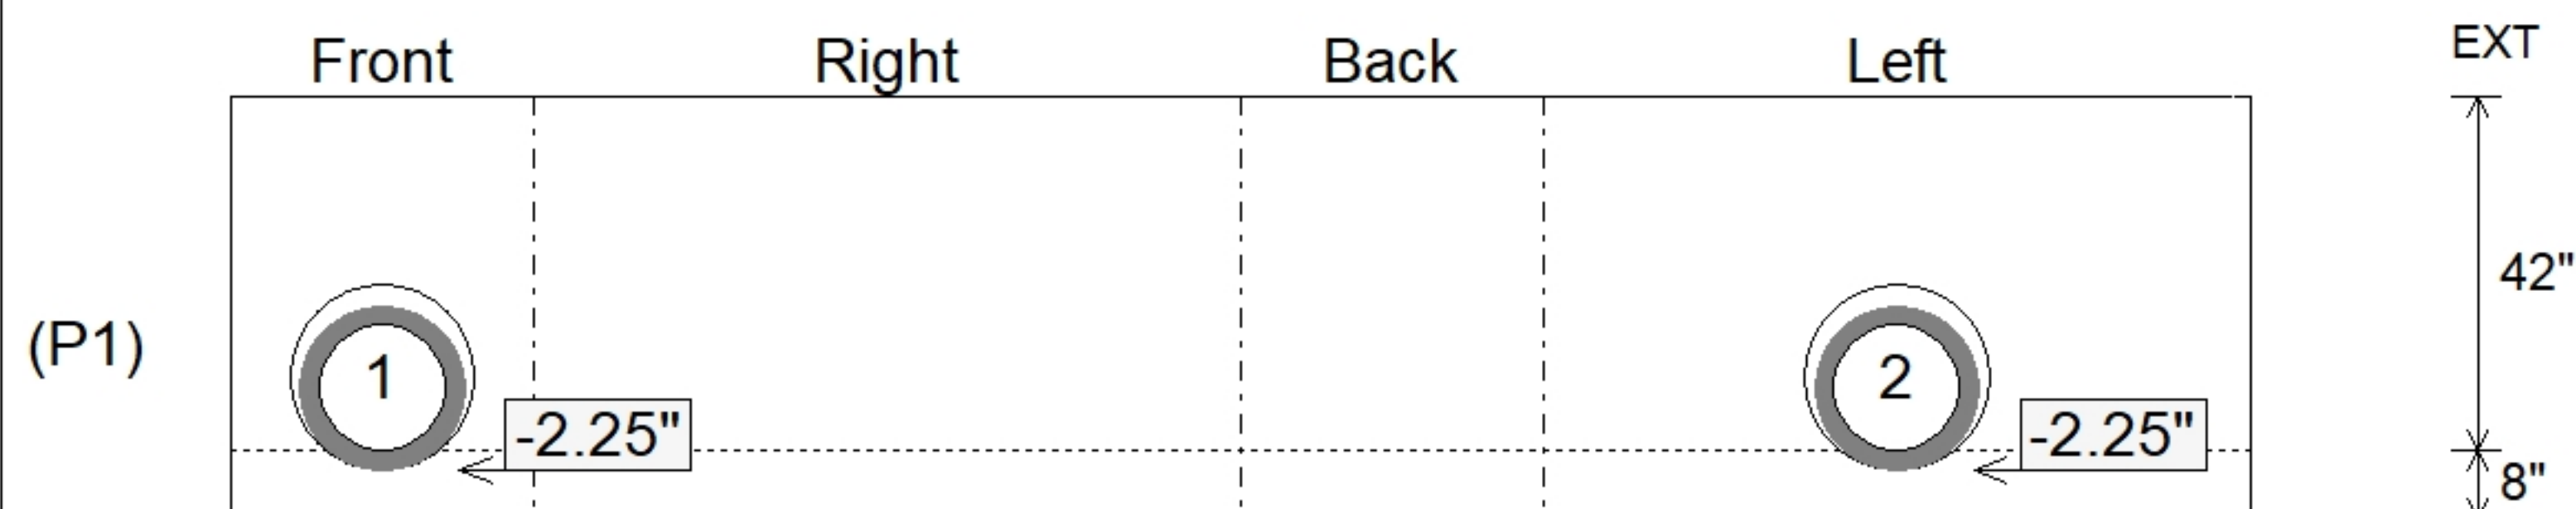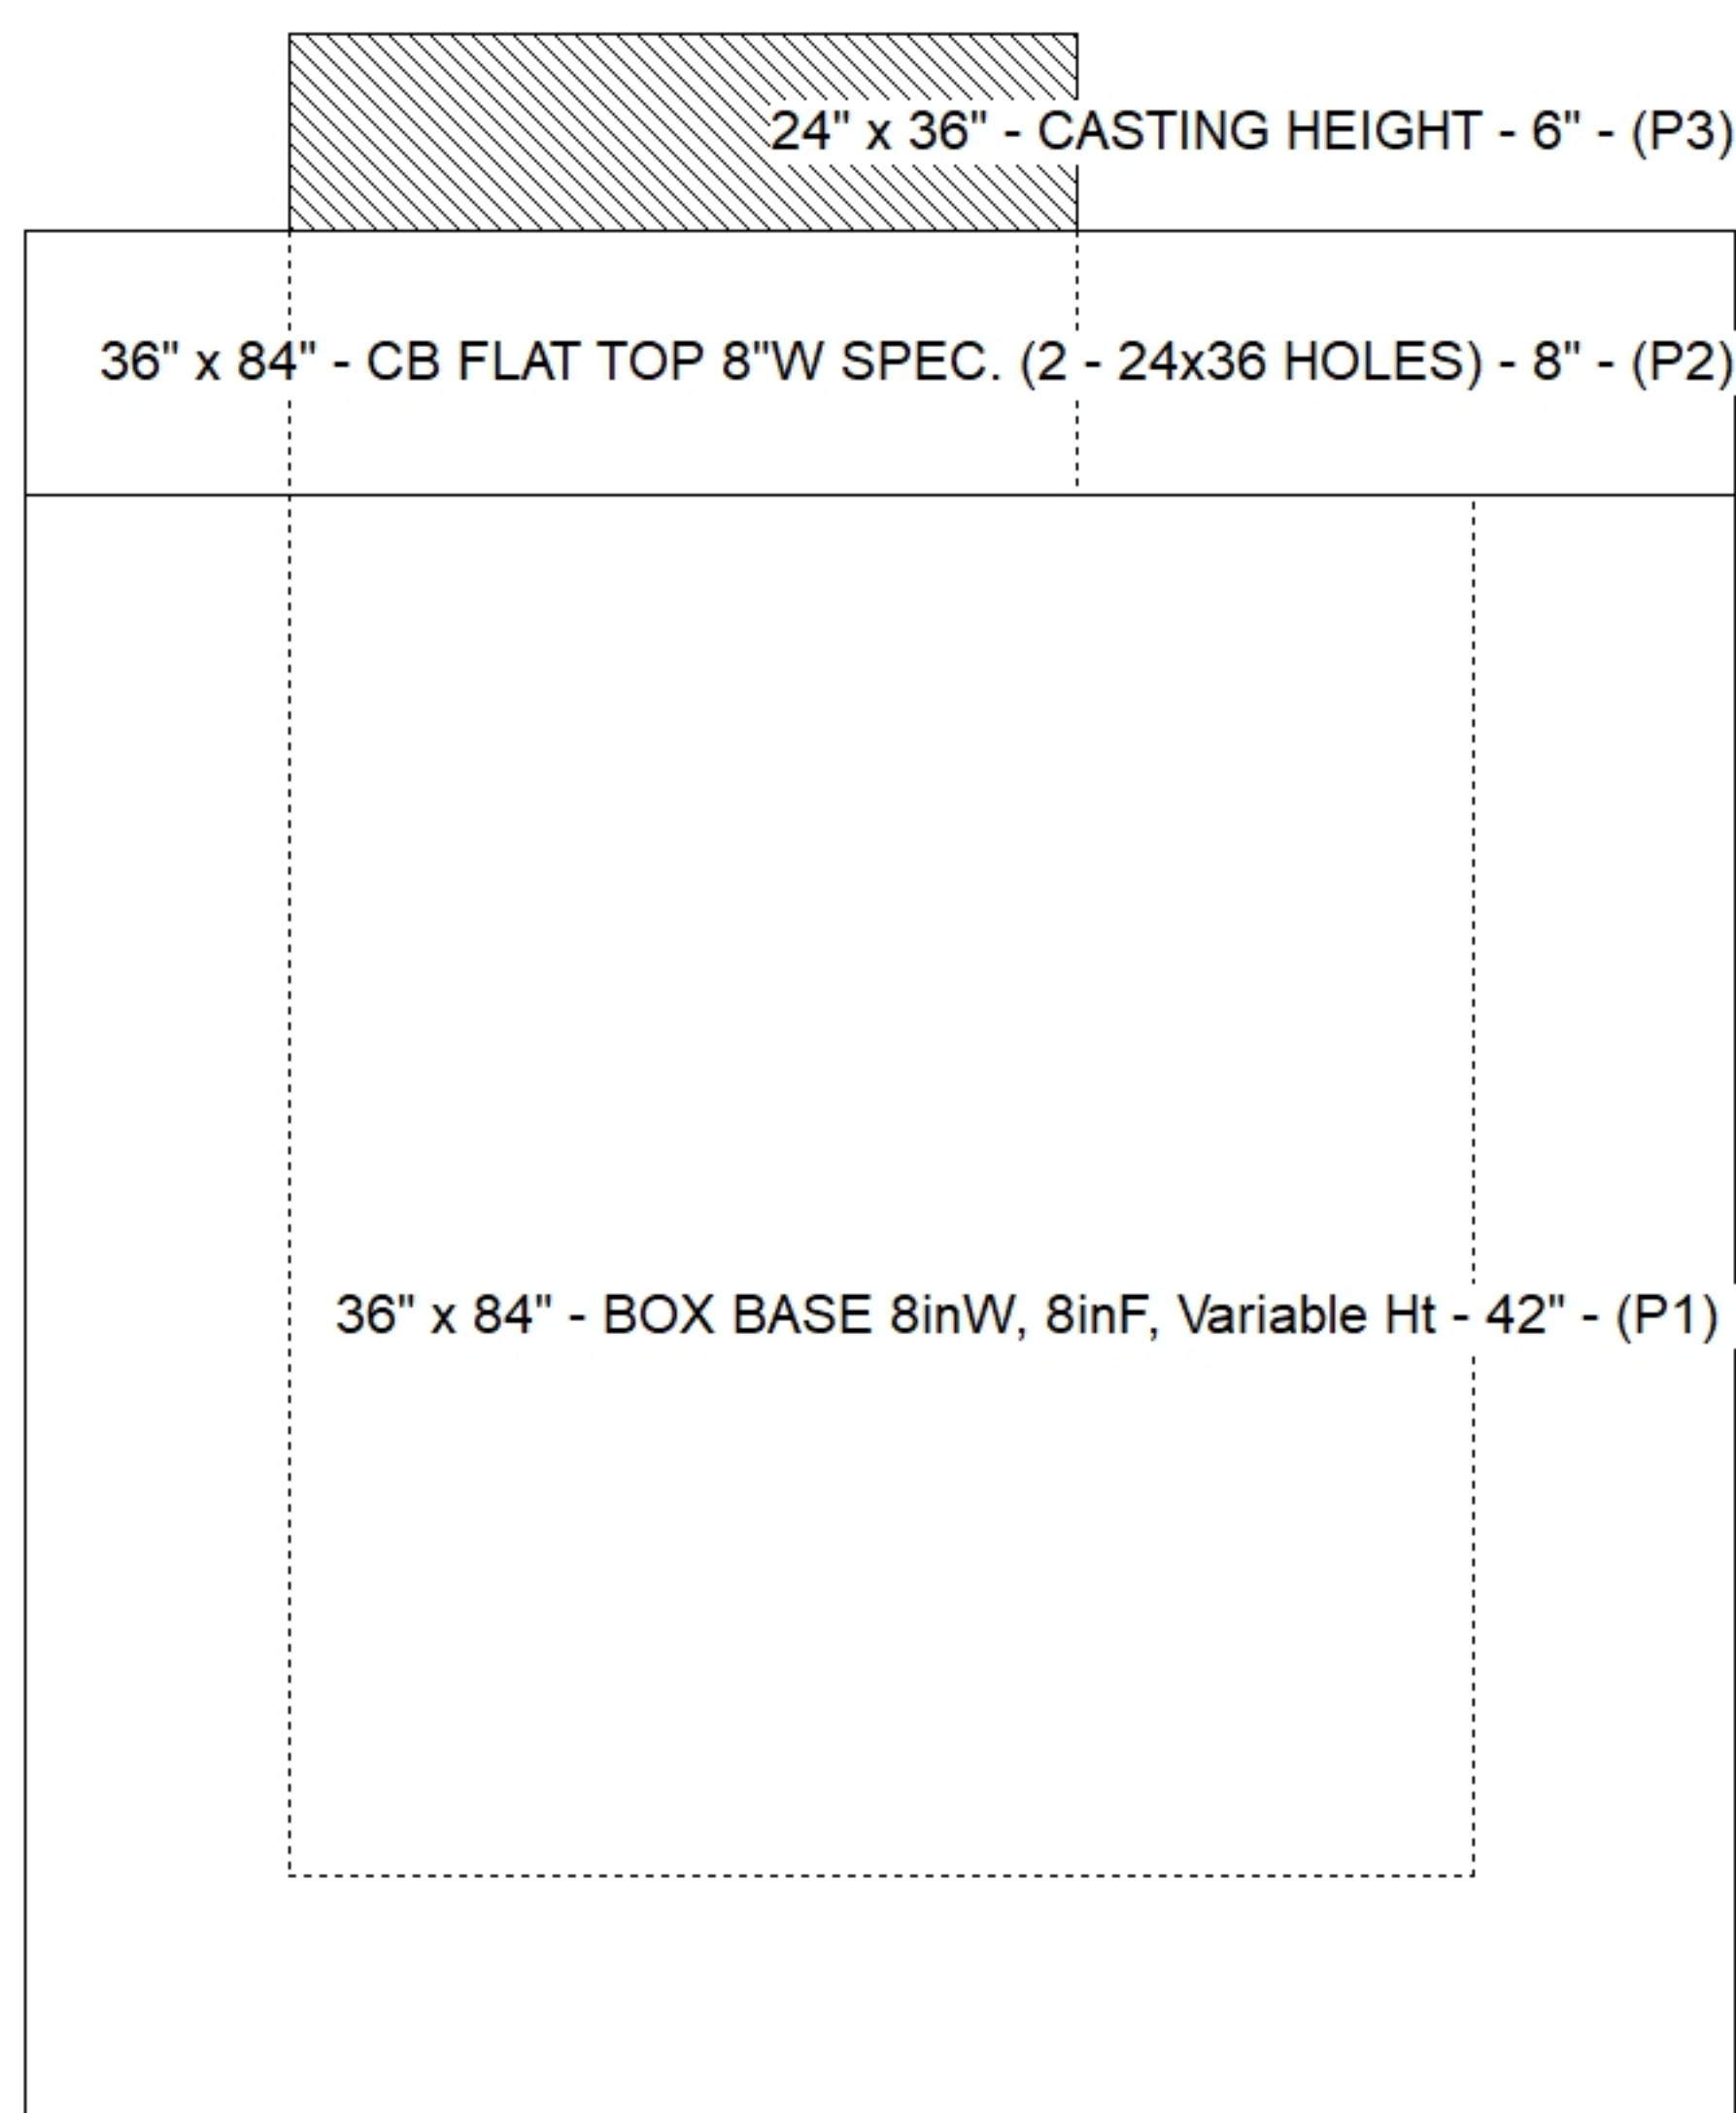

Submittal Drawing
6/8/2026 12:39:11 PM

SUBMITTAL
APPROVED BY:
