

Job Name: 26-1899 - Gateway 65 Industrial Road
Job Location: Franklin, KY
Contractor: RD Sitework LLC

Plant: 100

6/4/2026 4:39:28 PM

Tech: Jared - F
PC: E. Bardley



Structure ID: QL70-4 POND4

P2 BXLD4848FL-24SQ

BX FLAT LID 8inW w/CC 24"x24" HOLE F/F

P3) 24" x 24" - CASTING HEIGHT - 4"
P2) 48" x 48" - BX FLAT LID 8inW w/CC 24"x24" HOLE F/F - 8"
P1) 48" x 48" - BOX BASE 8inW, 8inF F/n - 36"
1) CASTING - HOE-326-BH F/G
1) 48" x 48" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
1) Hole - 0


Structure Total:

0 lb
2363 lb
8163 lb
289 lb
0 lb
0 lb
0 lb
10815 lb


Structure Notes:

1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE-326-BH F/G OR EJ 6626).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

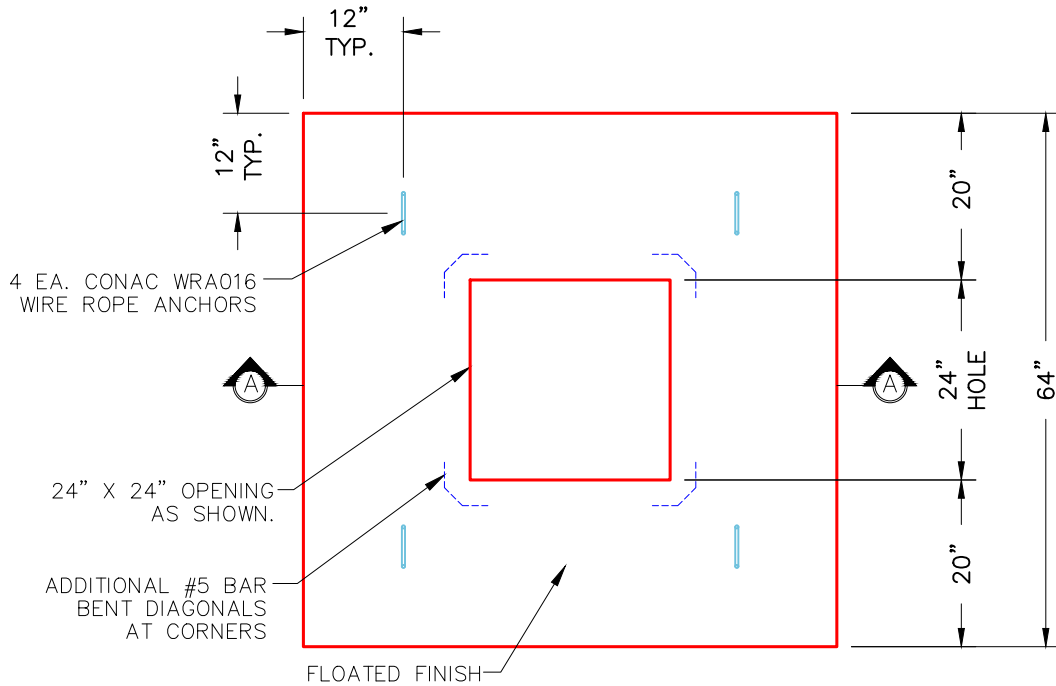

PLAN VIEW

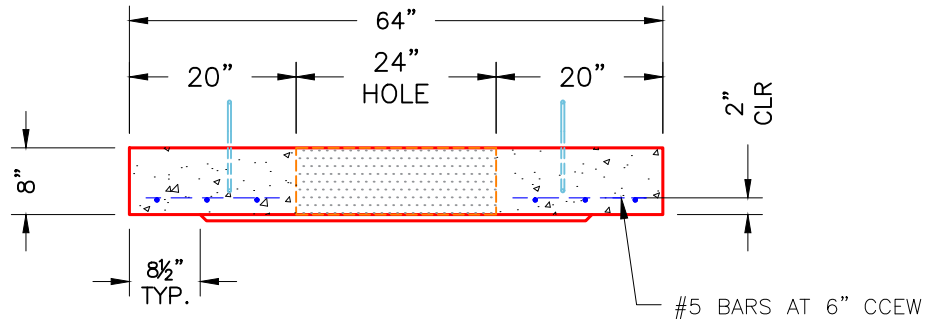

SECTION A-A

NOTES:

1. MANUFACTURED TO ASTM C-913 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 2363 lb
Volume (Net): 0.6cu.yd
