



Job Name: 26-1952 - HCWD 2 Fire Station Sanitary Sewer Extension Job Location: Glendale, KY Contractor: Phillips Bros. Construction, LLC				Plant: 100 5/20/2026 3:39:29 PM		Tech: J. Horsley PC: T. Ryan				
Structure ID: B SS-MHD										
P2 MH048RS60SCDARED			MH RISER w/DROP/ConBlock-CDA Red T/G							
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P3) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/DROP/ConBlock-CDA Red T/G - 60" P1) 48" - MH BASE w/DROP/ConBlock-CDA Red T/n - 48" 1) JOINT WRAP - 0.065"x12"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 1) A-Lok - 0285 1) Drop Elbow - 8" PVC 1) Drop Tee - 8" PVC 12) MH Step ML-10-TDS-NCR - 10"					0 lb 202 lb 2251 lb 4192 lb 4604 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 0 lb 1 lb 0 lb 0 lb 0 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY OTHERS (HOE MC-315 F/C SANITARY) 4. EXTERIOR DROP ASSEMBLY AT 189°. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 737.6'		Rim to Invert: 12.6'		Slack: 0.2"		Sump: 3"		Structure Total: 12948 lb Step Position: 94.5"		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

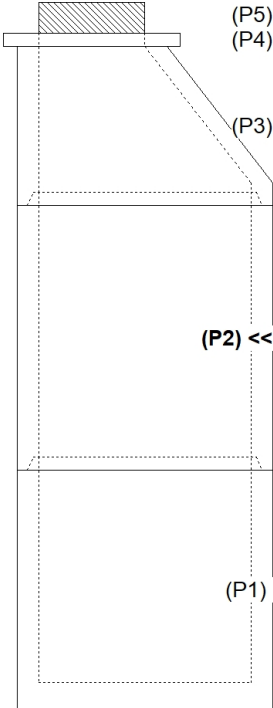


(P5)
(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 94.5°
Horz: 39.625"
+ 0°

INSIDE WALL DIMENSIONS

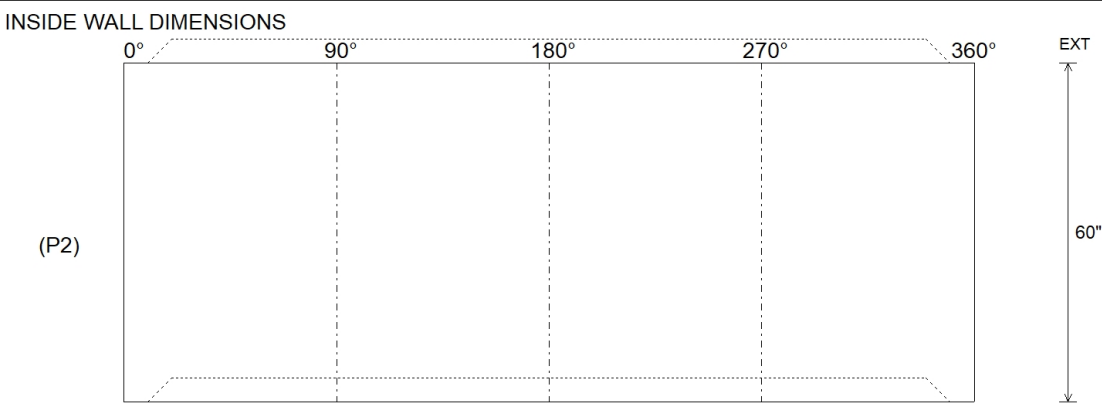

0° 90° 180° 270° 360°
EXT
60"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 5" Floor Height: 0"	Height (Int): 60" Height (Ext): 60"	Weight (Net): 4192 lb Volume (Net): 1.07cu.yd
----------------------------------	------------------------------------	--	--	--
