

Job Name: 26-1987P6 - Project Nova
Job Location: Sullivan, IN 47882
Contractor: McCreary Concrete Products, Inc.

Plant: Beaver Dam

Tech: J. Coppage

9/29/2026 12:38:04 PM

PC: M. Sullivan



Structure ID: 1306

P2 MH108RS72

MH RISER

- P5) 24" x 24" - CASTING HEIGHT - 0"
P4) 108" - MH FLAT TOP w/24in X 24in ECC Hole - 17"
P3) 108" - MH RISER - 48"
P2) 108" - MH RISER - 72"
P1) 108" - MH BASE - 96"
3) 108" - Conseal CS-102 1.00"
1) 24" x 24" - Conseal CS-102 1.00"
2) Hole - 76
1) Hole - 44
4) Hole - 6
18) MH Step ML-10-TDS-NCR - 10"


- 0 lb
13186 lb
14836 lb
22397 lb
33213 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
- Structure Notes: .
1. (CASTING PROVIDED BY OTHERS)
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .36)
- FLOOR (As .47) #5 BARS AT 8" C.C.E.W.

Structure Total: 83632 lb


Rim: 510.04' Rim to Invert: 18.94' Slack: 0.28" Sump: 6" Step Position: 120°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

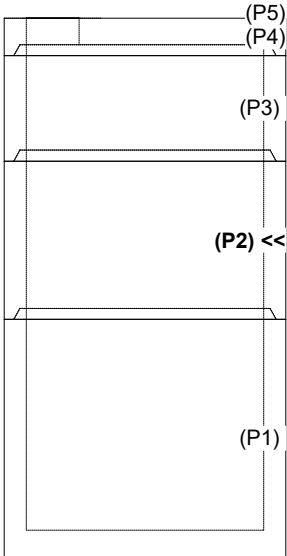

Step: 120°
Horz: 113.097"



INSIDE WALL DIMENSIONS



Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 10"
Floor Height: 0"

Height (Int): 72"
Height (Ext): 72"

Weight (Net): 22397 lb
Volume (Net): 5.72cu.yd
