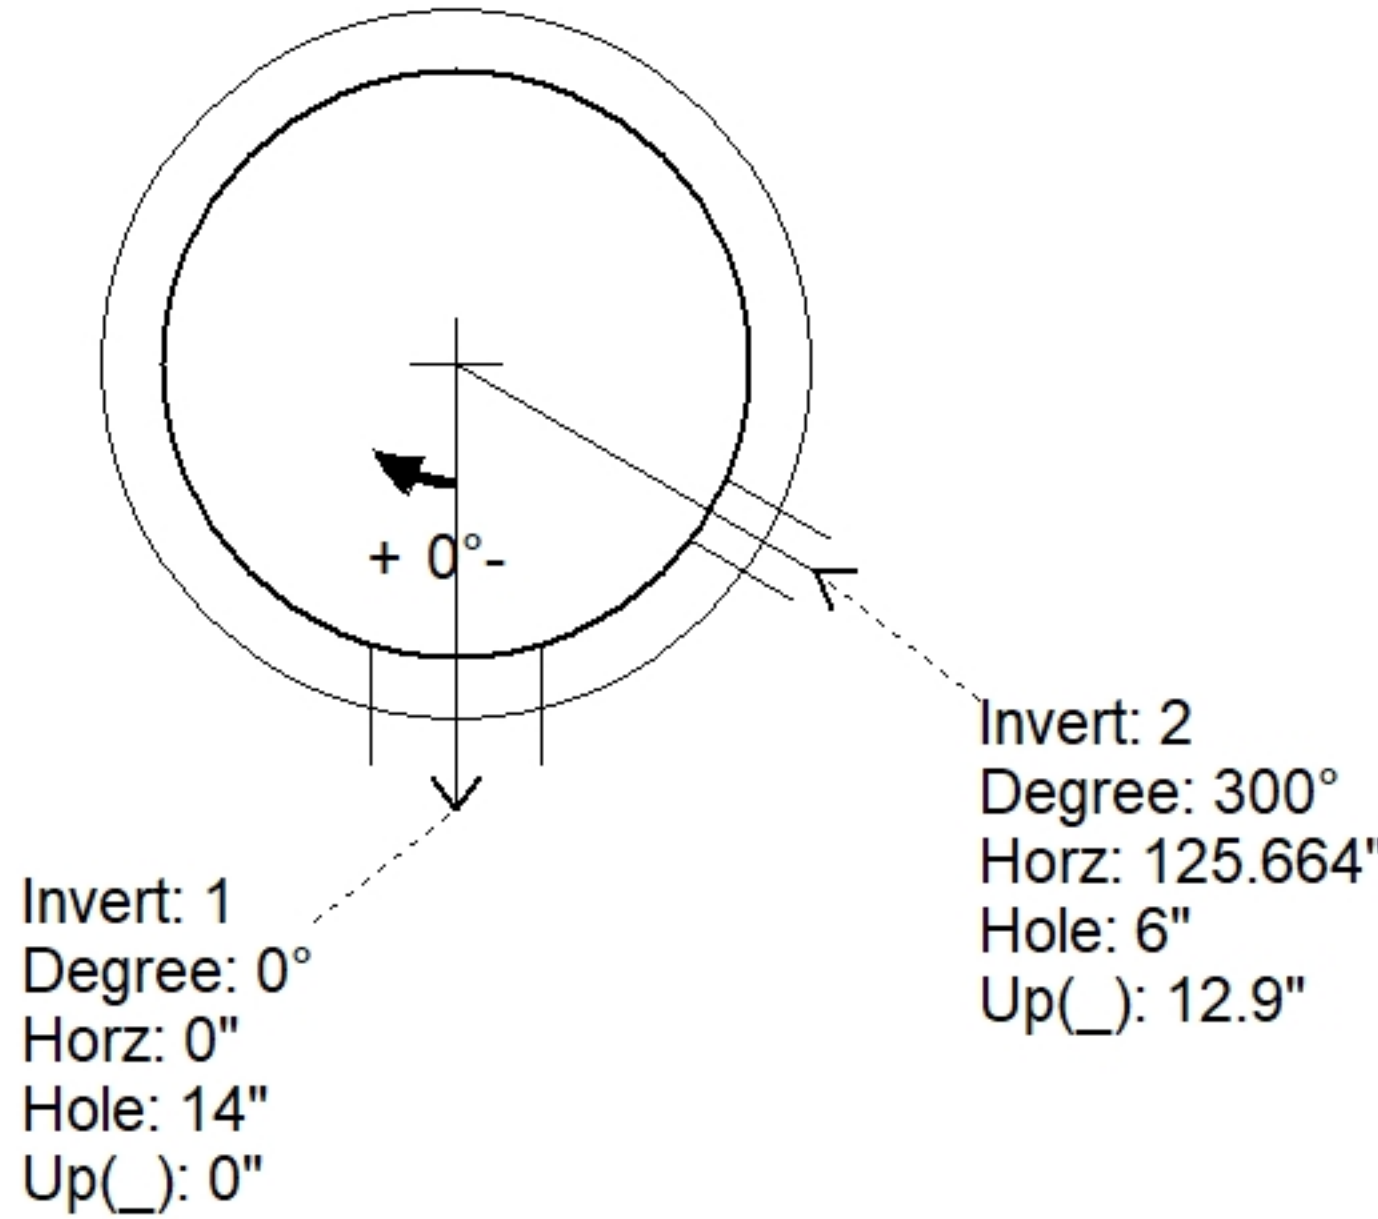
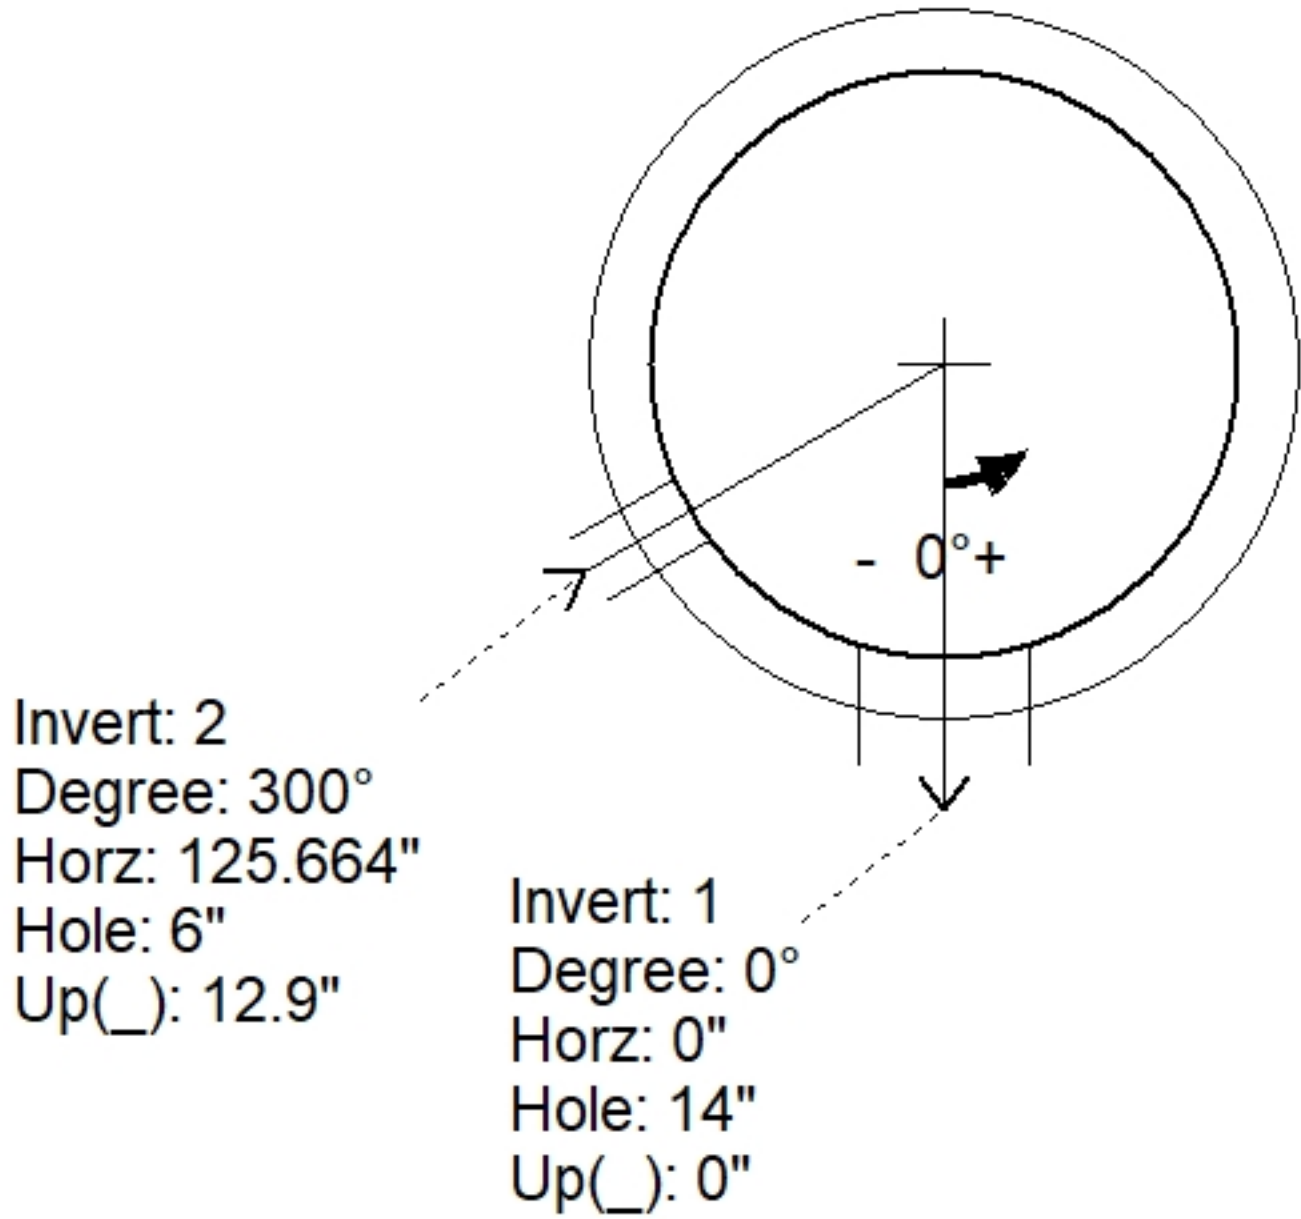
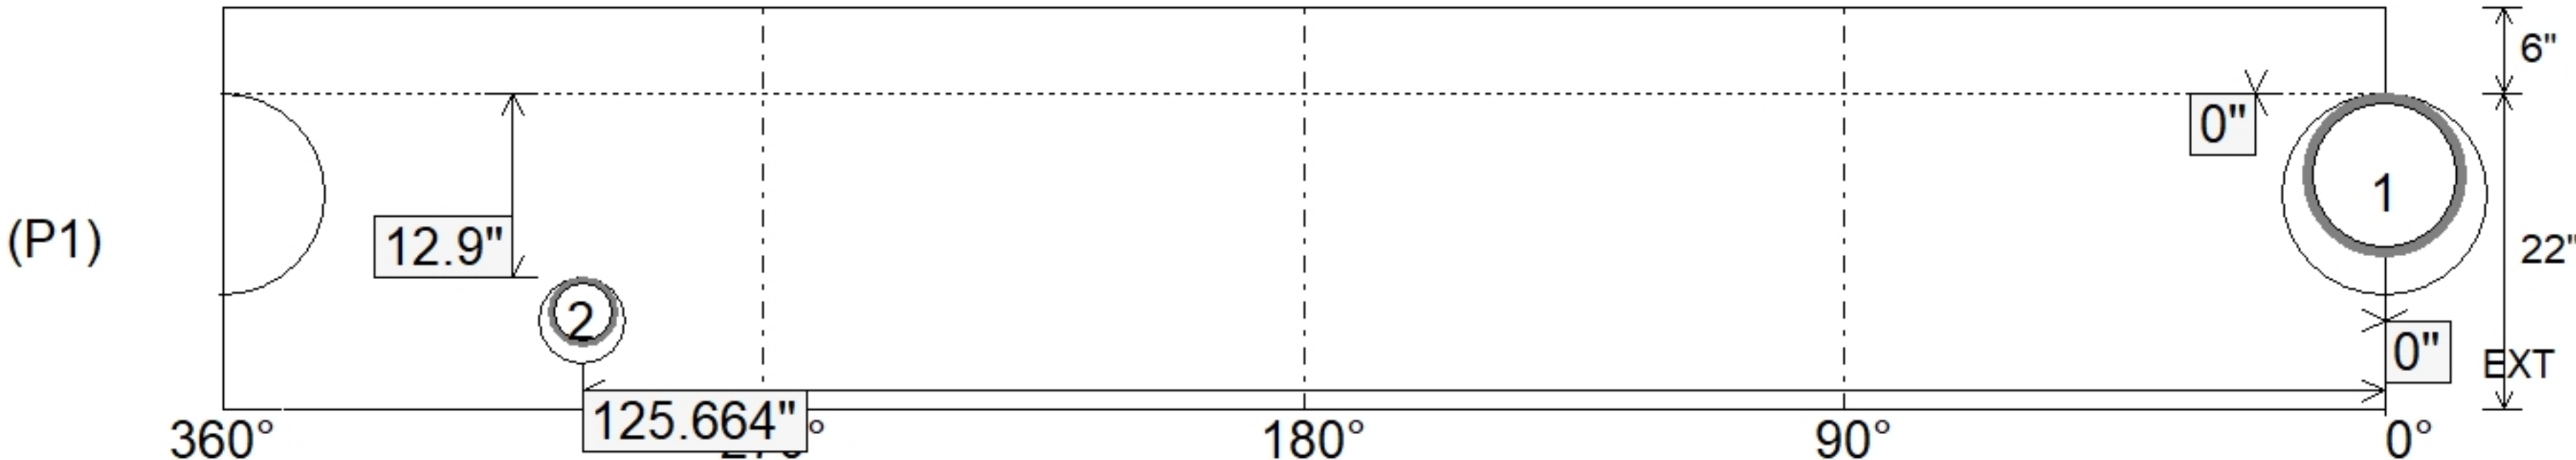


Job Name: 26-2018B Hancock Co Middle School Utility				Plant: Beaver Dam		Tech: S. Felletter				
Job Location: South Lewisport, KY				10/12/2026 8:19:42 AM		PC: A. Chambers				
Contractor: Winwater Hartford KY Co.										
Structure ID: DI-2B ST-MH										
P1		MH048BAVF		MH BASE Custom Ht F/n						
P3) 24" - CASTING HEIGHT - 7" P2) 48" - MH FLAT TOP w/ 24" Center Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 22" 1) CASTING - HOE MCB-315-B Fr./Bar Grate 1) 48" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 1) Hole - 14 1) Hole - 6						0 lb 1700 lb 2790 lb 255 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4745 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MCB-315-B F/ BAR GRATE). . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.		
Rim: 413.75'		Rim to Invert: 3'		Slack: 0.7"		Sump: 0.7"		Step Position: 0°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	410.75'	0°	0"	10" HDPE	11.4"	Hole 14	14"	14.207"	0"	0"
Invert 2	411.8'	300°	151.844"	4" HDPE	4.8"	Hole 6	6"	6.016"	12.9"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions)   INSIDE WALL DIMENSIONS 										
Coating (Int):			Seam Up: Flat		Wall Thickness: 5"		Height (Int): 22"		Weight (Net): 2790 lb	
Coating (Ext):			Seam Dn: n/a		Floor Height: 6"		Height (Ext): 28"		Volume (Net): 0.71cu.yd	
