

Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam




Slack: 0.09"

- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

1) Hole - 12



0 lb

Structure Total: 4802 lb

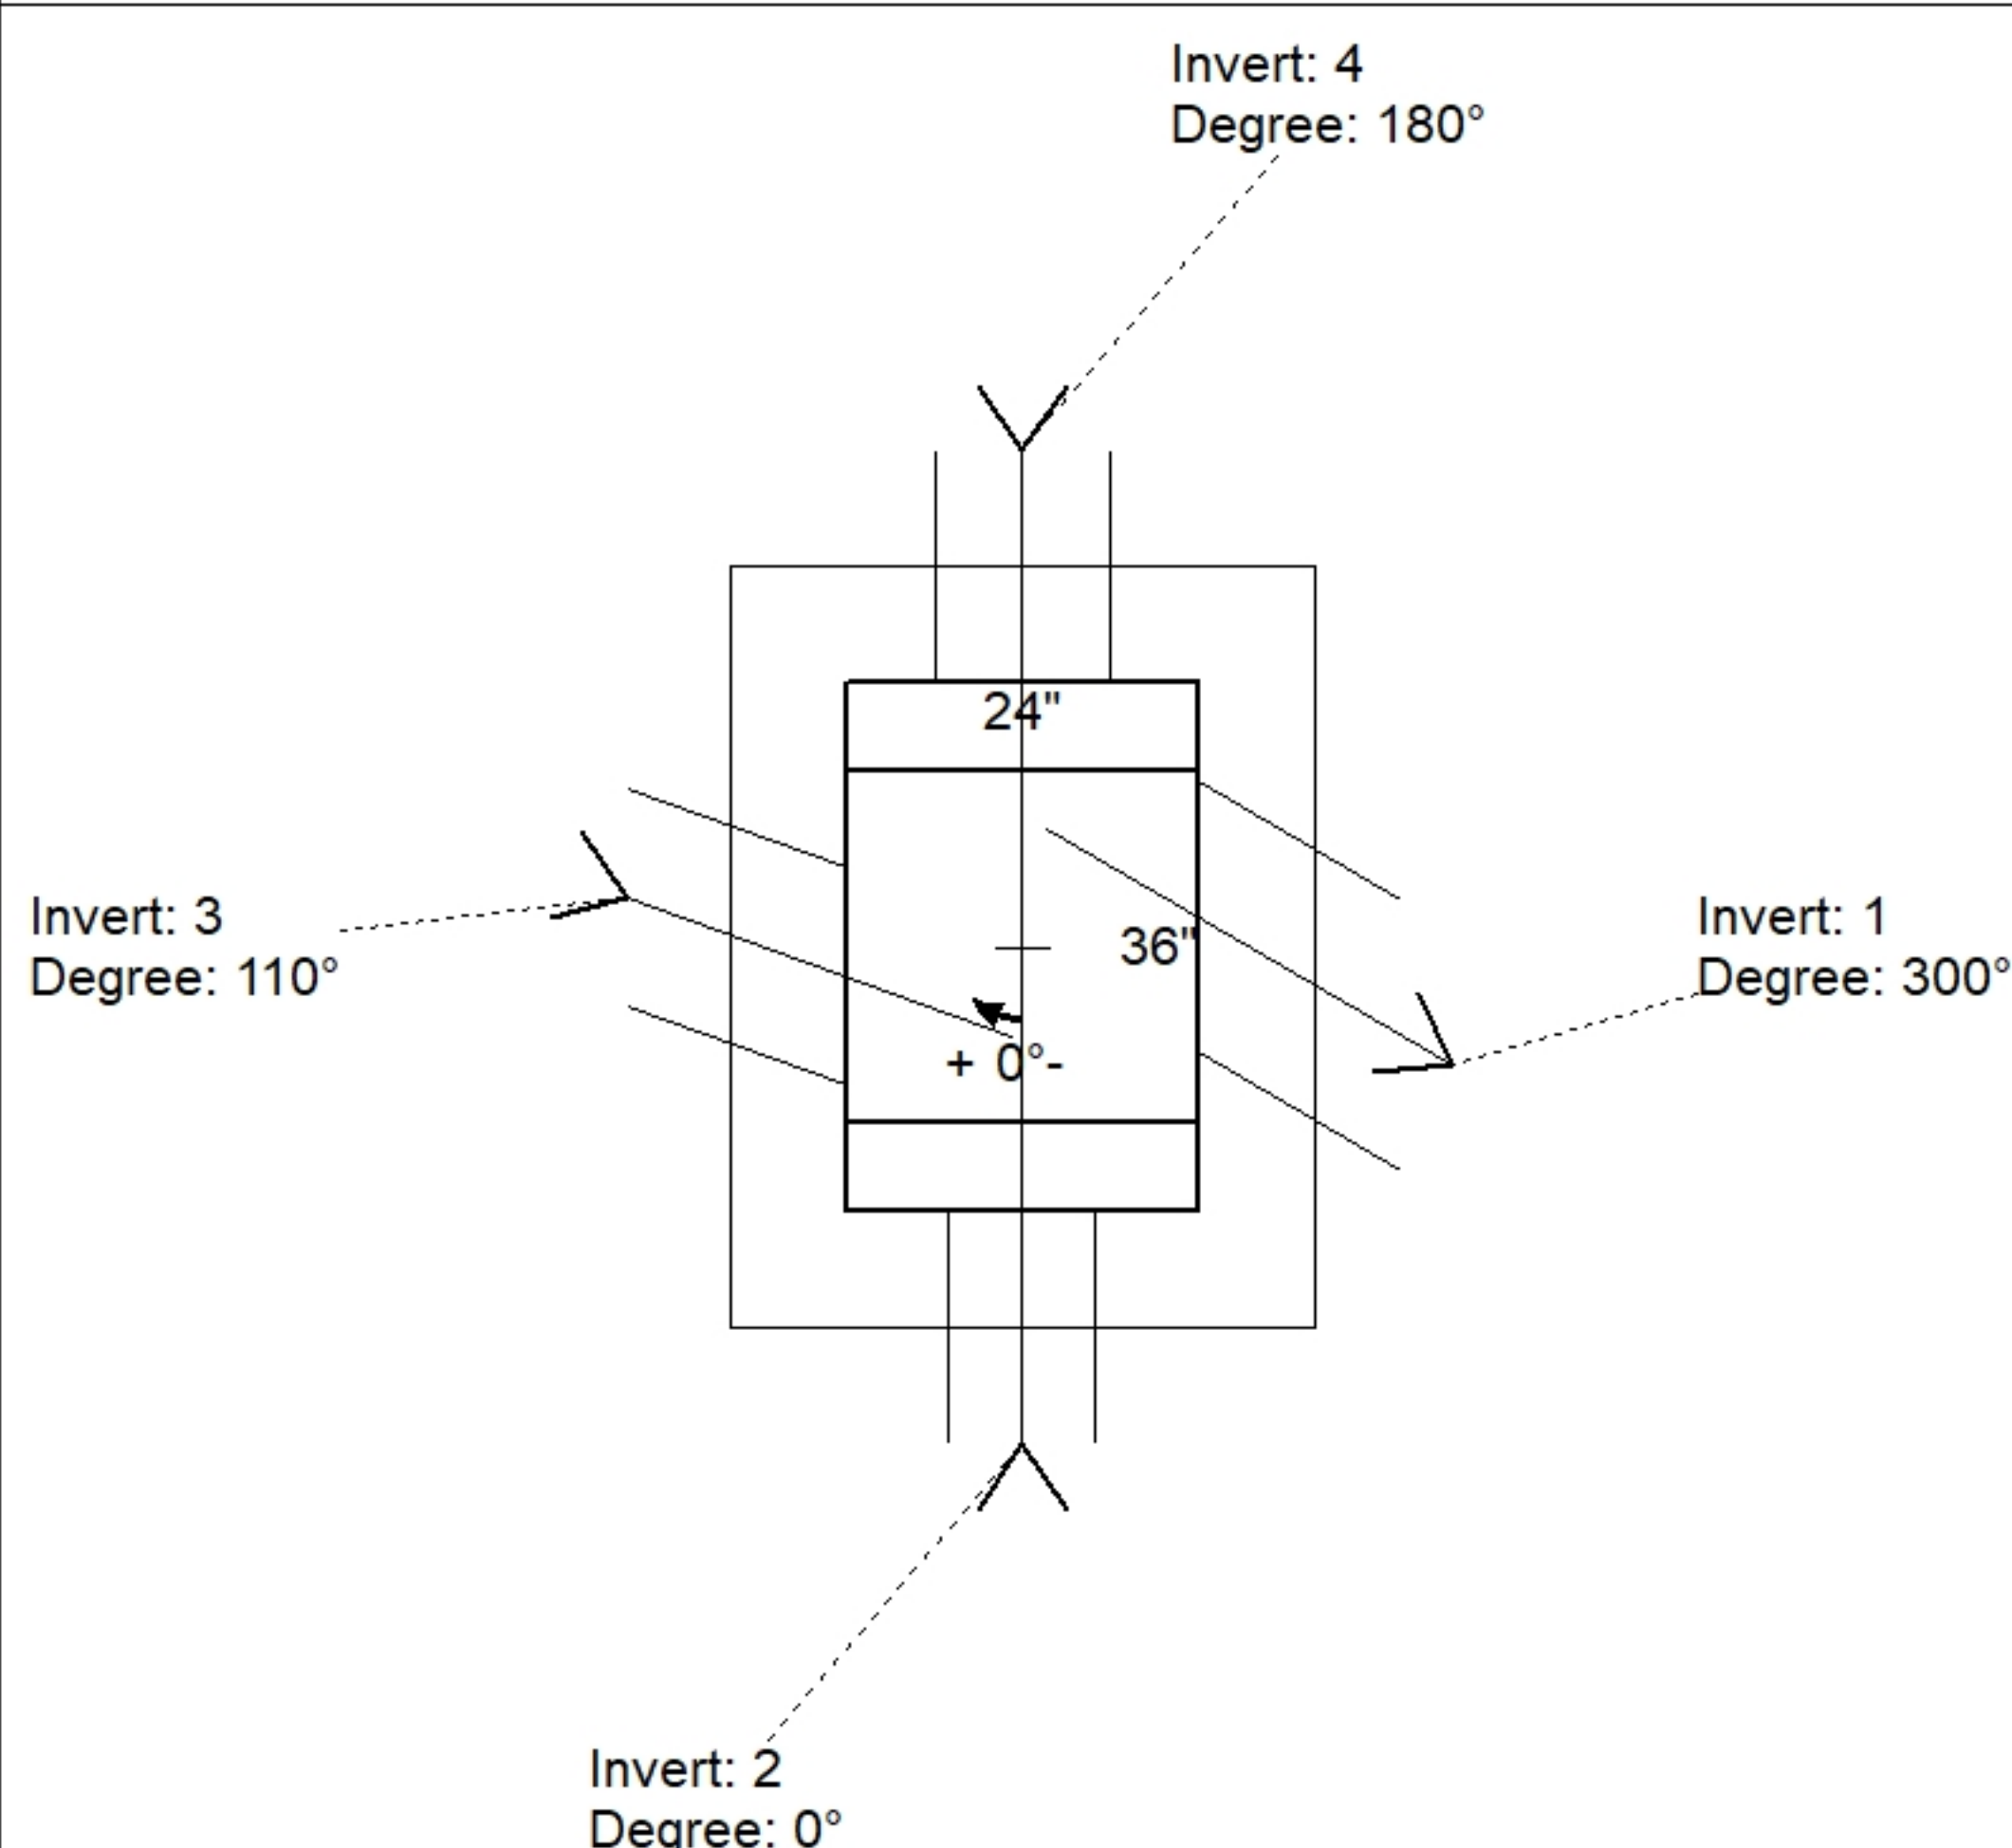

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	412.14'							
Reducer								
Invert 1	409.07'	300°	12" HDPE	14.5"	16"	Hole 16	0"	P1
Invert 2	409.17'	0°	6" PVC SDR35	6.25"	10"	Hole 10	2.325"	P1
Invert 3	409.17'	110°	10" HDPE	11.4"	14"	Hole 14	1.75"	P1
Invert 4	409.17'	180°	8" PVC SDR35	8.5"	12"	Hole 12	2.2"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

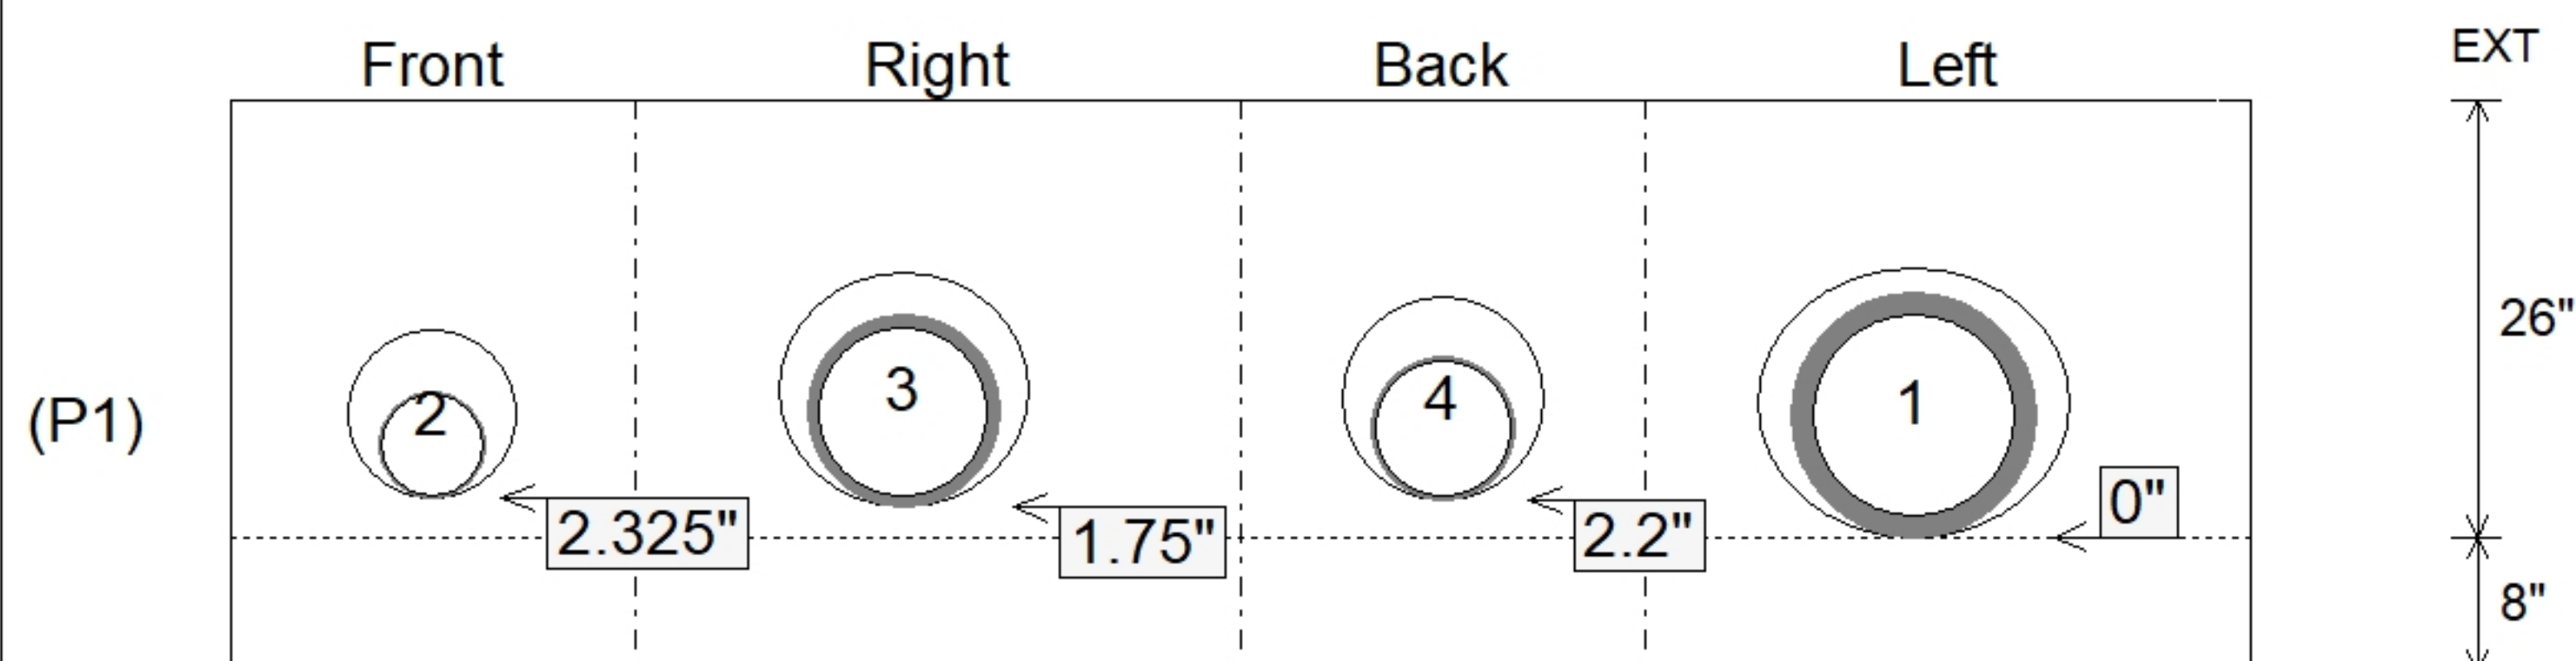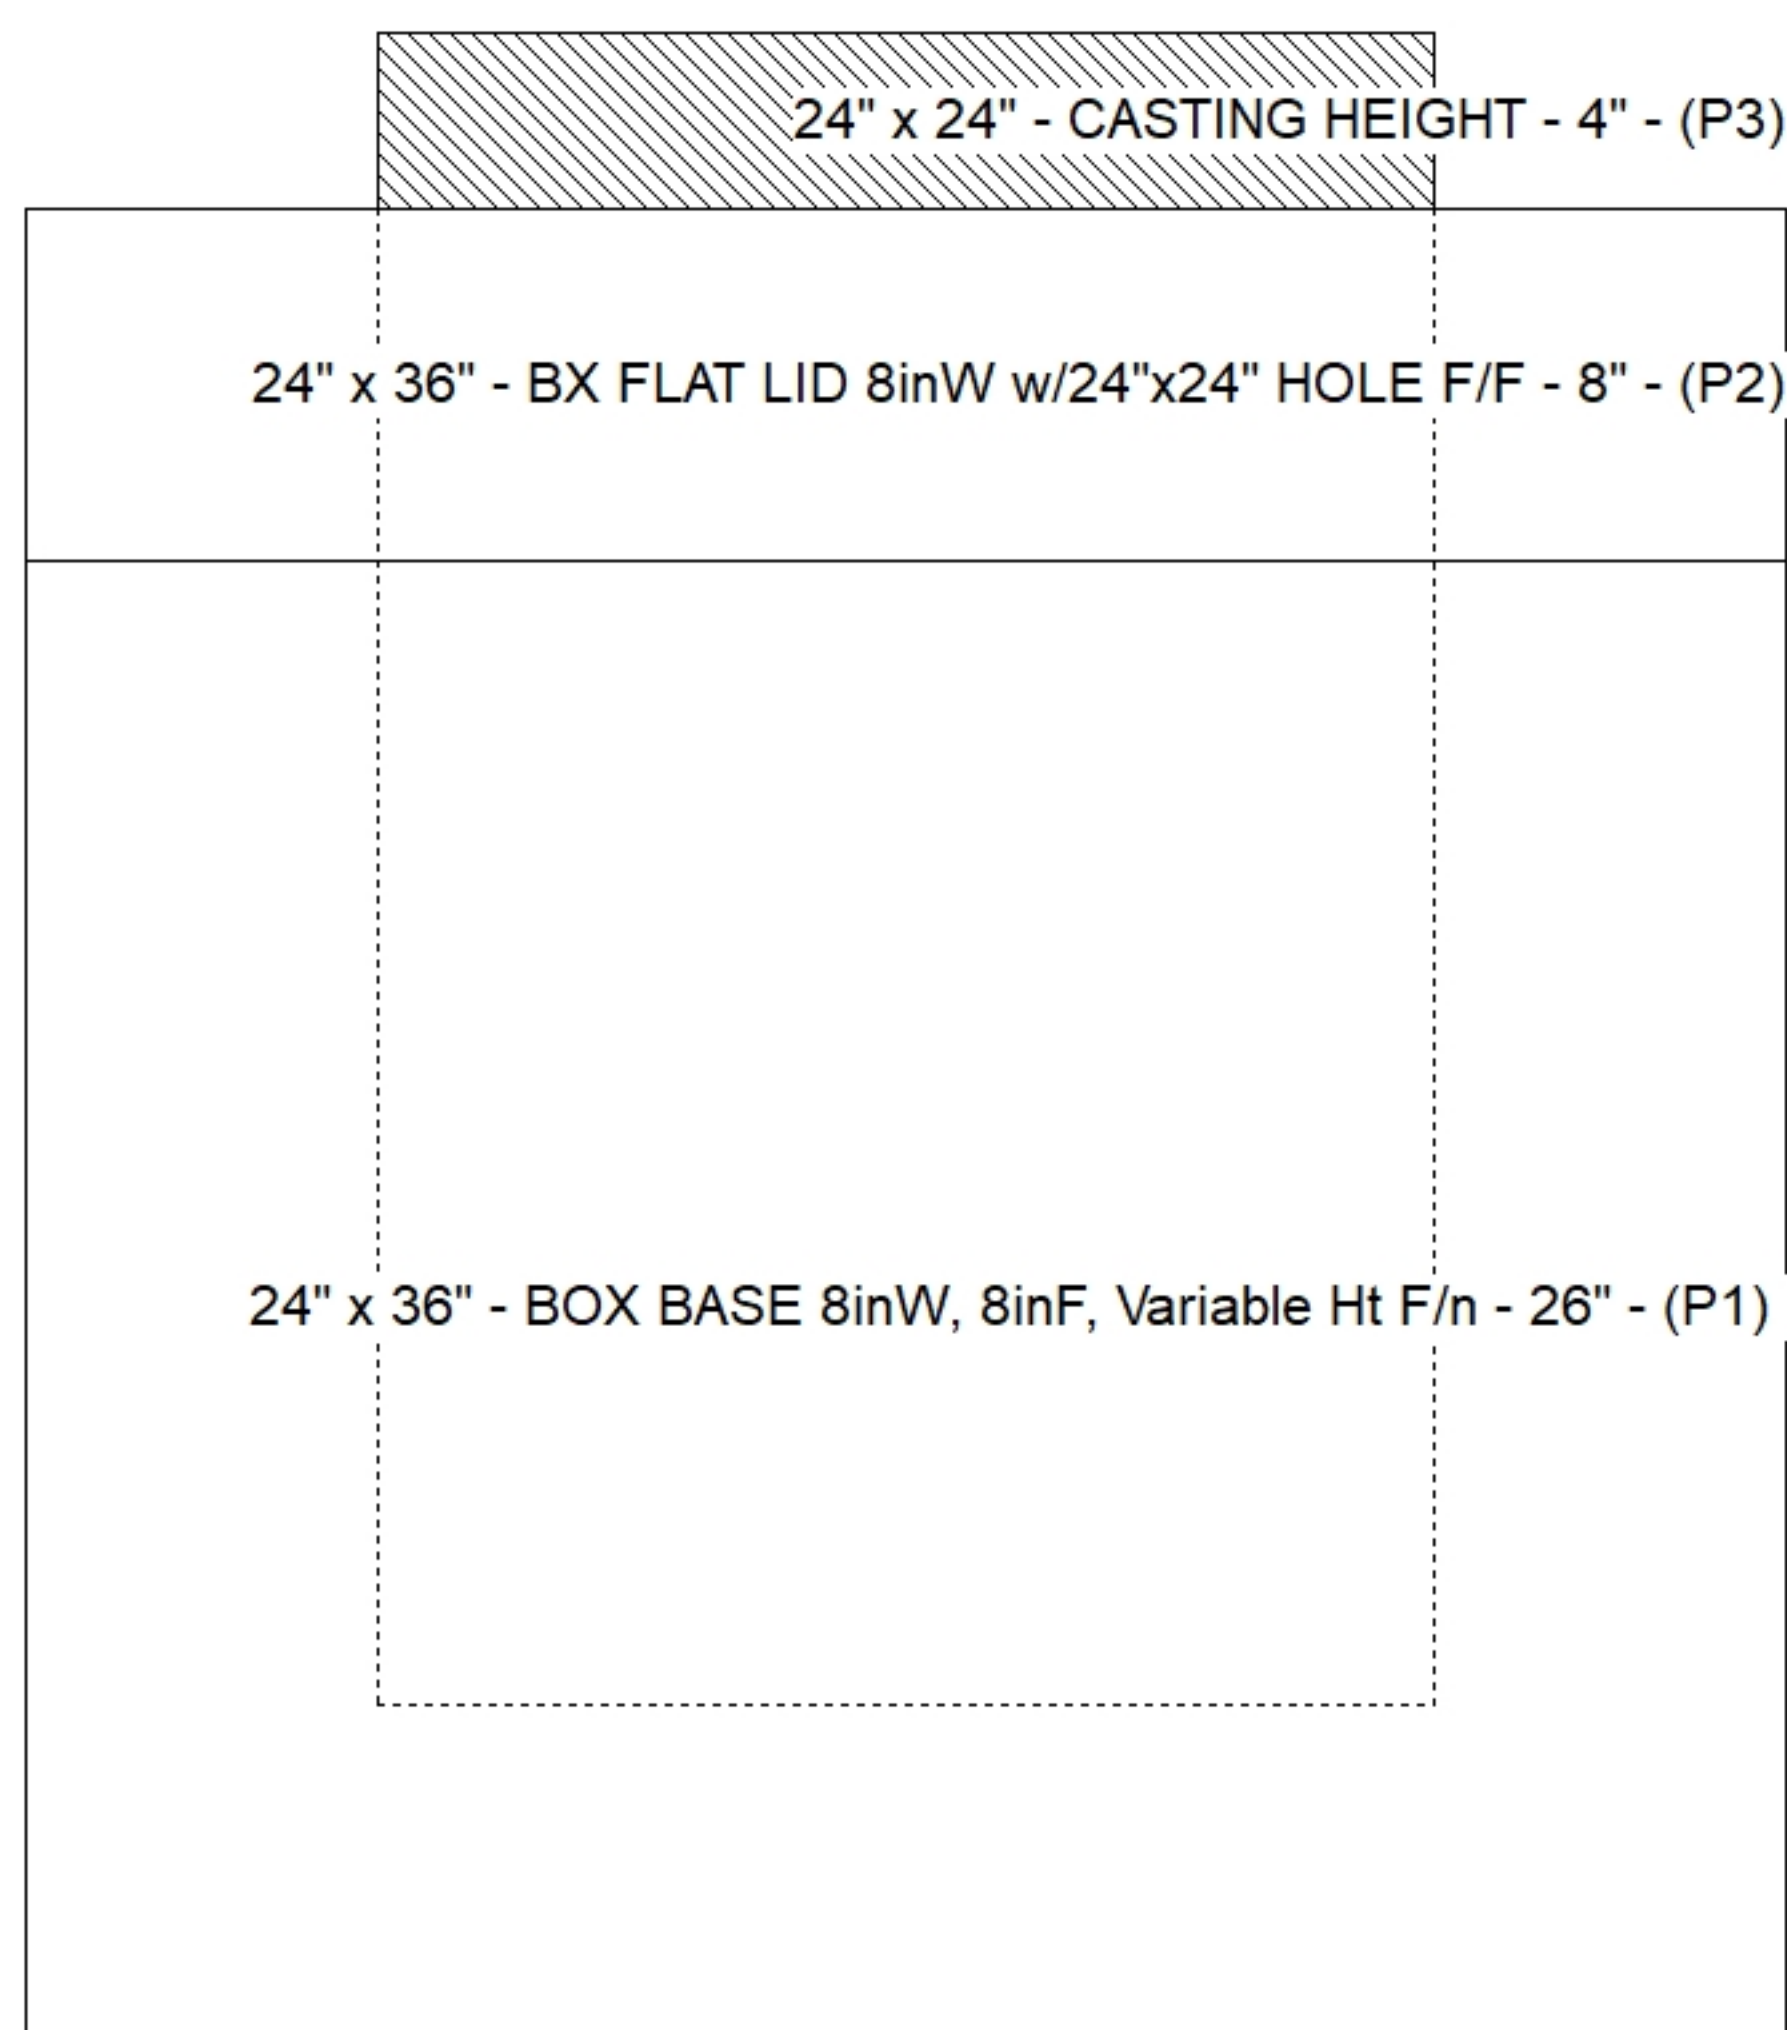

SUBMITTAL
APPROVED BY:
