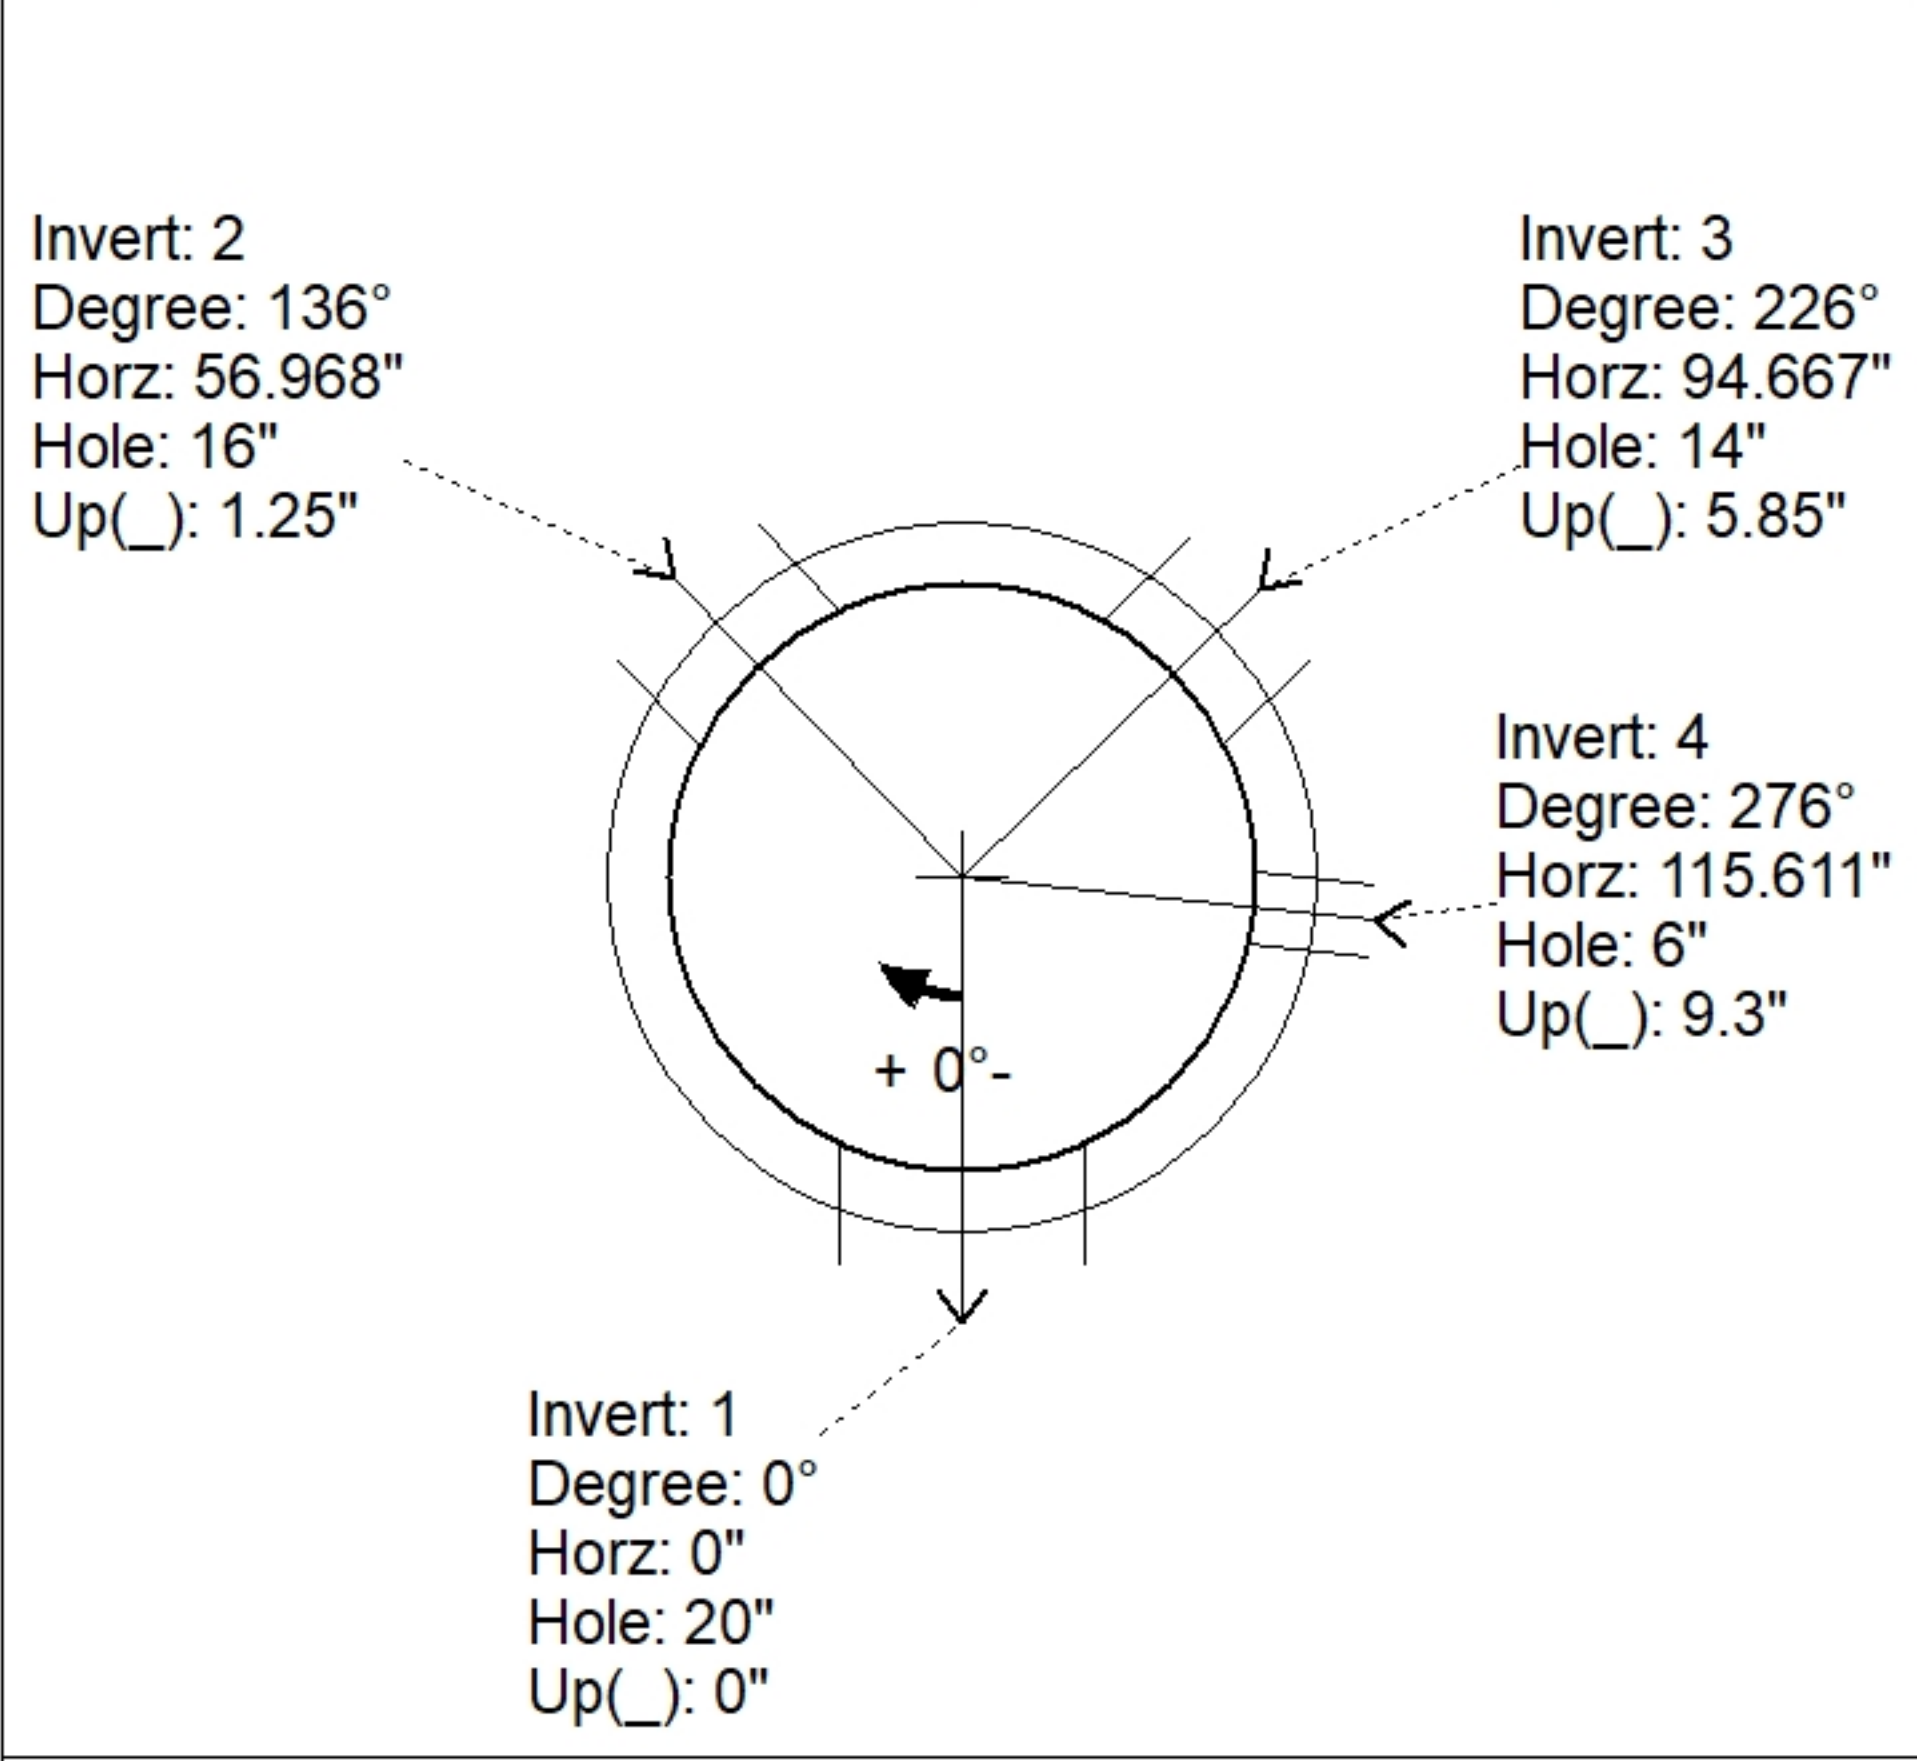
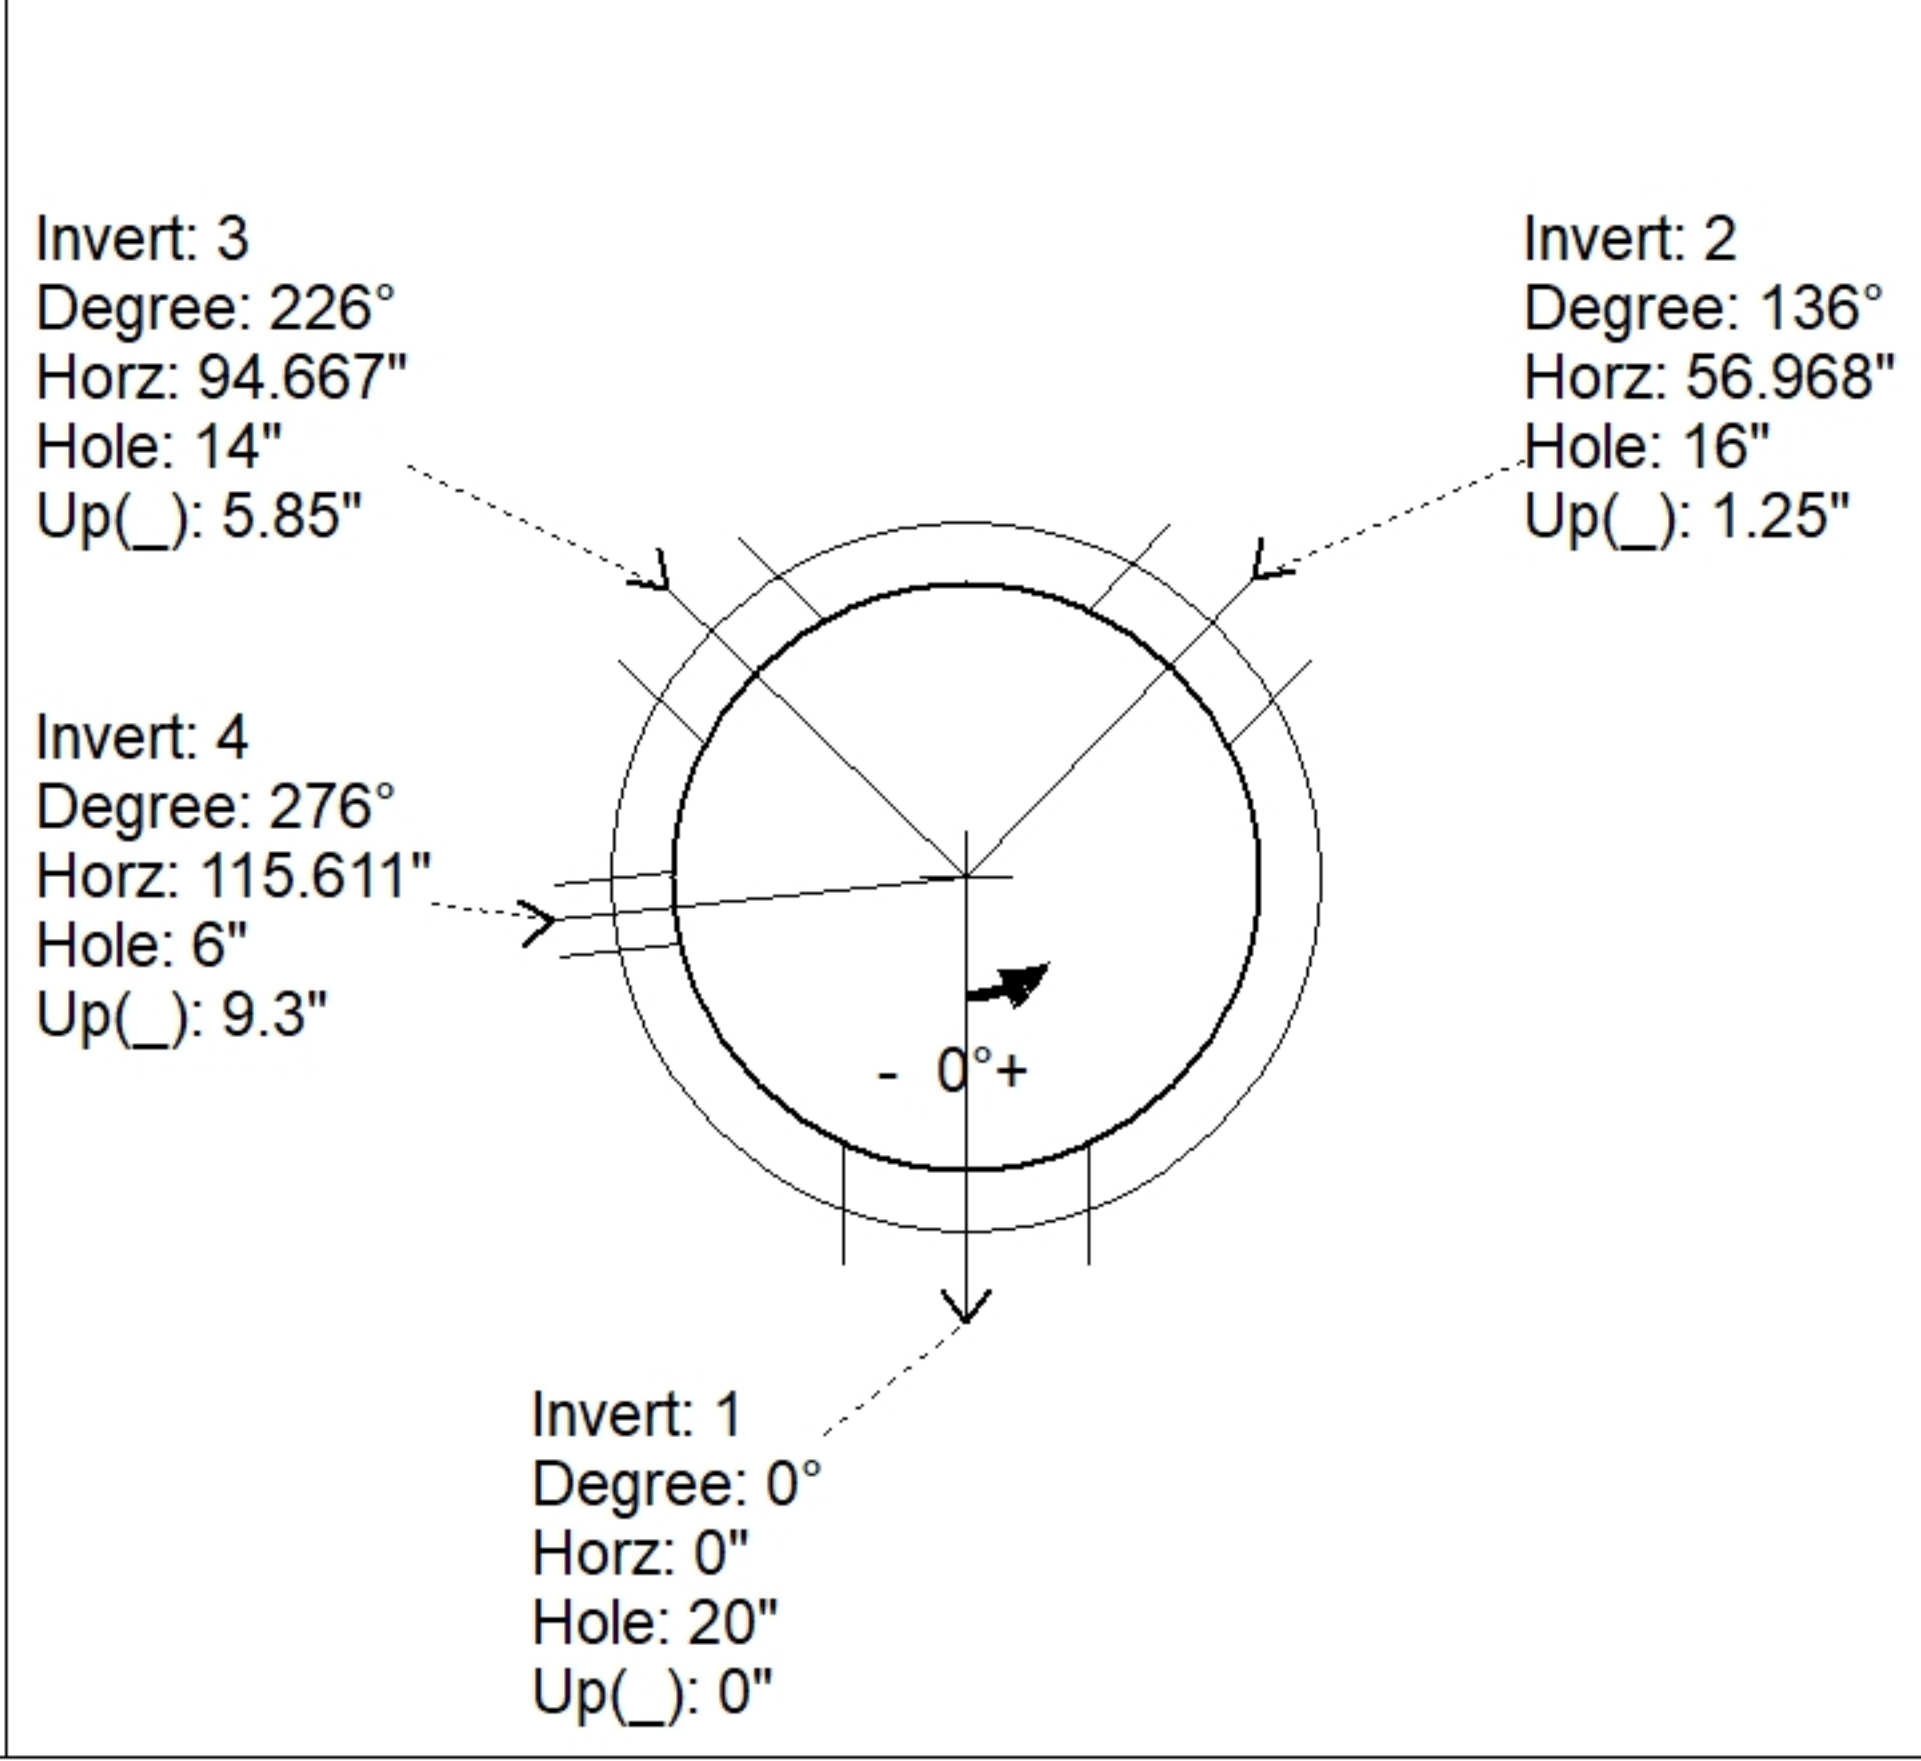
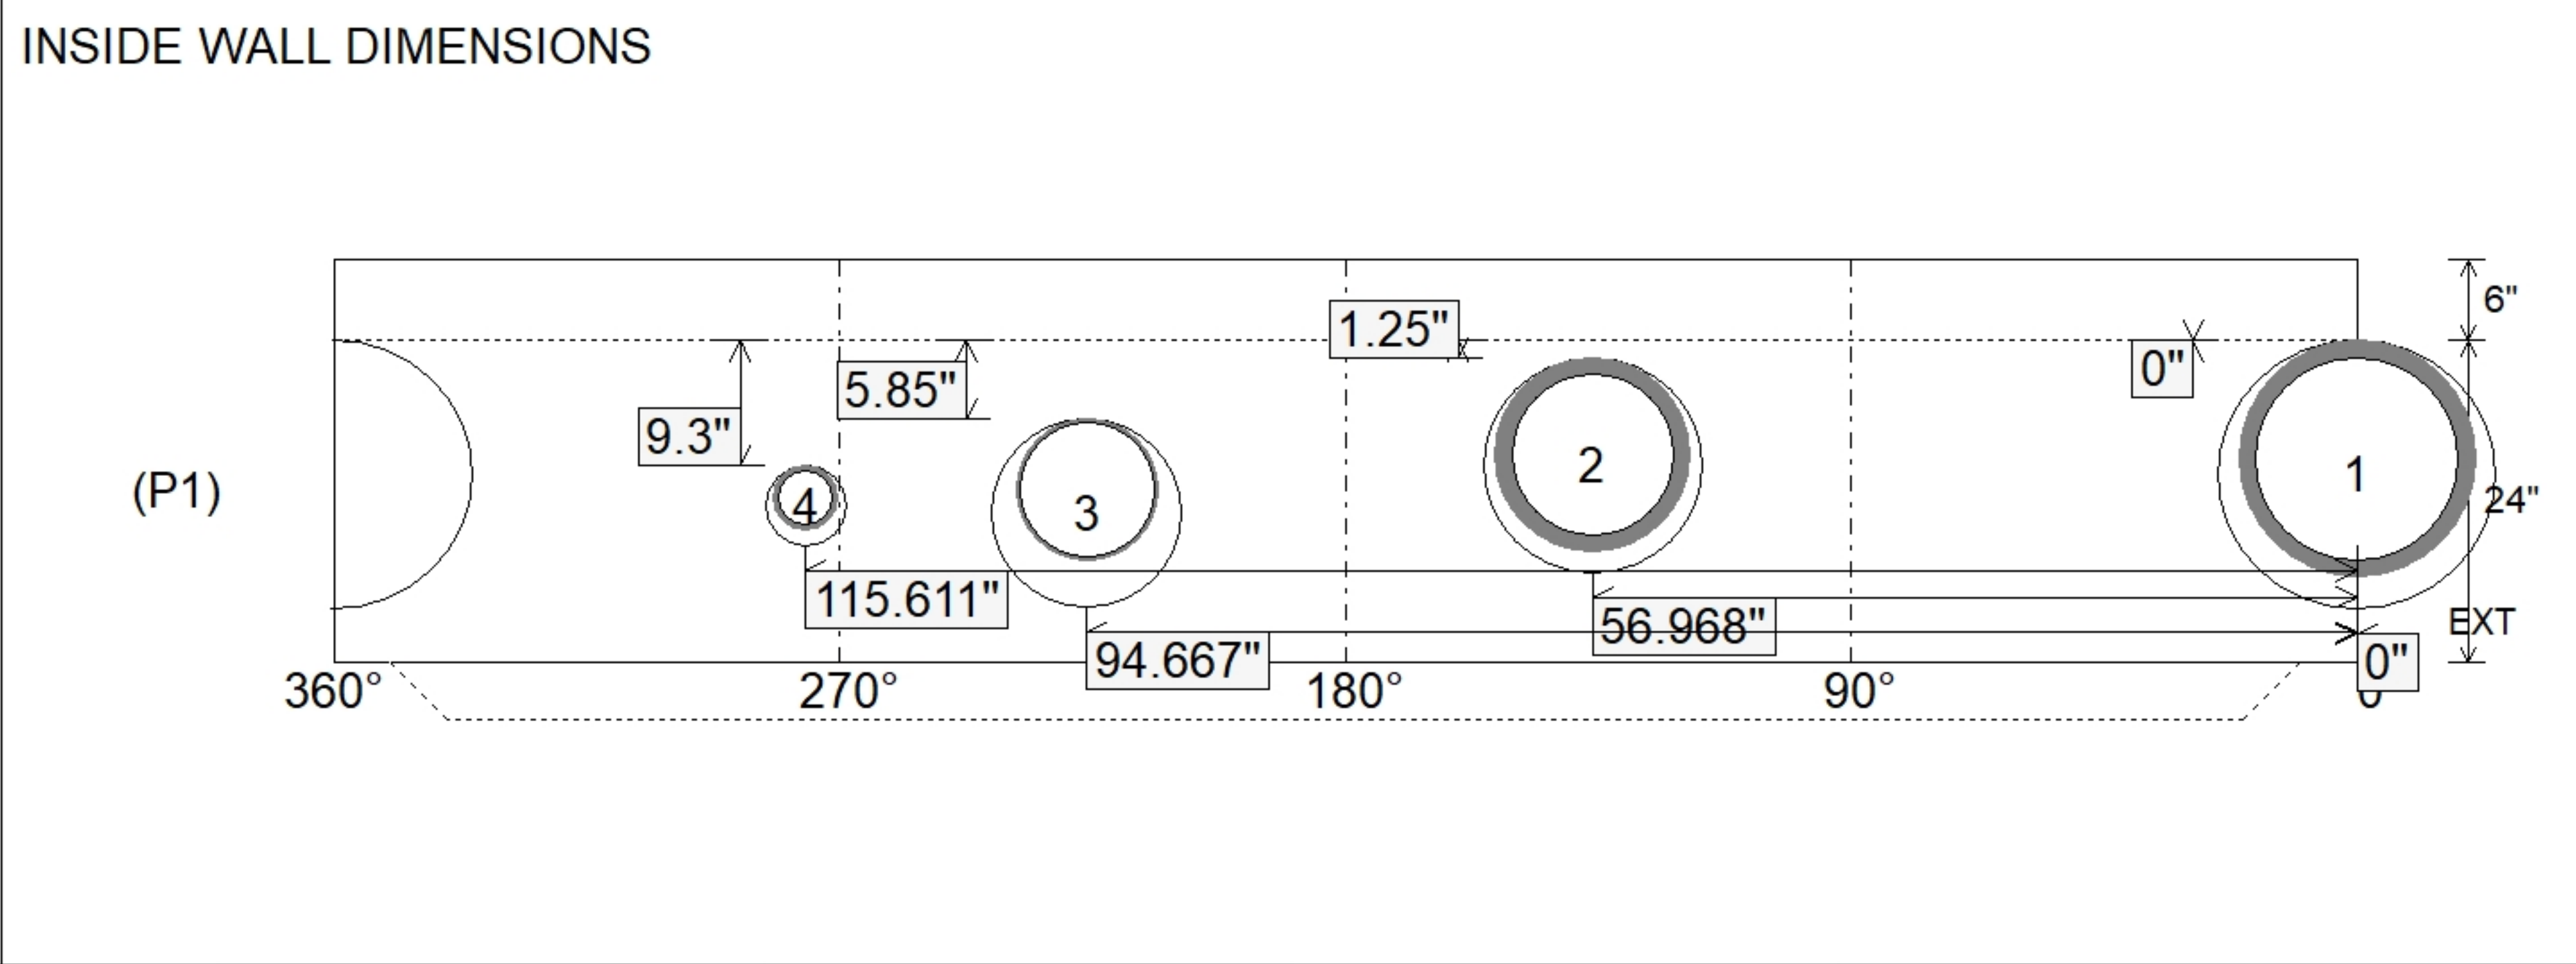


Job Name: 26-2018B Hancock Co Middle School Utility					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: South Lewisport, KY					10/12/2026 8:19:46 AM		PC: A. Chambers				
Contractor: Winwater Hartford KY Co.											
Structure ID: DI-3C ST-MH											
P1 MH048BA24			MH BASE T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 48" - MH FLAT TOP w/ 24" Center Hole F/G - 12" P1) 48" - MH BASE T/n - 24" 1) CASTING - HOE MC-315 F/C Storm 1) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 16 1) Hole - 14 1) Hole - 6					0 lb 270 lb 1580 lb 2709 lb 258 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 4816 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C "STORM"). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 412.26' Rim to Invert: 3.96' Slack: 1.82' Sump: 1.3' Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	408.3'	0°	0"	15" HDPE	17.6"	Hole 20	20"	20.629"	0"	0"	
Invert 2	408.4'	136°	68.836"	12" HDPE	14.5"	Hole 16	16"	16.312"	1.25"	0"	
Invert 3	408.7'	226°	114.389"	10" PVC SDR35	10.5"	Hole 14	14"	14.207"	5.85"	0"	
Invert 4	409'	276°	139.696"	4" HDPE	4.8"	Hole 6	6"	6.016"	9.3"	0"	
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions)  INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 24" Height (Ext): 30"		Weight (Net): 2709 lb Volume (Net): 0.69cu.yd		
