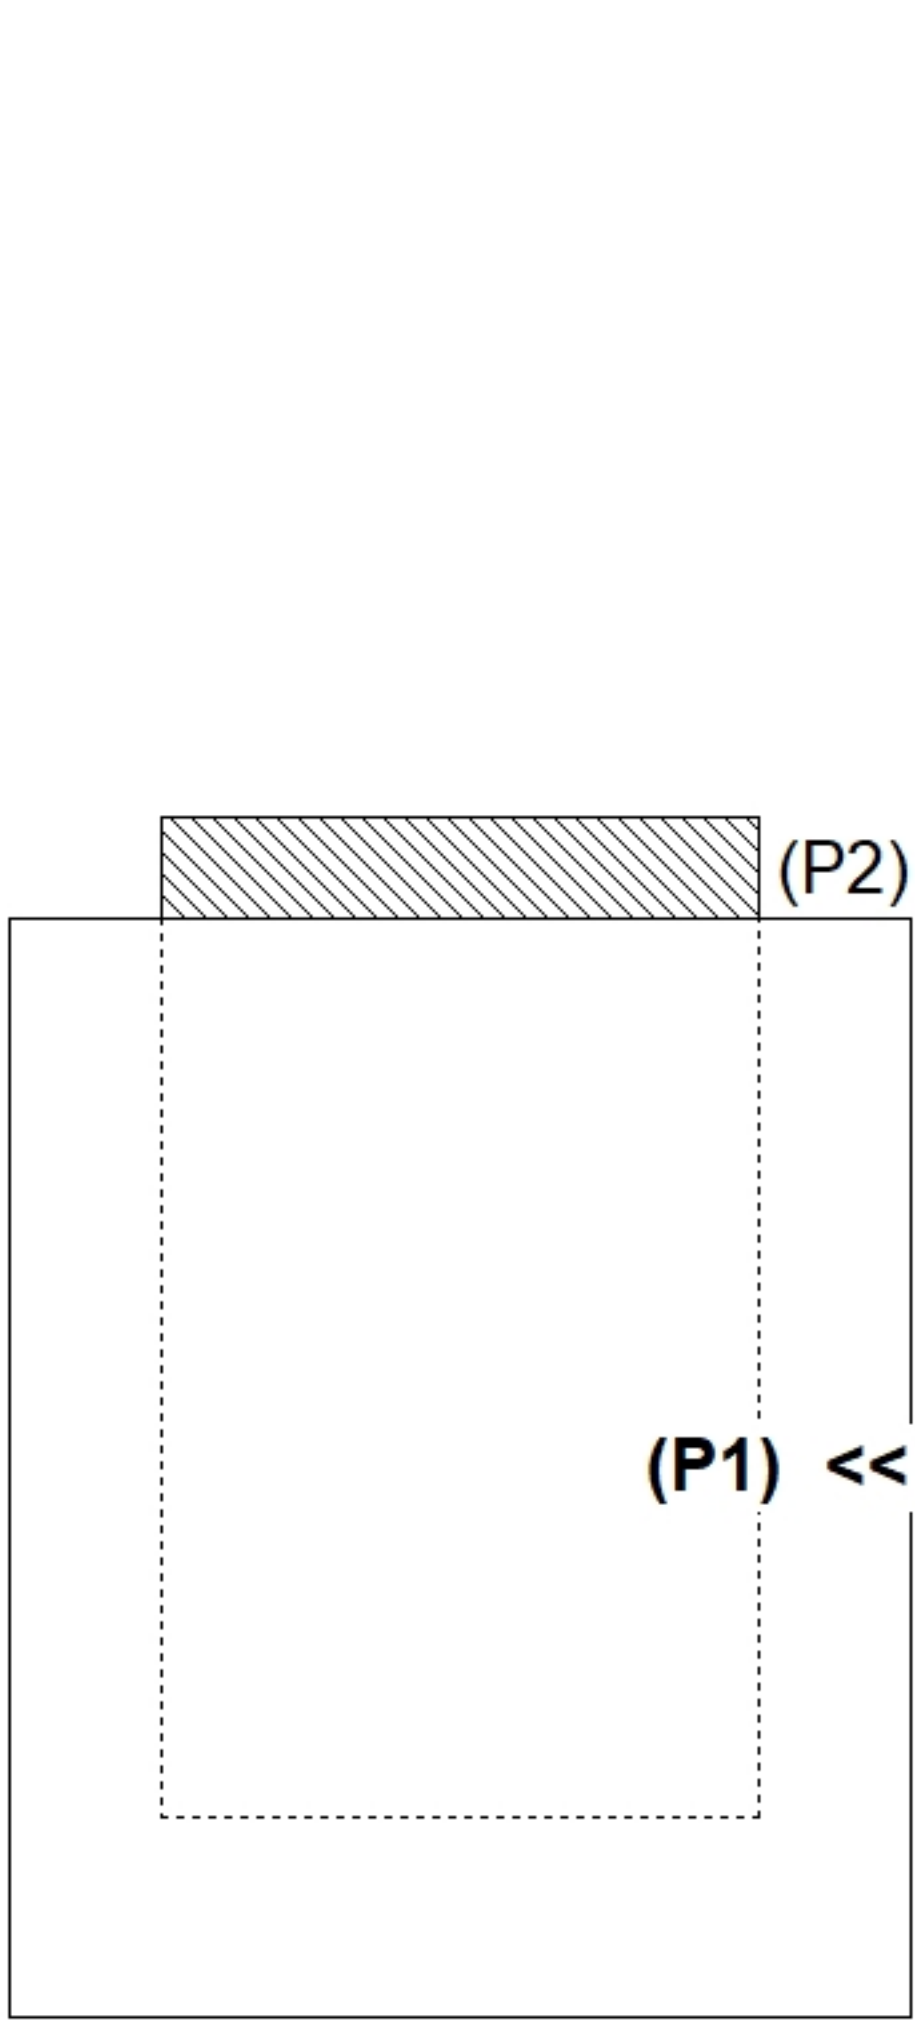
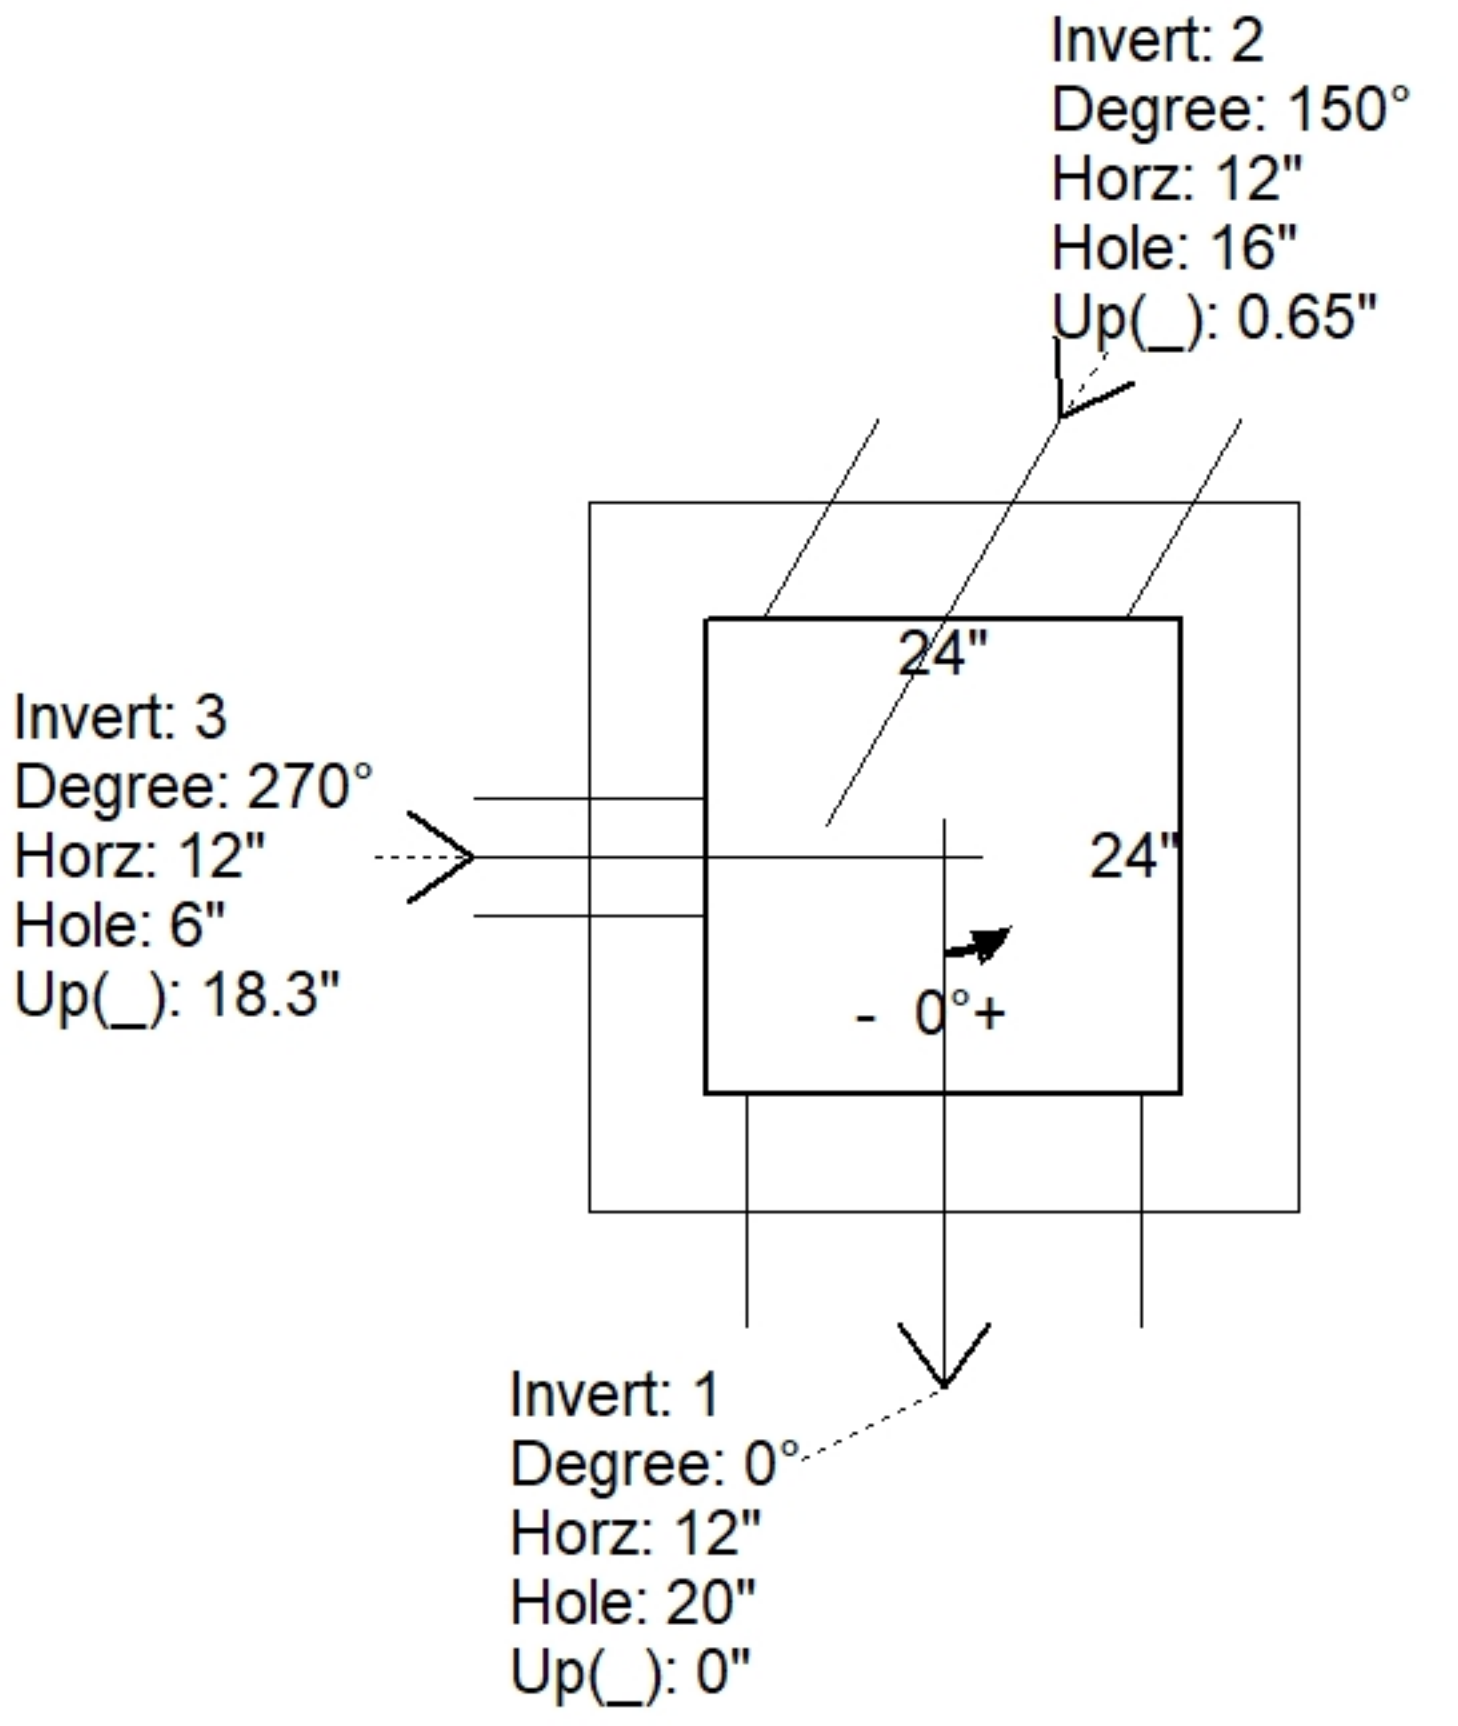
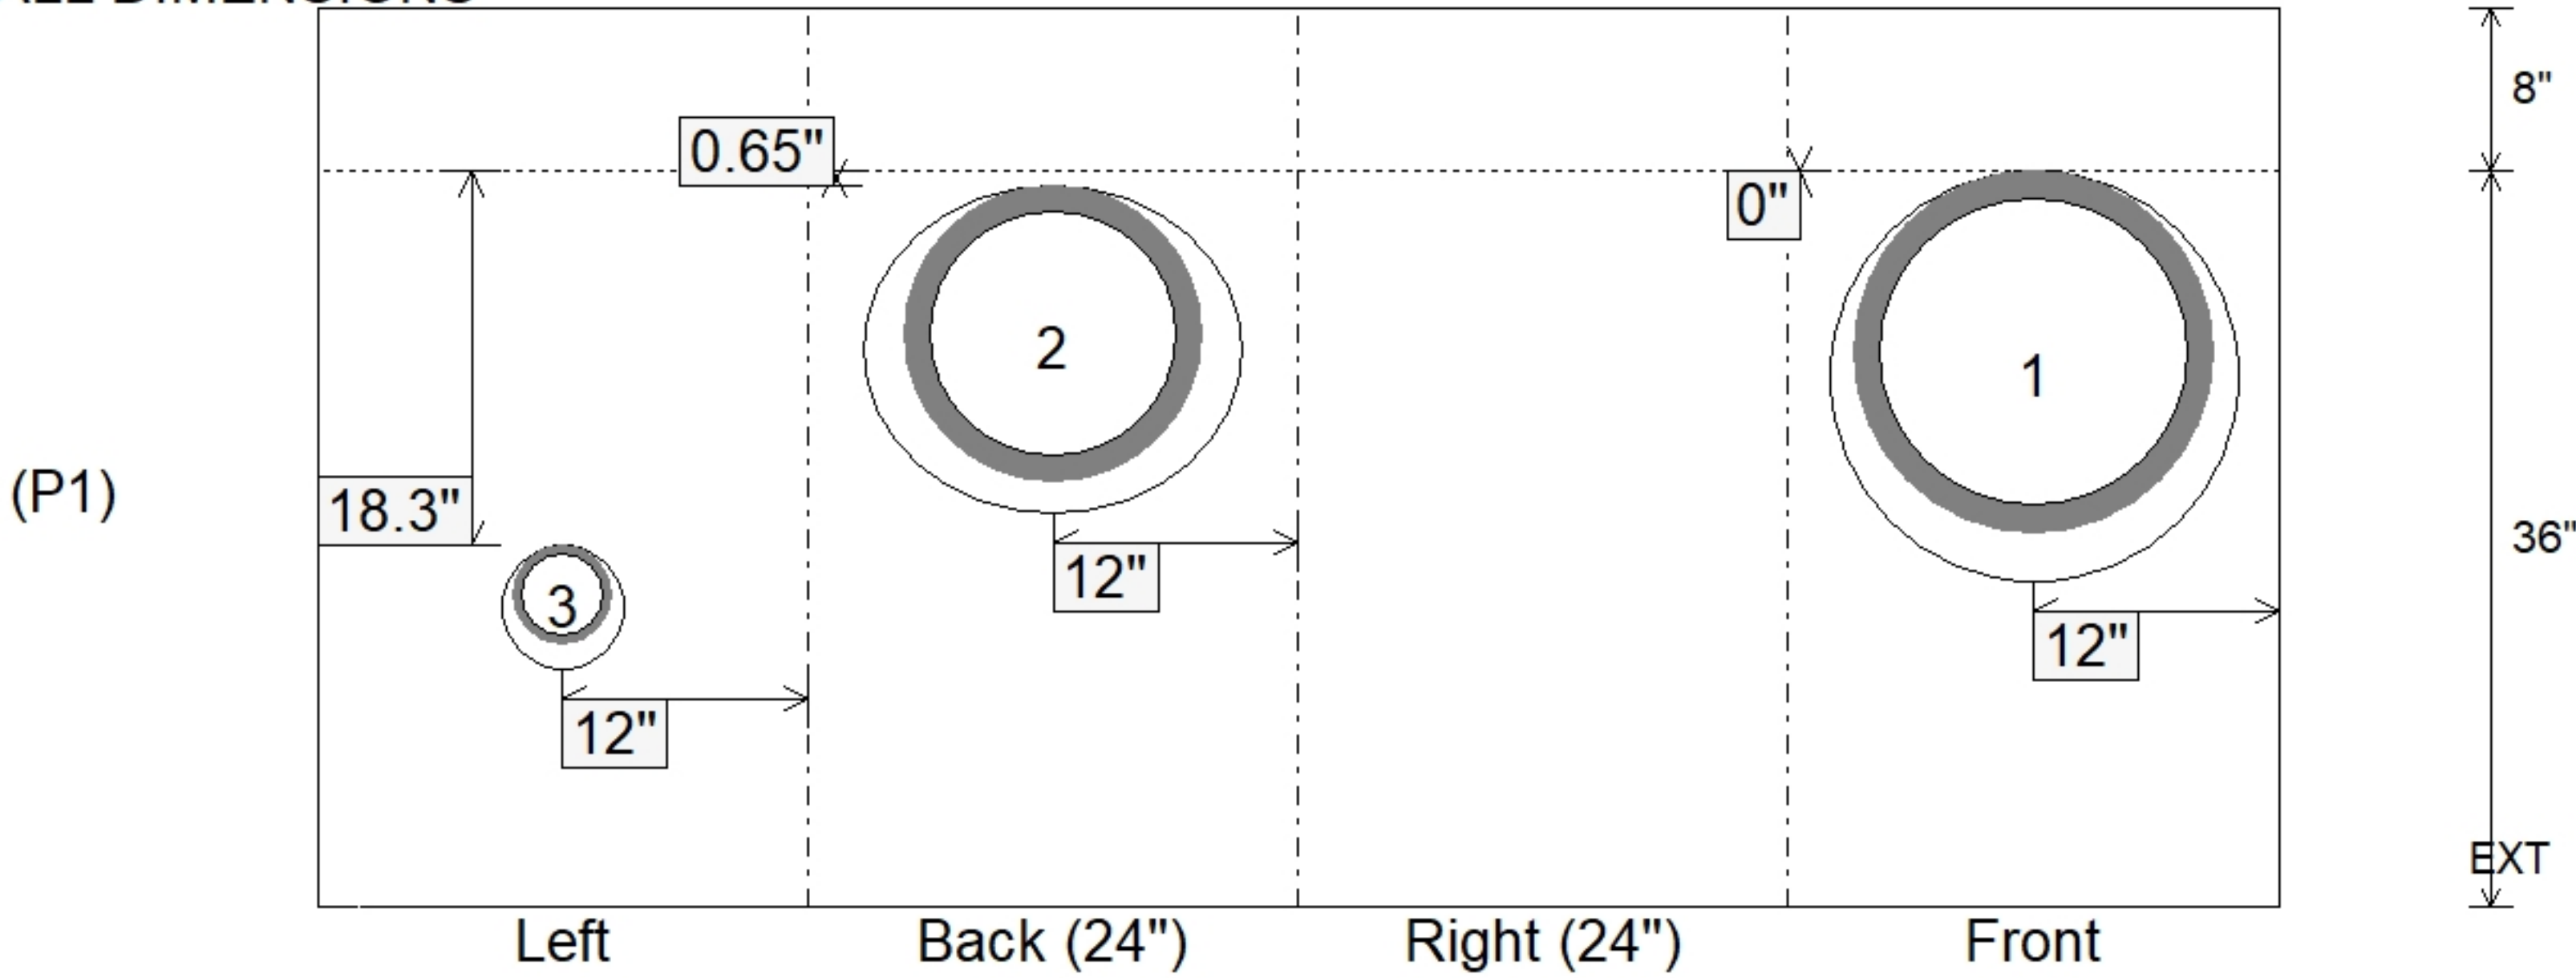


Job Name: 26-2018B Hancock Co Middle School Utility					Plant: Beaver Dam		Tech: S. Felletter				
Job Location: South Lewisport, KY					10/12/2026 8:19:39 AM		PC: A. Chambers				
Contractor: Winwater Hartford KY Co.											
Structure ID: DI-5A ST-IN											
P1		BX2424-06W08F-BAVF			BOX BASE 6inW, 8inF, Variable Ht F/n						
P2) 24" x 24" - CASTING HEIGHT - 4" P1) 24" x 24" - BOX BASE 6inW, 8inF, Variable Ht F/n - 36" 1) CASTING - HOE 280T F/G 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 16 1) Hole - 6					0 lb 2756 lb 182 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 2938 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE 280T F/G). . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 412' Rim to Invert: 3.25' Slack: 0.3" Sump: 1.3" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	408.75'	0°	18"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"	
Invert 2	408.8'	150°	14.536"	12" HDPE	14.5"	Hole 16	16"	18.475"	0.65"	6"	
Invert 3	410.2'	270°	18"	4" HDPE	4.8"	Hole 6	6"	6"	18.3"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) 					UPSIDE-DOWN VIEW (int. dimenions) 						
INSIDE WALL DIMENSIONS 											
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 8"		Height (Int): 36" Height (Ext): 44"		Weight (Net): 2756 lb Volume (Net): 0.7cu.yd		
