

Contractor: Winwater Hartford KY Co.

Plant: Beaver Dam




Slack: 0.84"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


1) Hole - 6

0 lb

Structure Total: 6583 lb

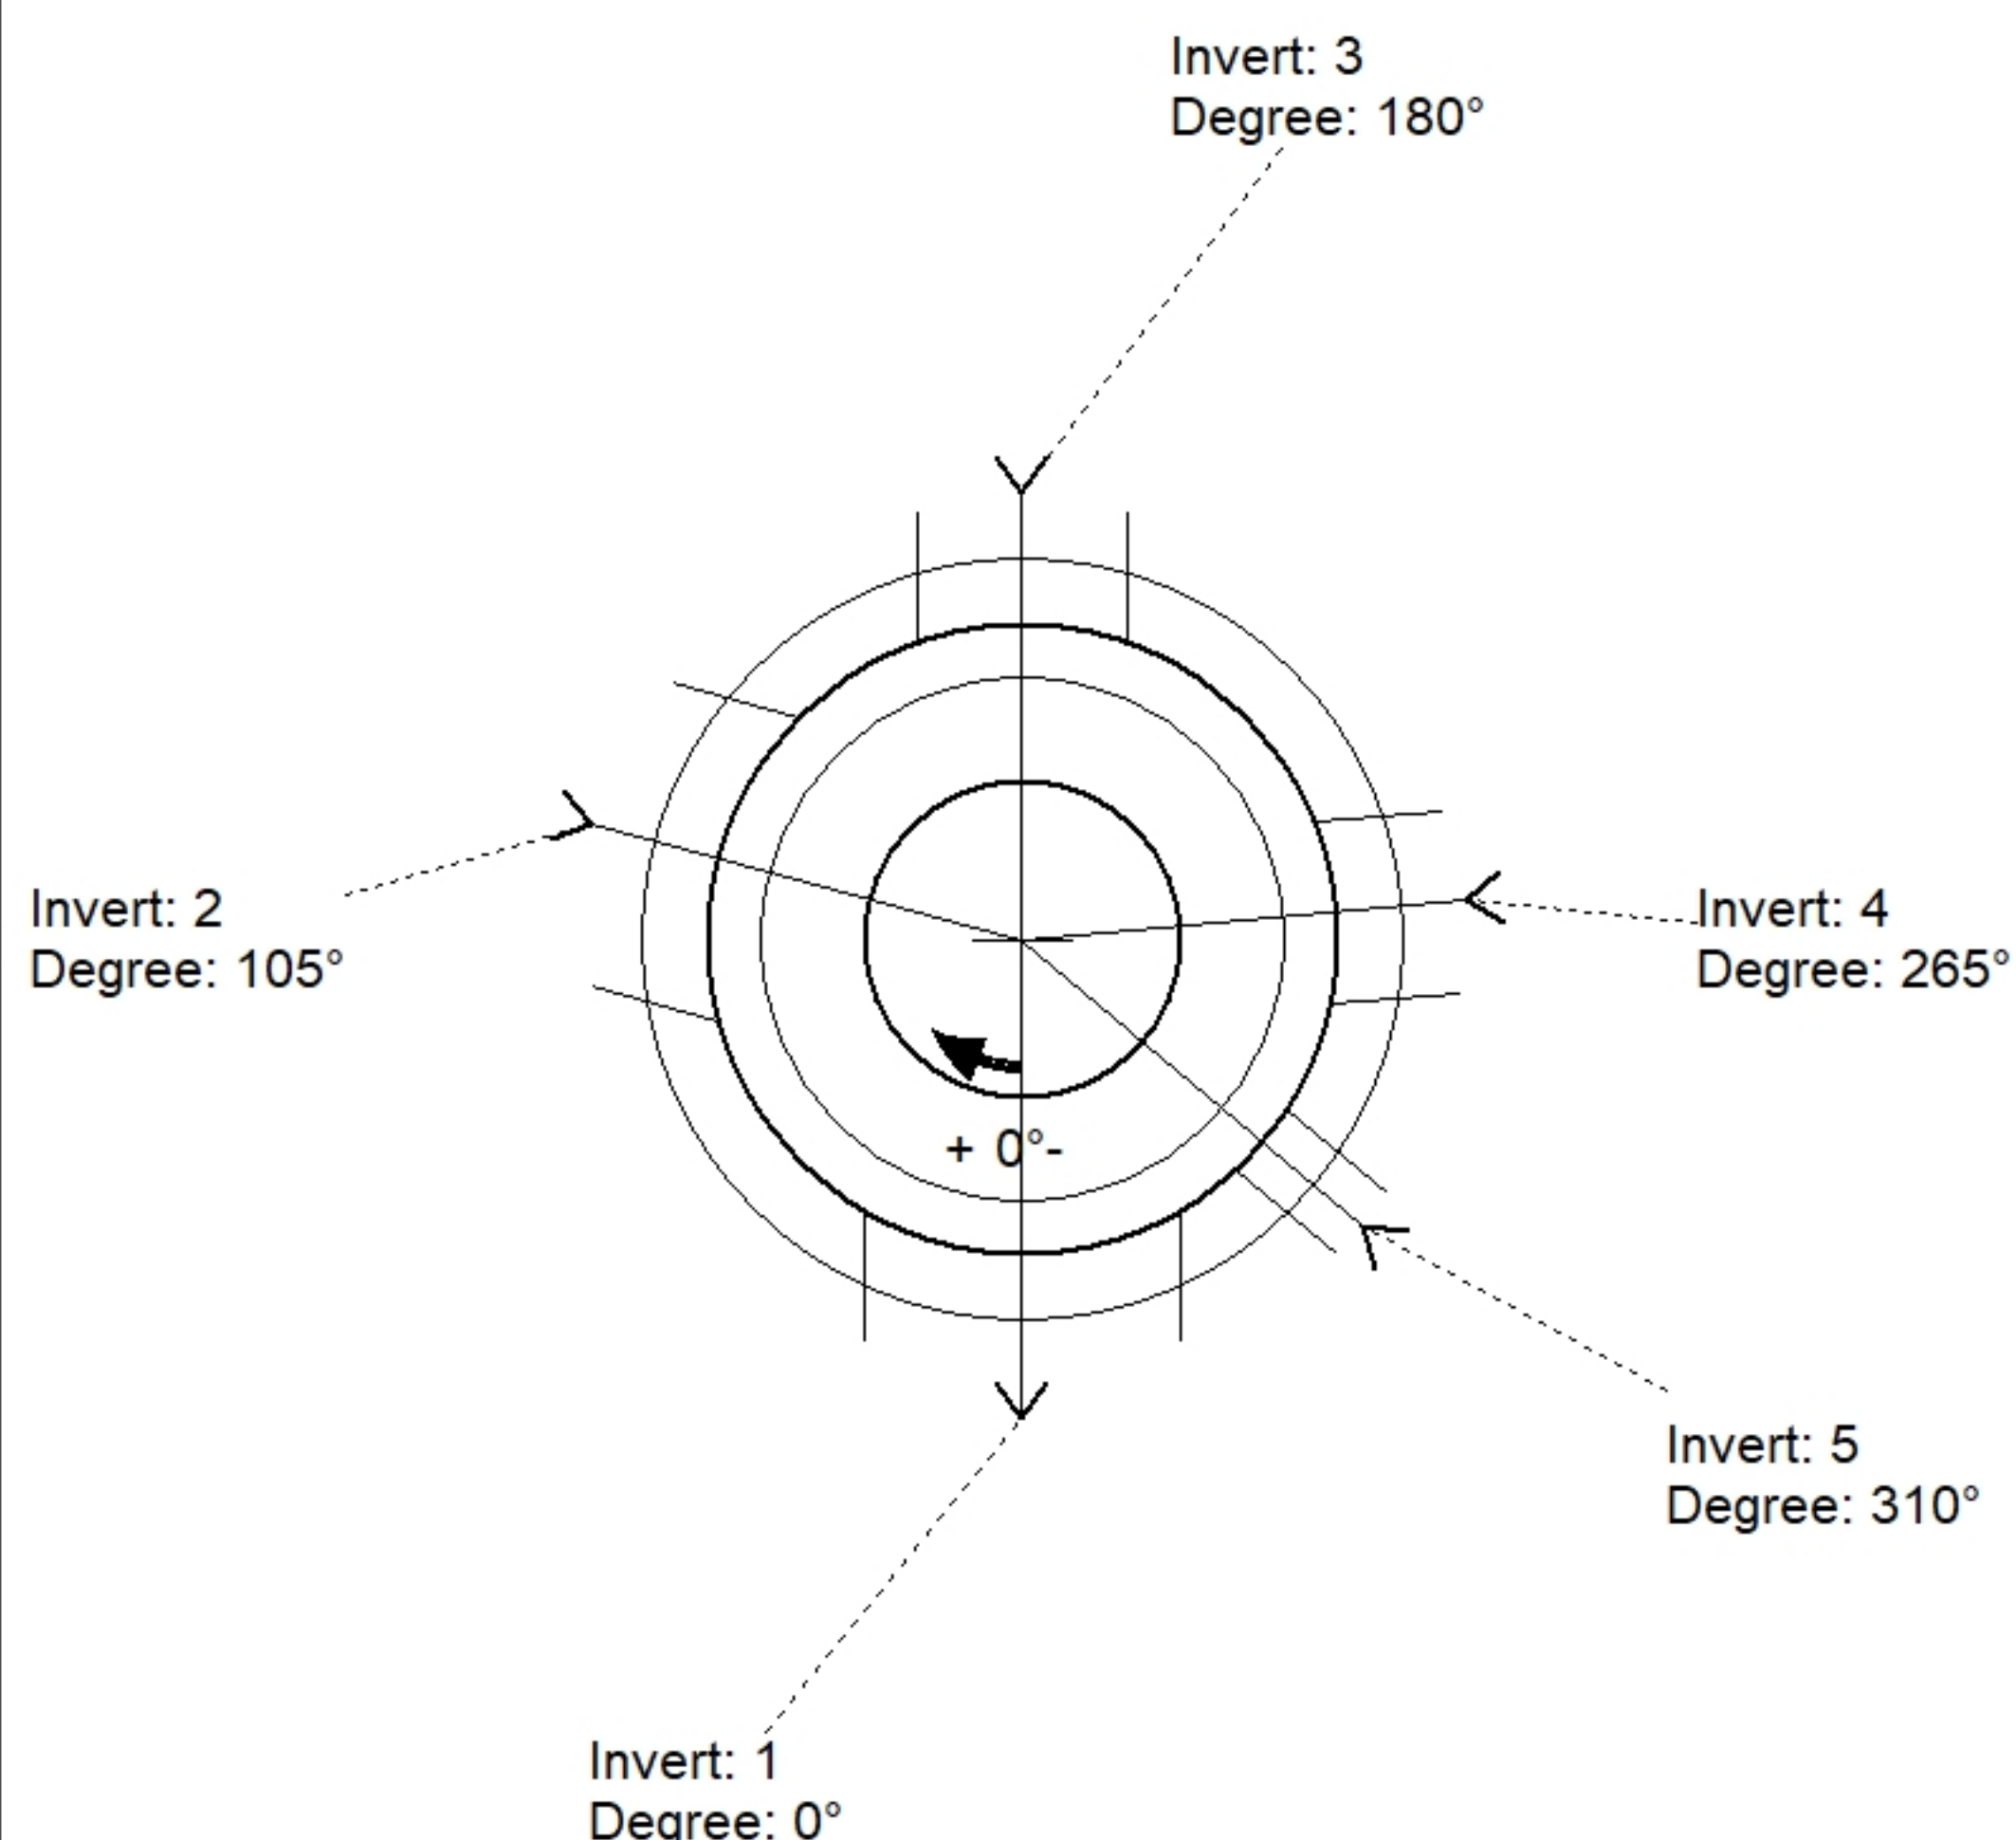

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	413.75'							
Reducer								
Invert 1	407.48'	0°	18" HDPE	21.2"	24"	Hole 24	0"	P1
Invert 2	407.53'	105°	18" HDPE	21.2"	24"	Hole 24	0.6"	P1
Invert 3	407.9'	180°	12" HDPE	14.5"	16"	Hole 16	5.39"	P1
Invert 4	407.9'	265°	10" HDPE	11.4"	14"	Hole 14	5.94"	P1
Invert 5	409.3'	310°	4" HDPE	4.8"	6"	Hole 6	23.04"	P1
Invert 6								
Invert 7								
Invert 8								

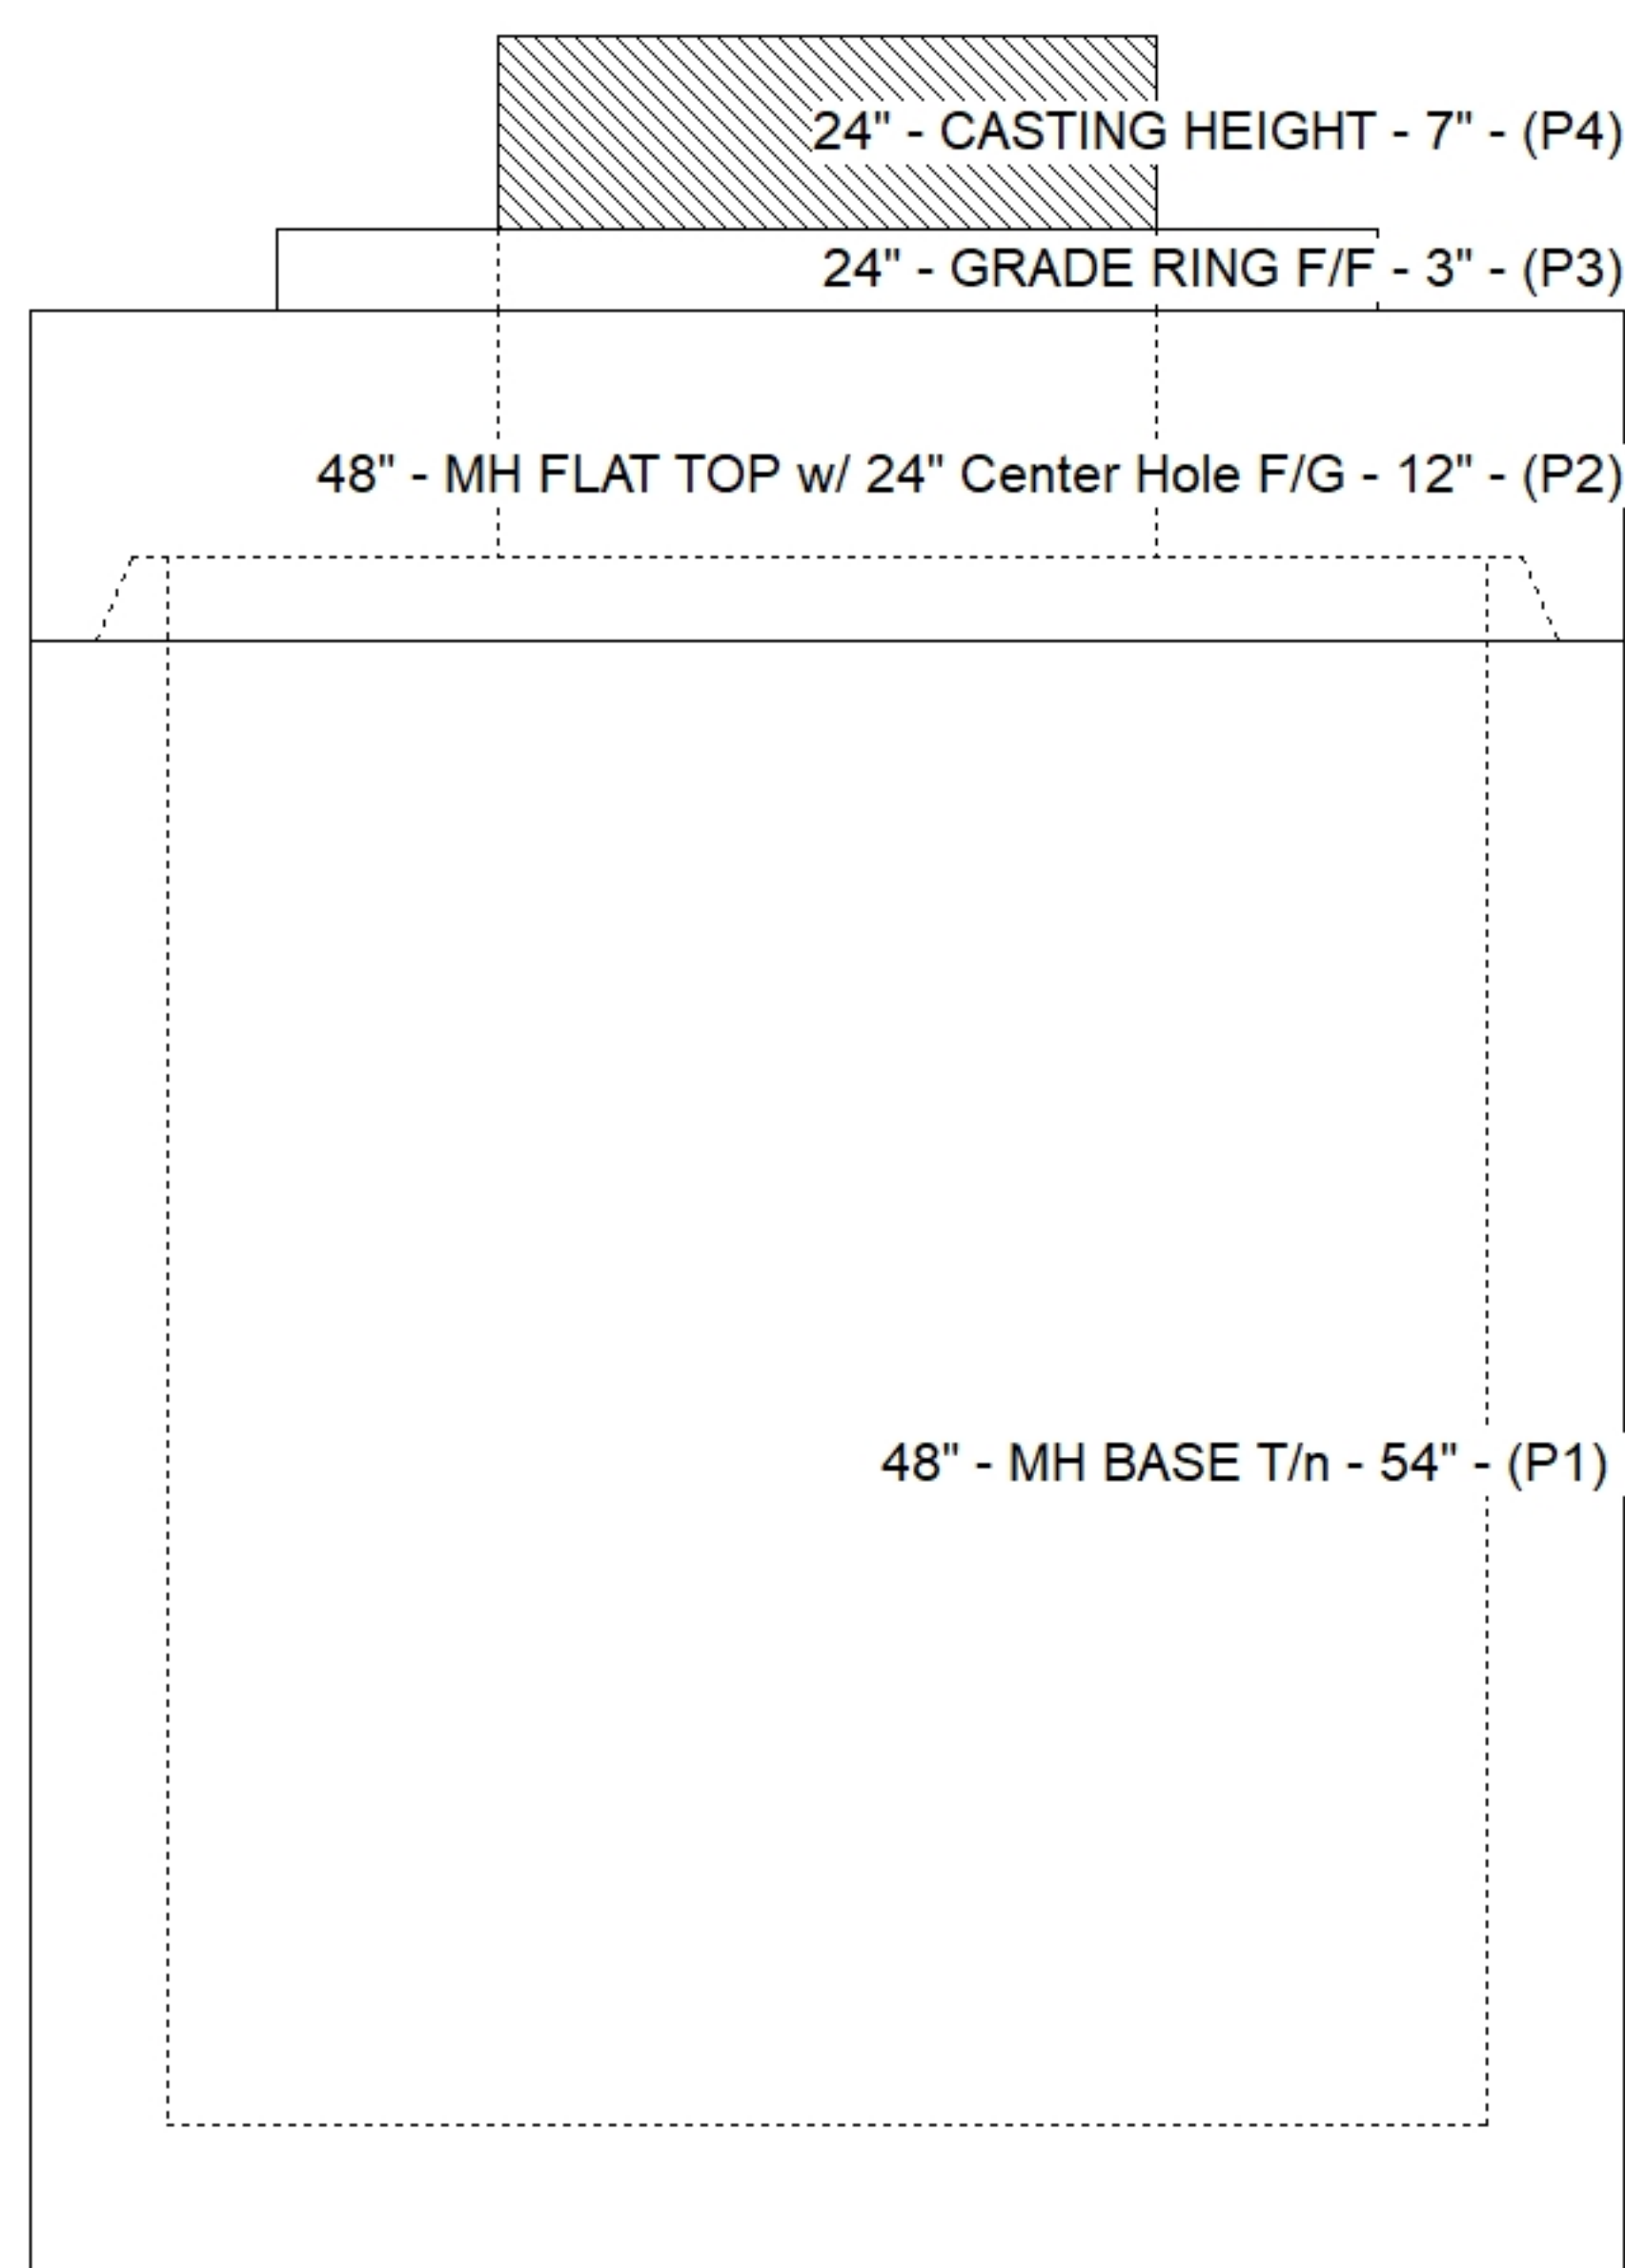

SUBMITTAL
APPROVED BY:
