

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"


Rim to Invert: 5.67'

Floor Height: 8"

Slack: 3.04"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 13537 lb

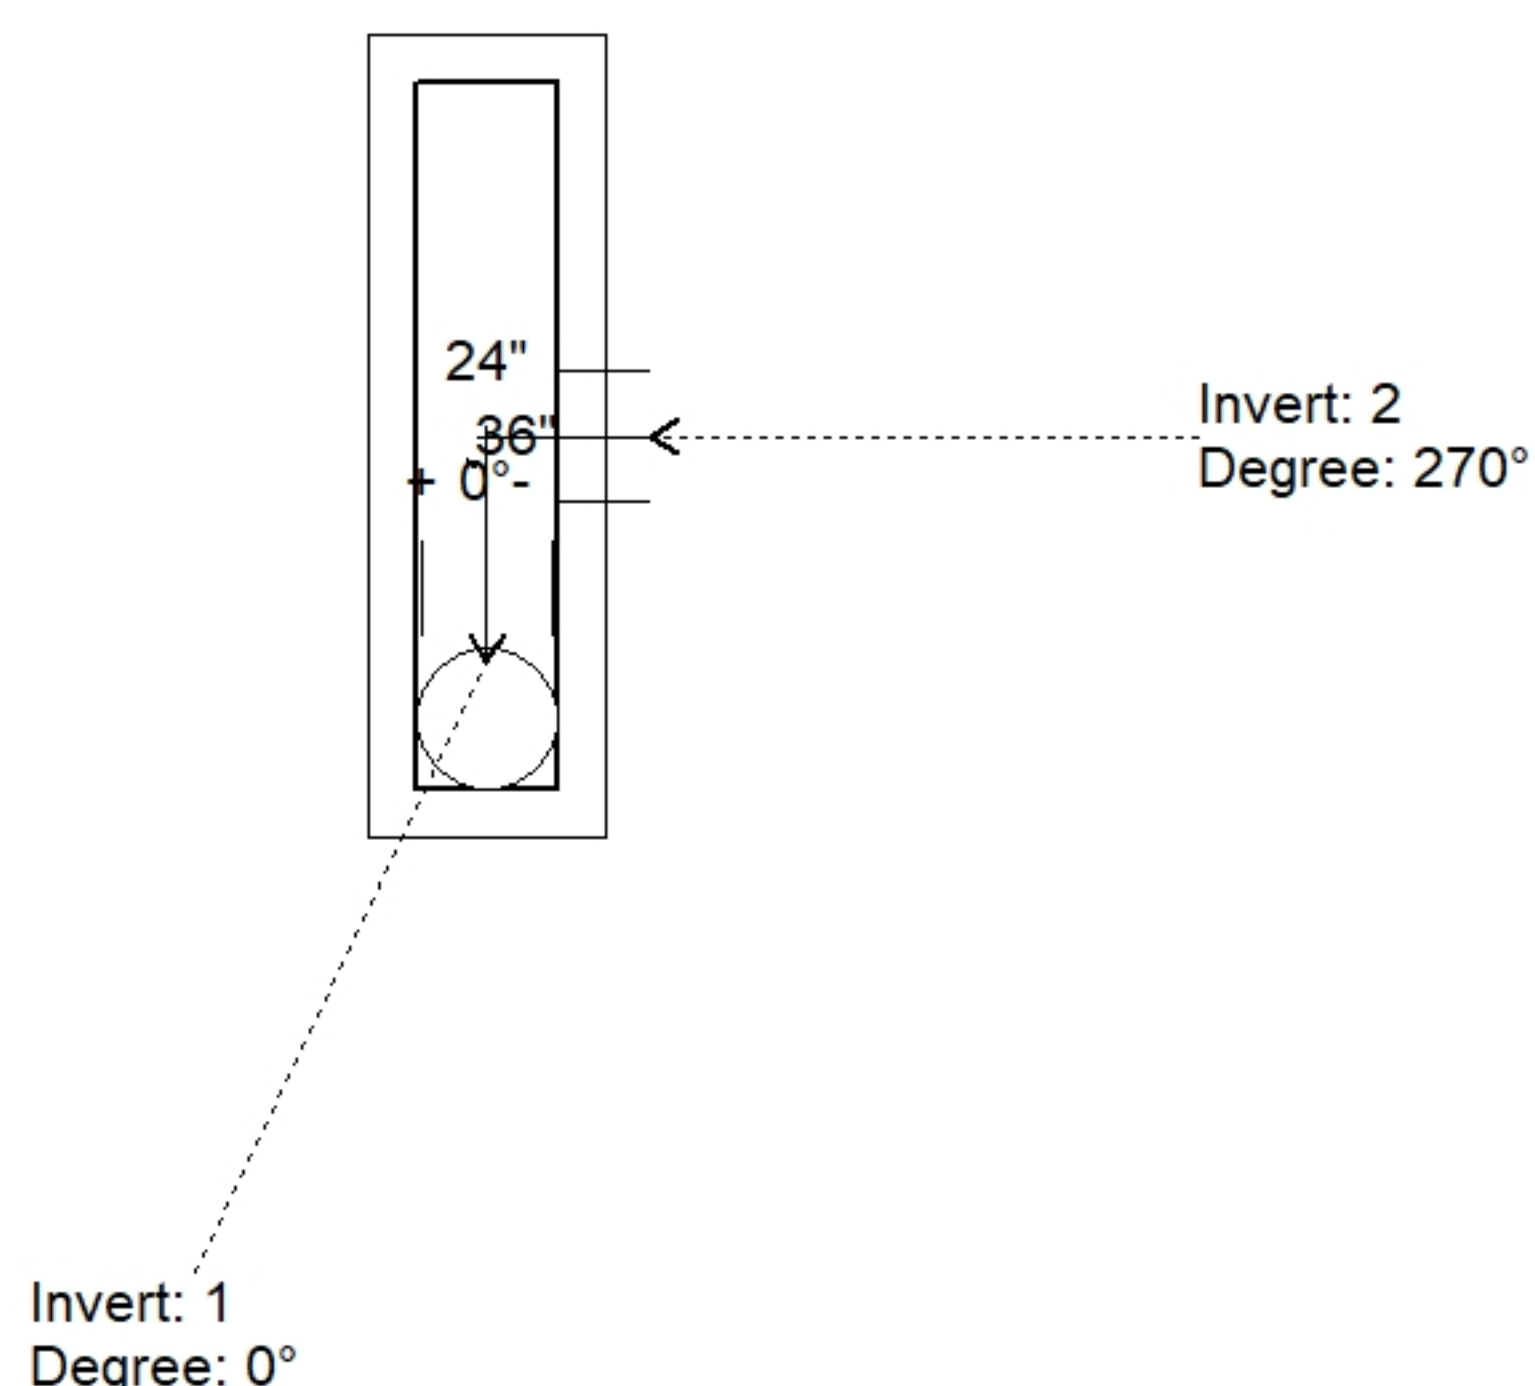


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	576.38'							
Reducer								
Invert 1	570.71'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	570.79'	270°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP LEFT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 37" - (P1)

Default - Interior Dimensions

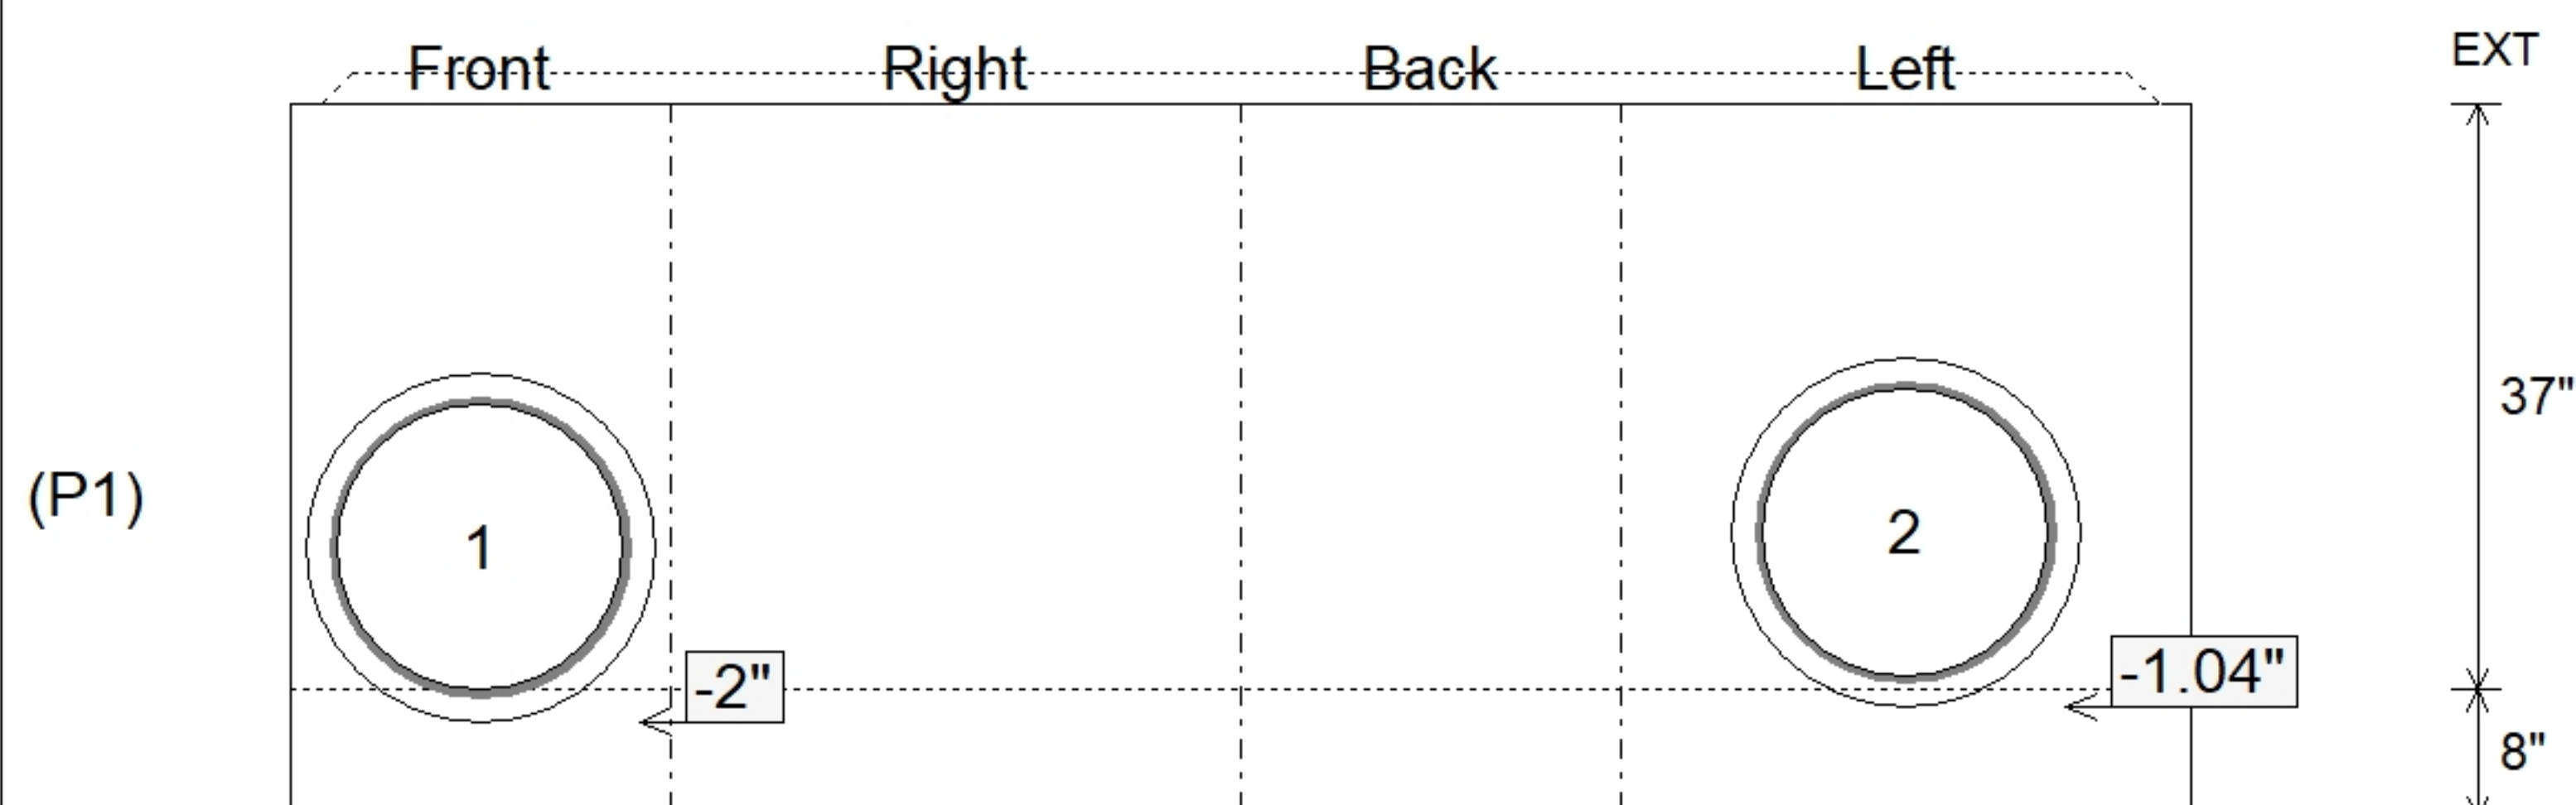

8/27/2026 12:40:49 PM

APPROVED BY:
