

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"


Rim to Invert: 5.67'

Floor Height: 8"

Slack: 3.04"


- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 13282 lb

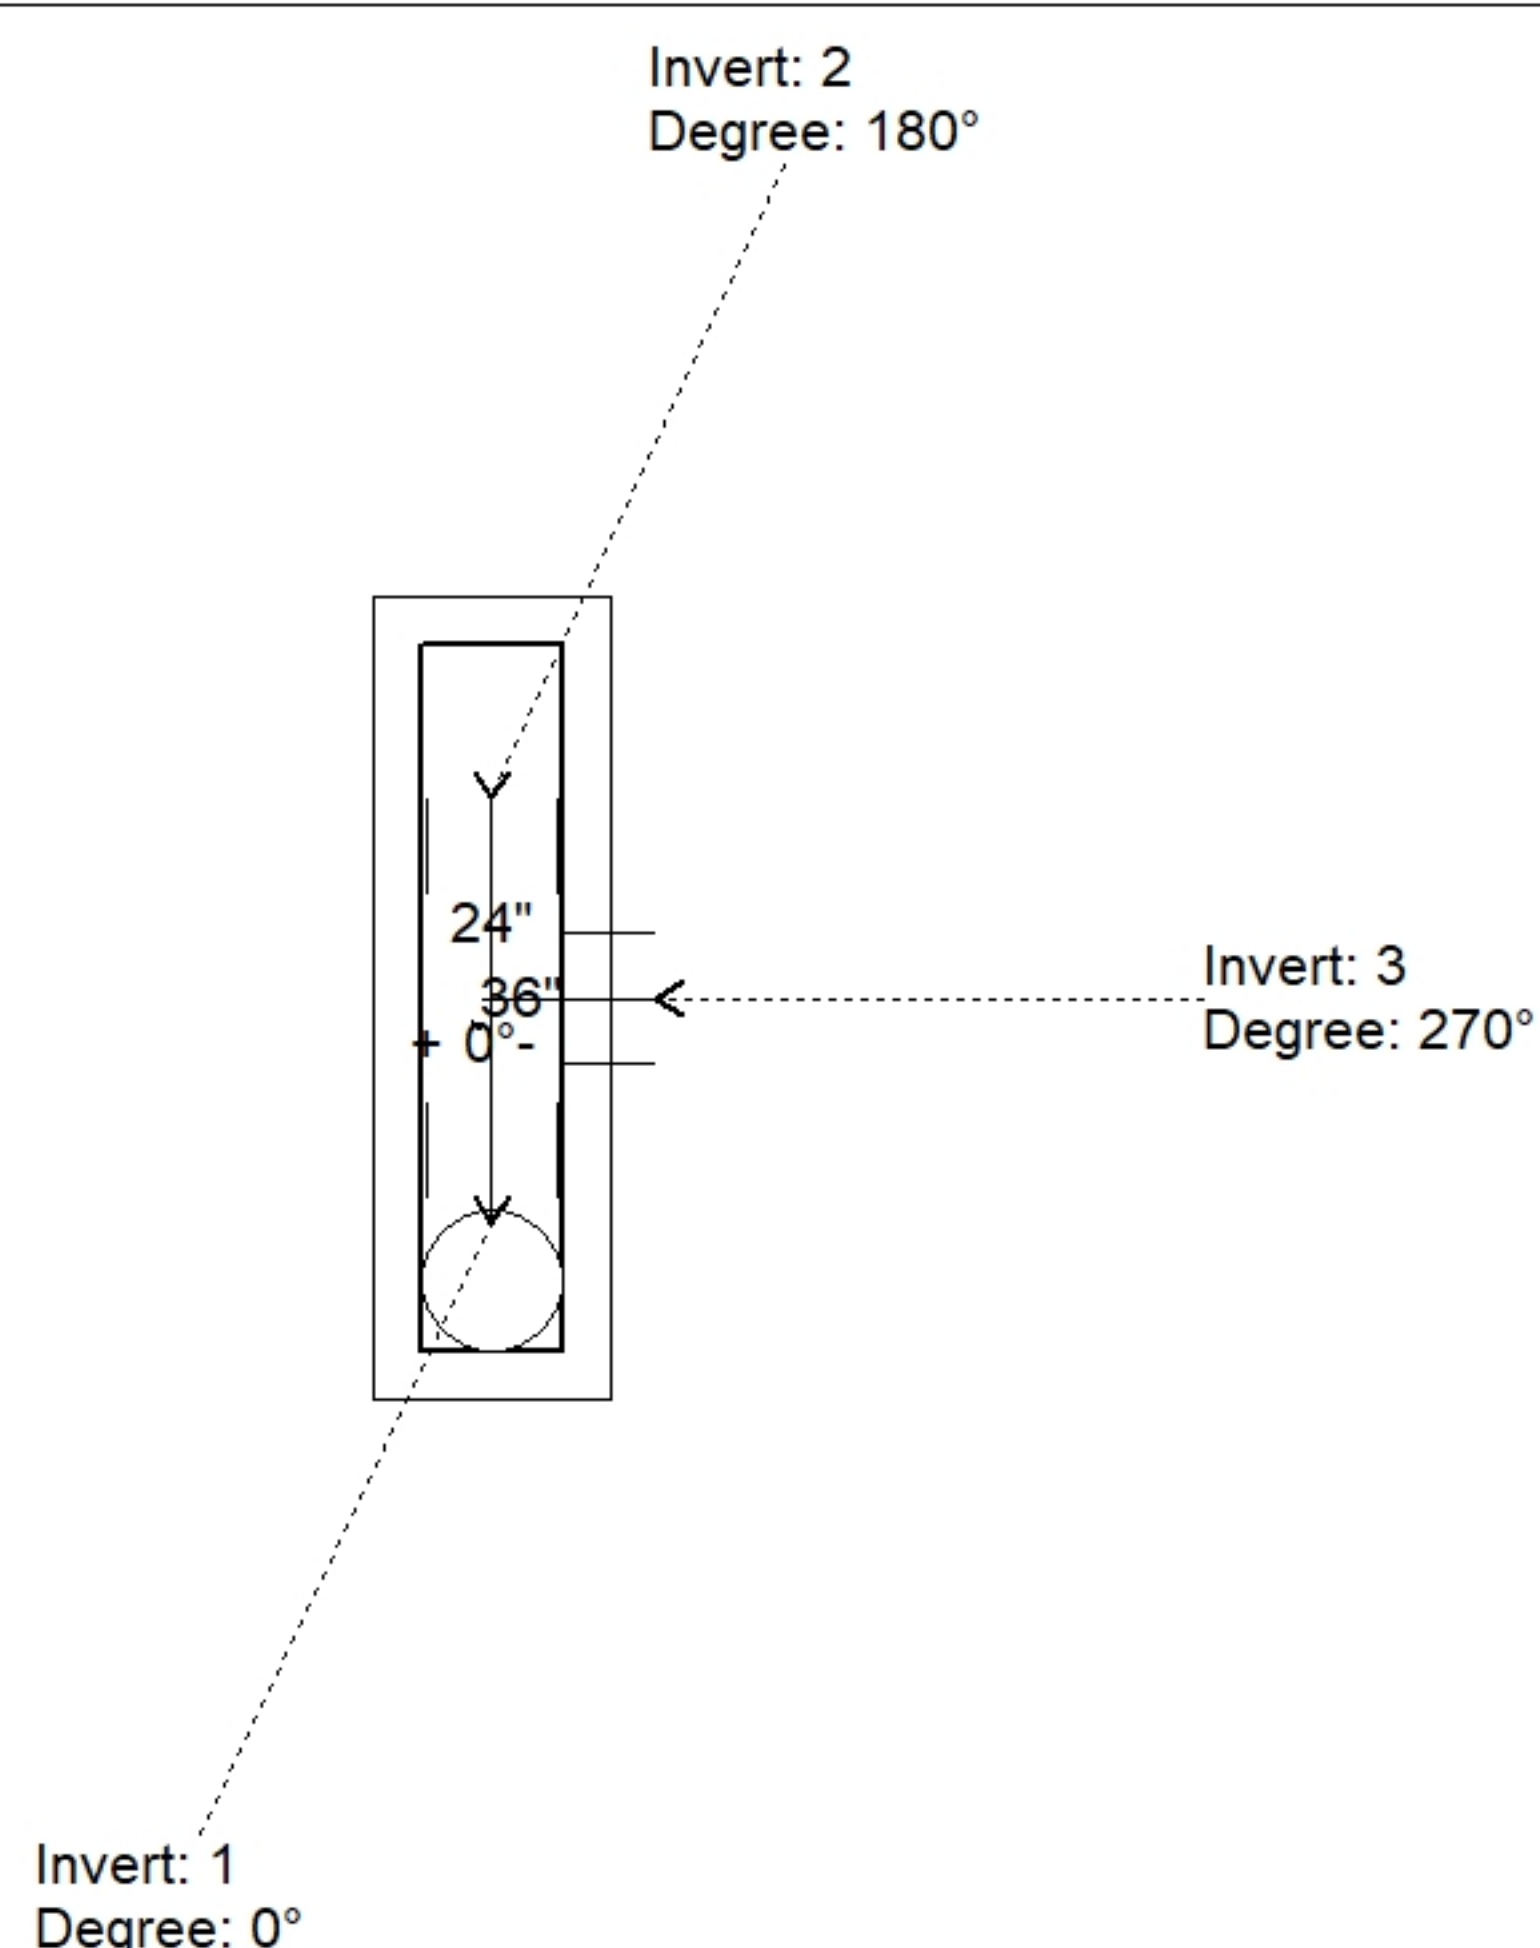

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	556.61'							
Reducer								
Invert 1	550.94'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	551.02'	180°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 3	551.02'	270°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

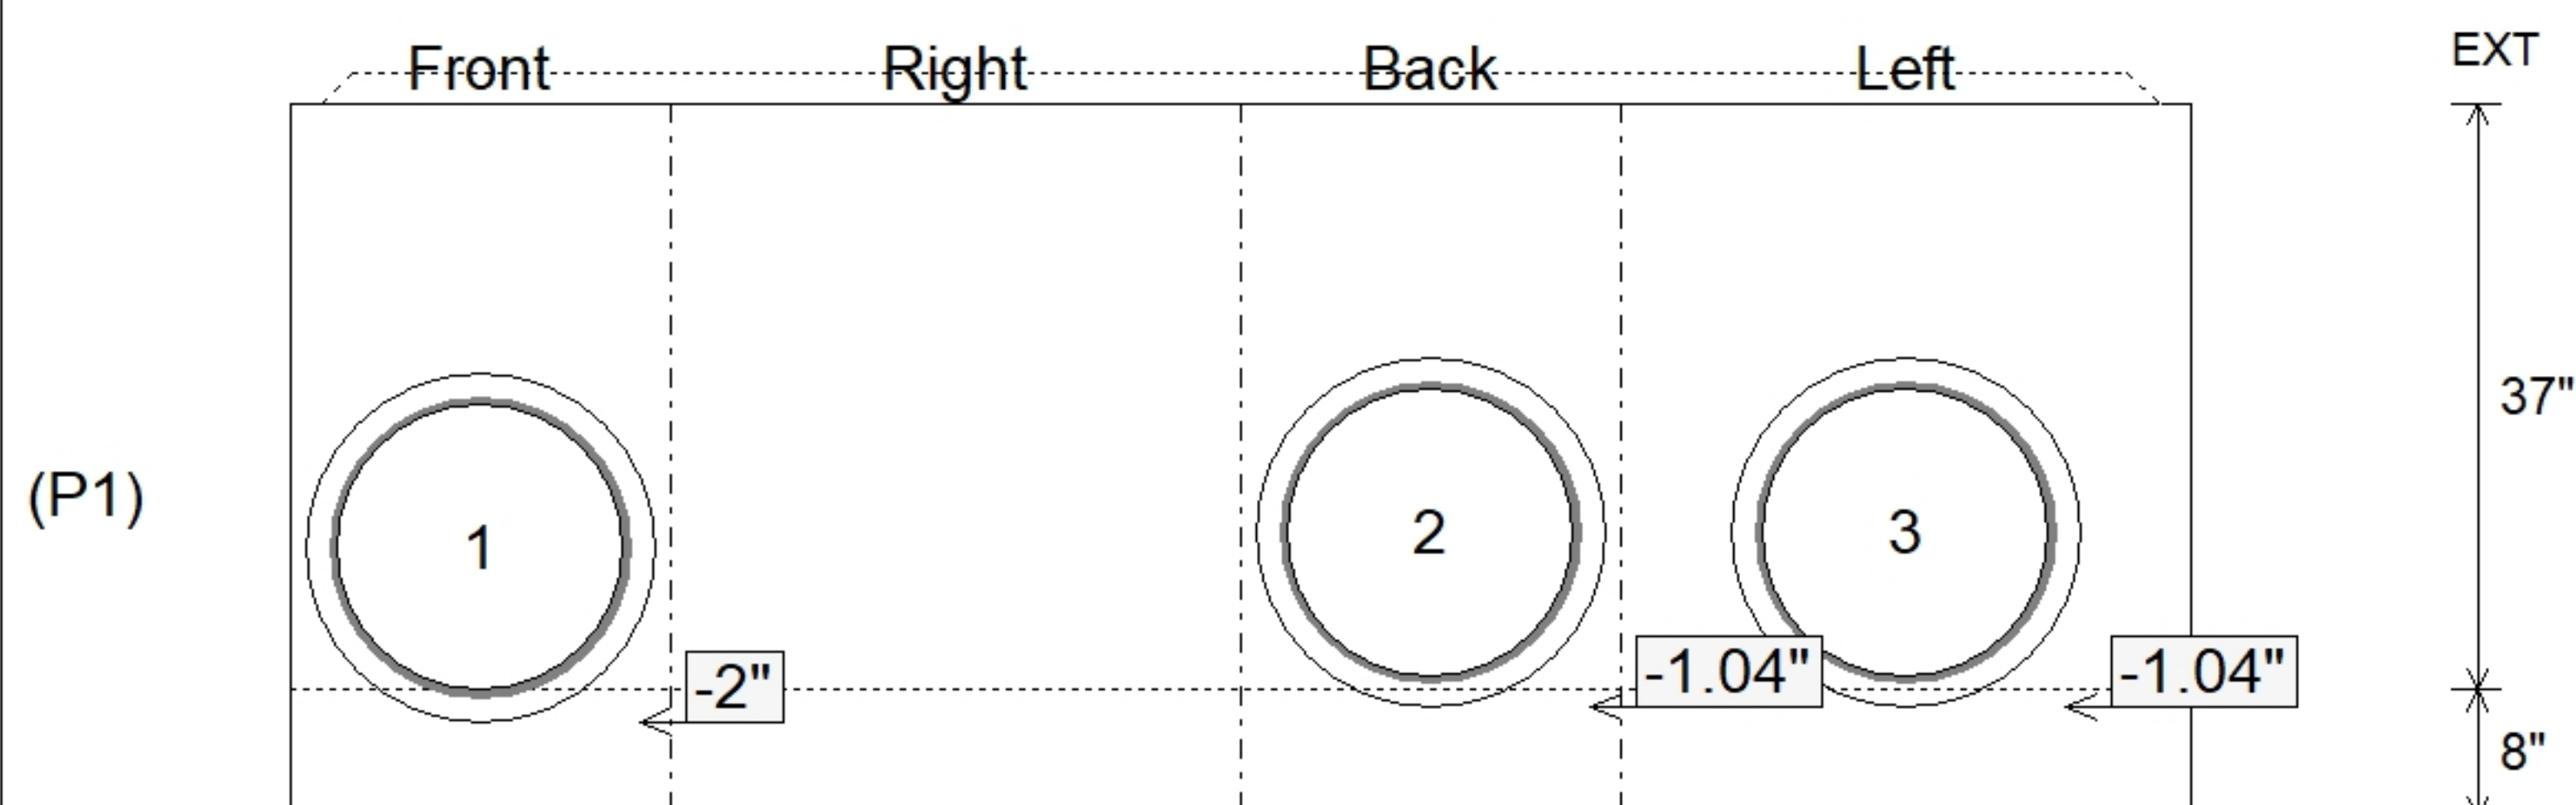

Submittal Drawing
8/27/2026 12:40:50 PM

SUBMITTAL
APPROVED BY:
