

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"

Rim to Invert: 7.67'


Floor Height: 8"

Slack: 3.04"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


0 lb

Structure Total: 17084 lb

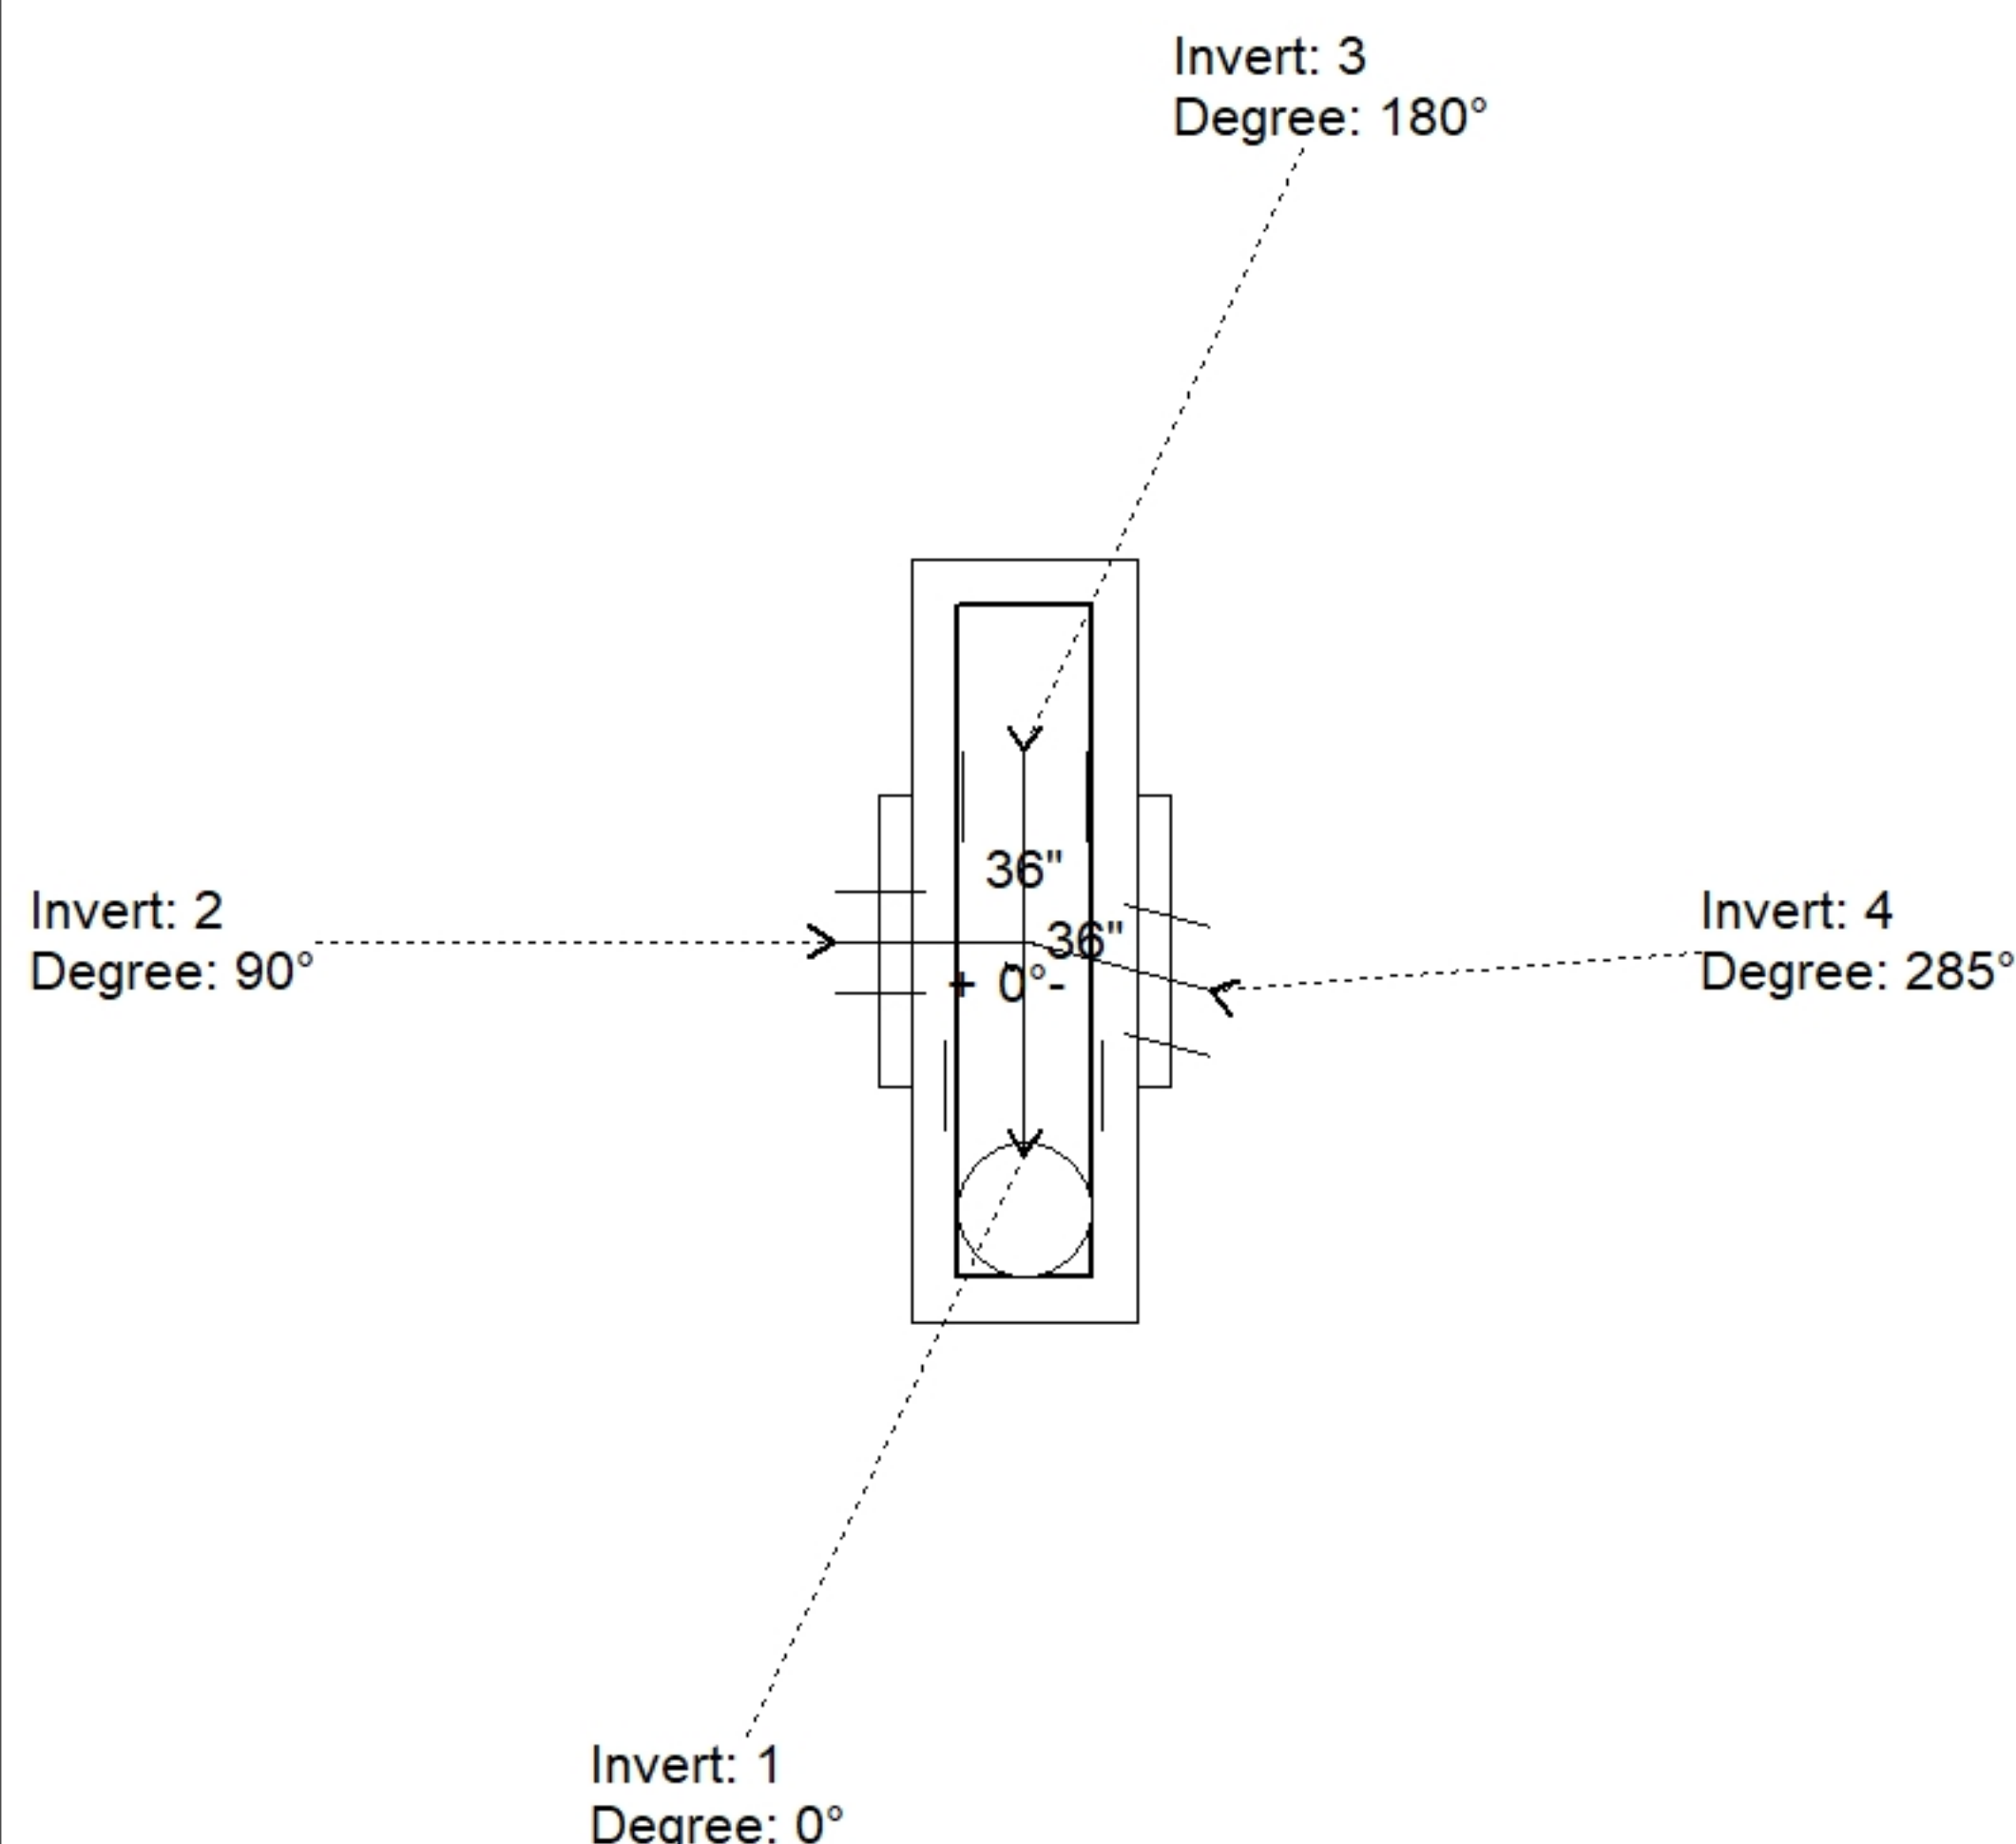

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	545.89'							
Reducer	542.637'							
Invert 1	538.22'	0°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	538.3'	90°	15" CMP	16"	18"	Hole 18	-0.54"	P1
Invert 3	538.3'	180°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 4	538.3'	285°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

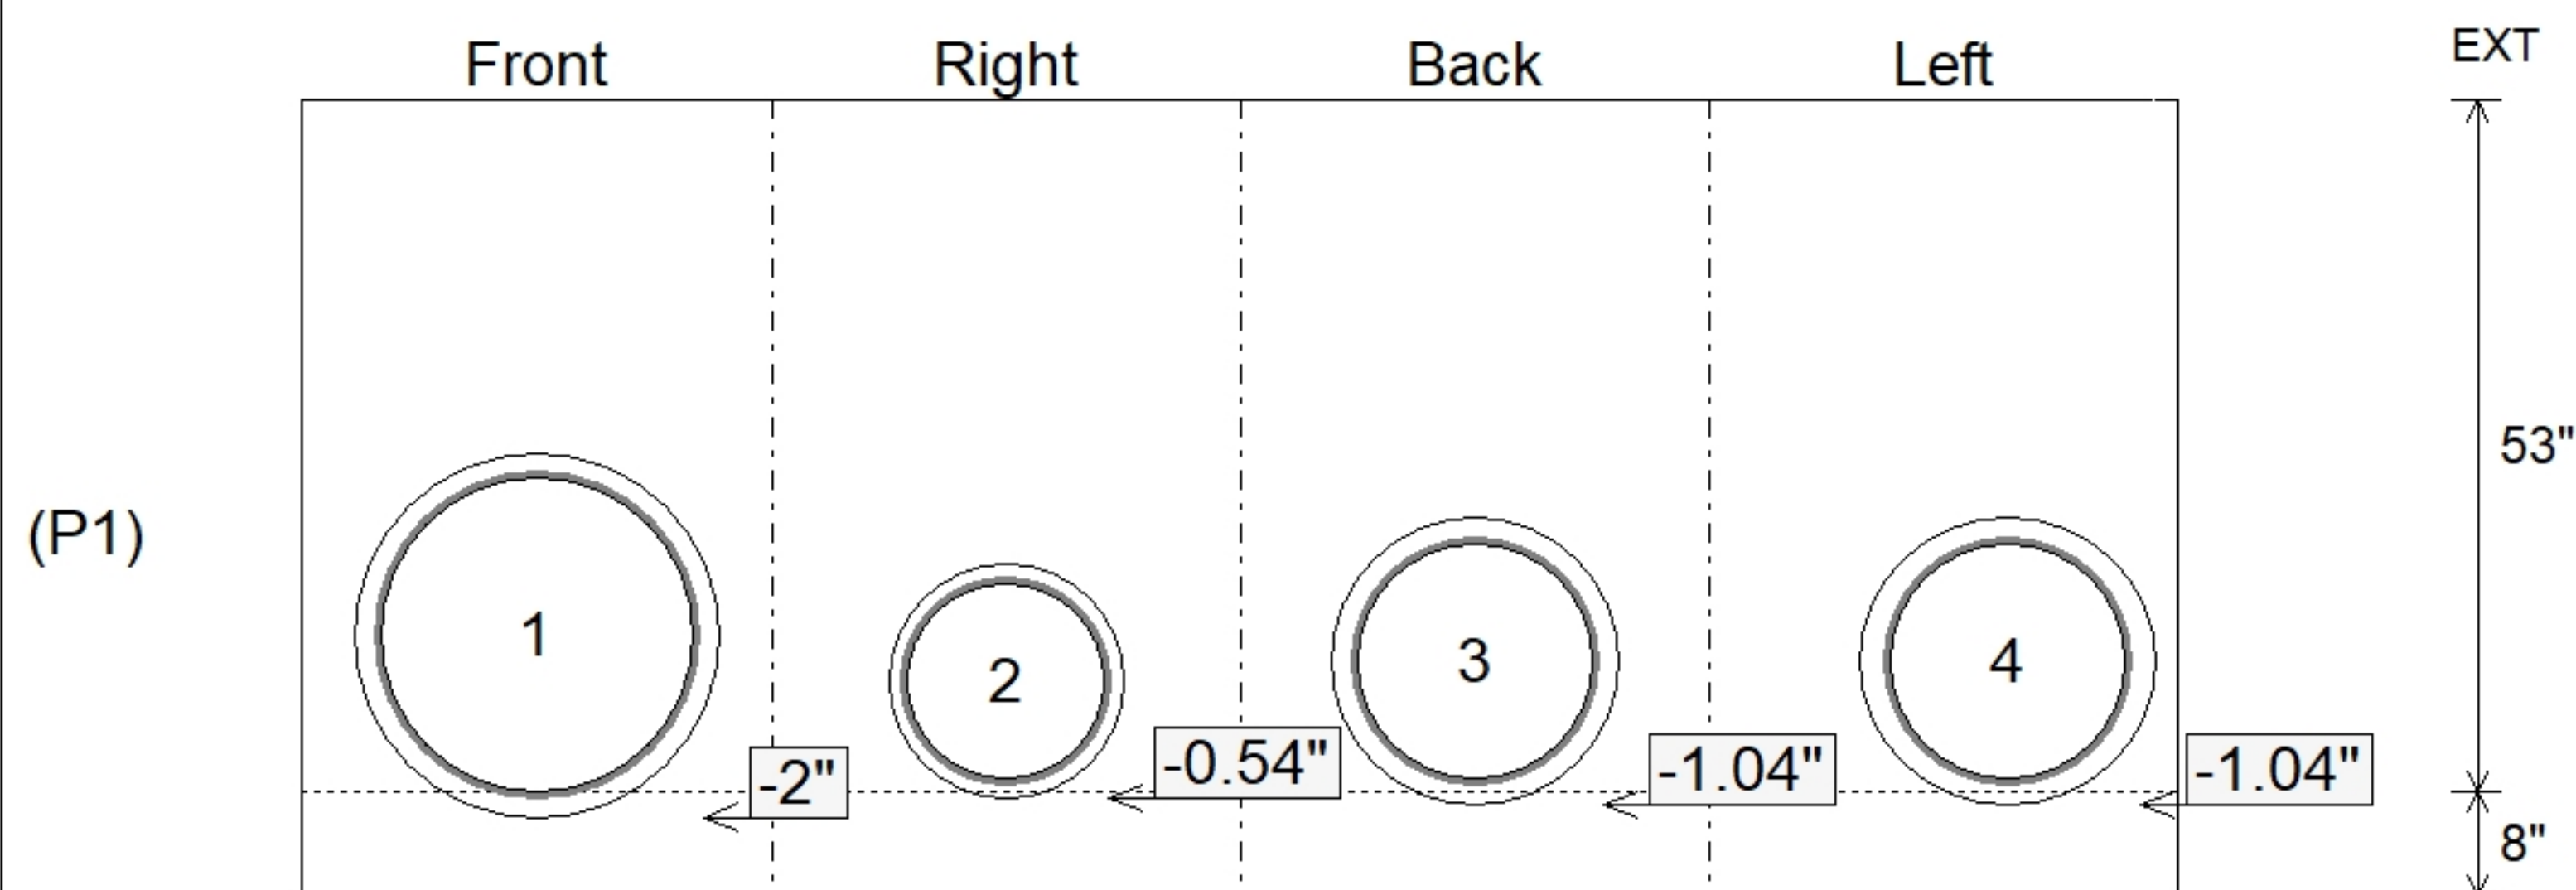

Submittal Drawing
8/27/2026 12:40:51 PM

SUBMITTAL
APPROVED BY:
