

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"

Rim to Invert: 7.67'


Floor Height: 8"

Slack: 3.04"


- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- TRANS. SLAB (As .62) #5 BARS AT 6" C.C.E.W (DBL MAT)
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P4) 24" x 120" - CB INLET KY A 10' TOP LEFT - 10"	3400 lb
P3) 24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18"	5270 lb
P2) 36" x 36" - CB TRANSITION SLAB 24"X36" HOLE - 8"	1235 lb
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 53"	6995 lb
1) CASTING - HOE KY-206 F/C (KY CBI A)	206 lb
1) 36" x 36" - Conseal CS-102 1.00"	0 lb
1) 24" x 36" - Conseal CS-102 1.00"	0 lb
2) Hole - 28	0 lb
1) Hole - 22	0 lb


Structure Total: 17106 lb

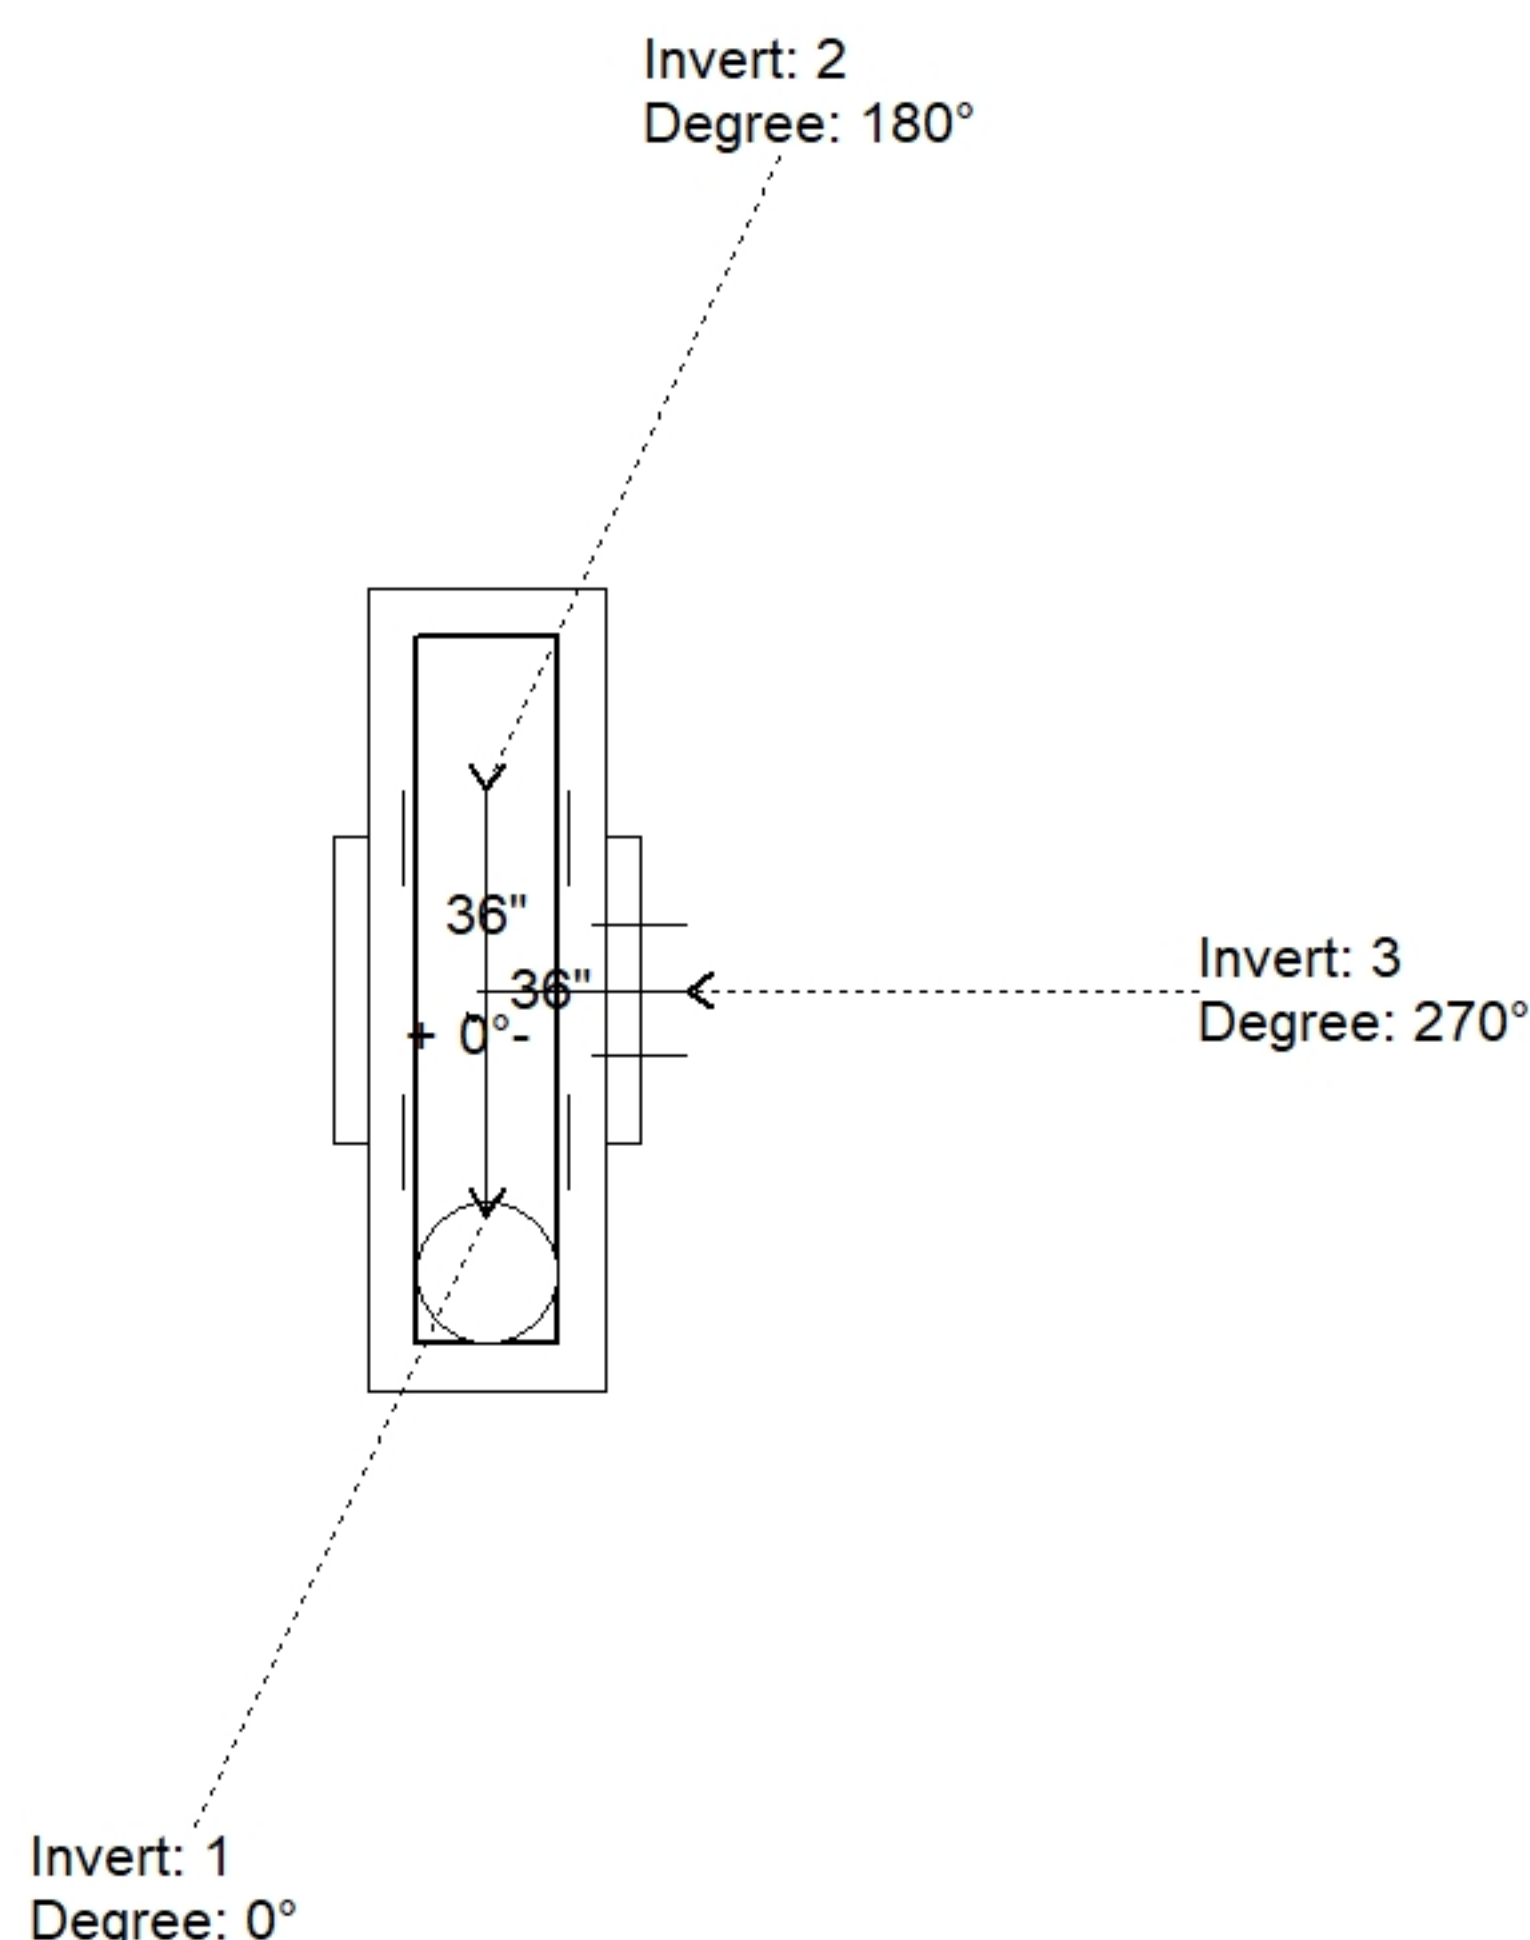

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	542.36'							
Reducer	539.107'							
Invert 1	534.69'	0°	24" CMP	25"	28"	Hole 28	-2"	P1
Invert 2	534.77'	180°	24" CMP	25"	28"	Hole 28	-1.04"	P1
Invert 3	534.77'	270°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

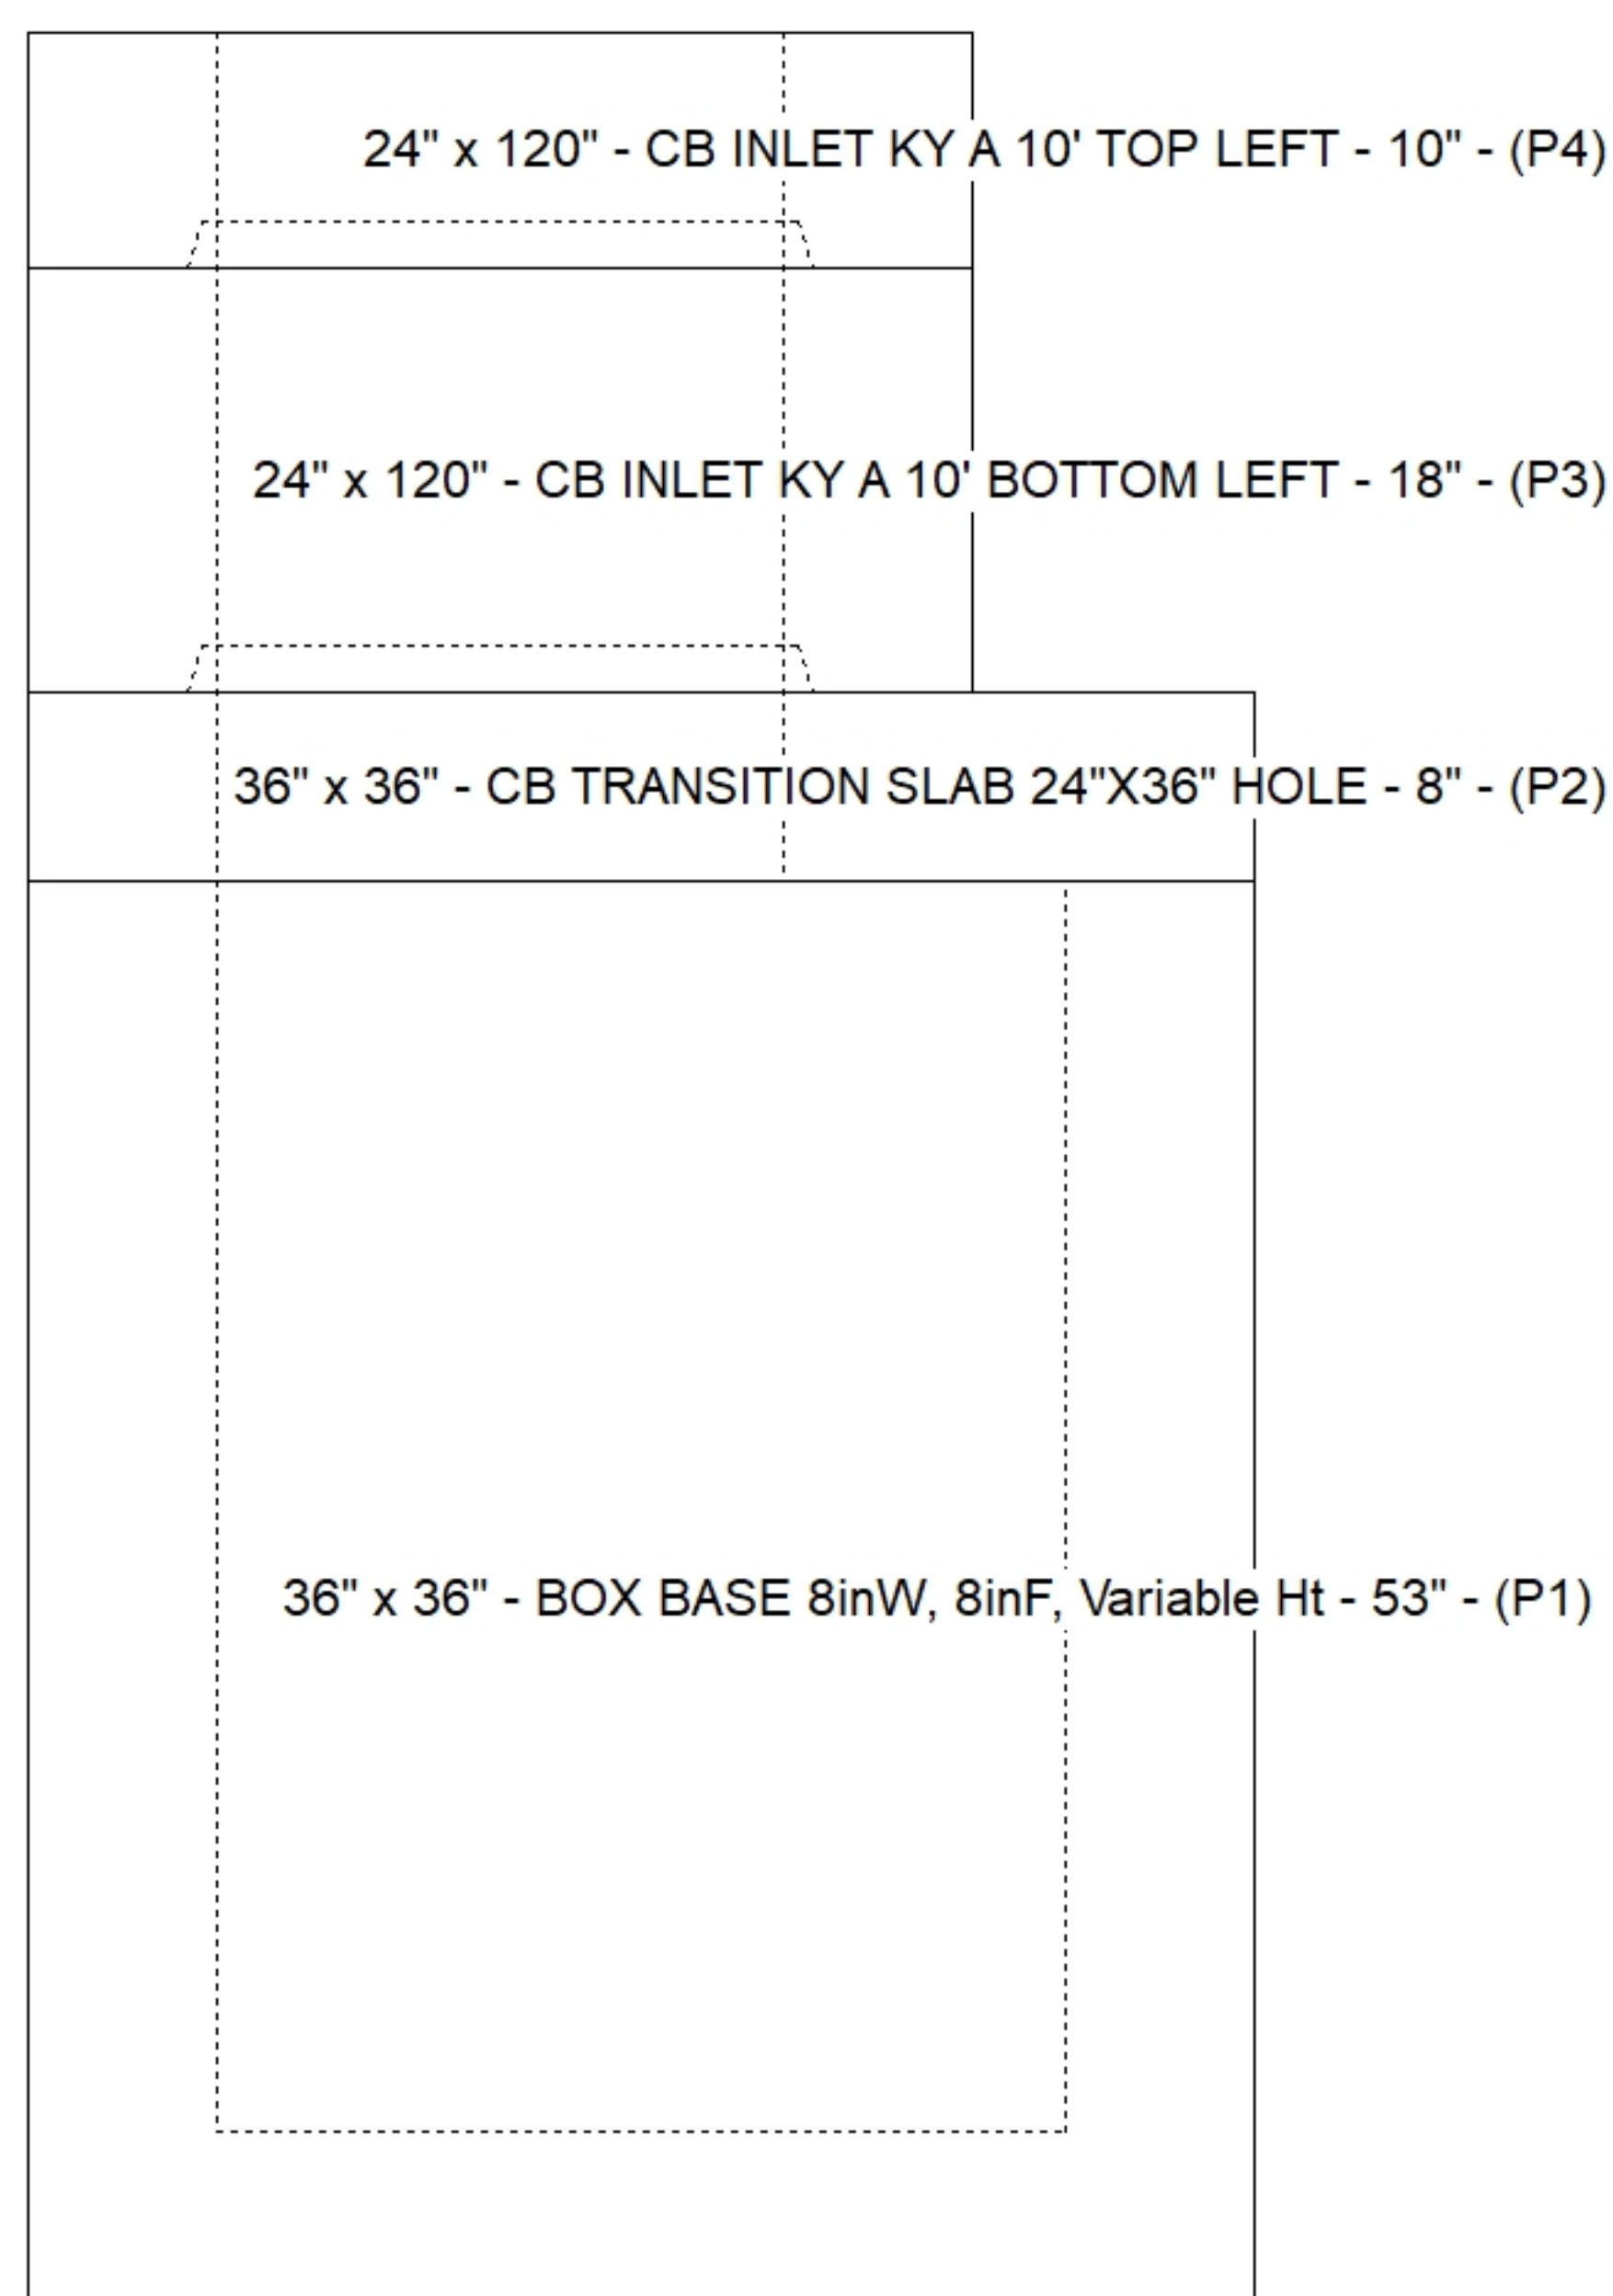

Default - Interior Dimensions

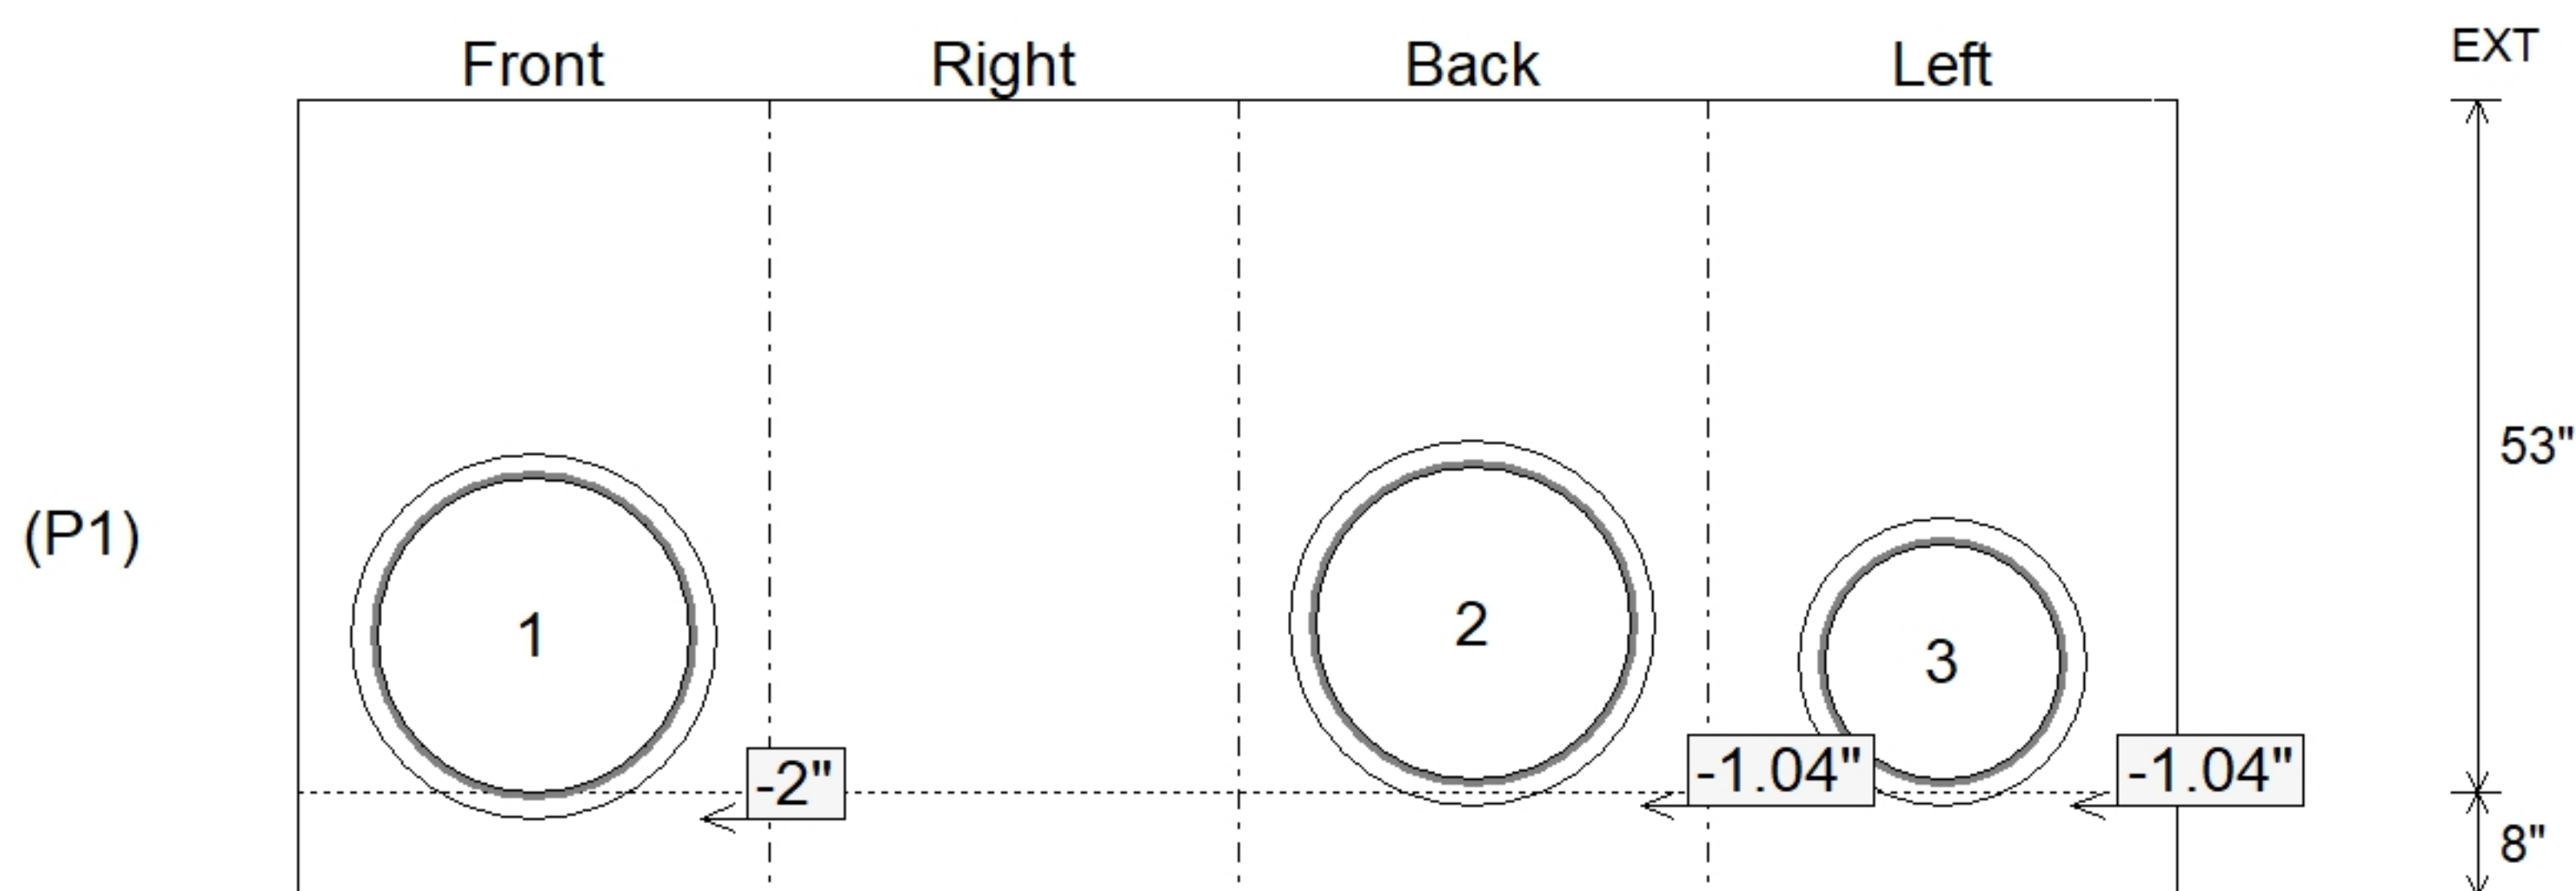

Submittal Drawing
8/27/2026 12:40:53 PM

SUBMITTAL
APPROVED BY:
