

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 5.17'


Floor Height: 8"

Slack: 3.04"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP PHASE (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 12925 lb

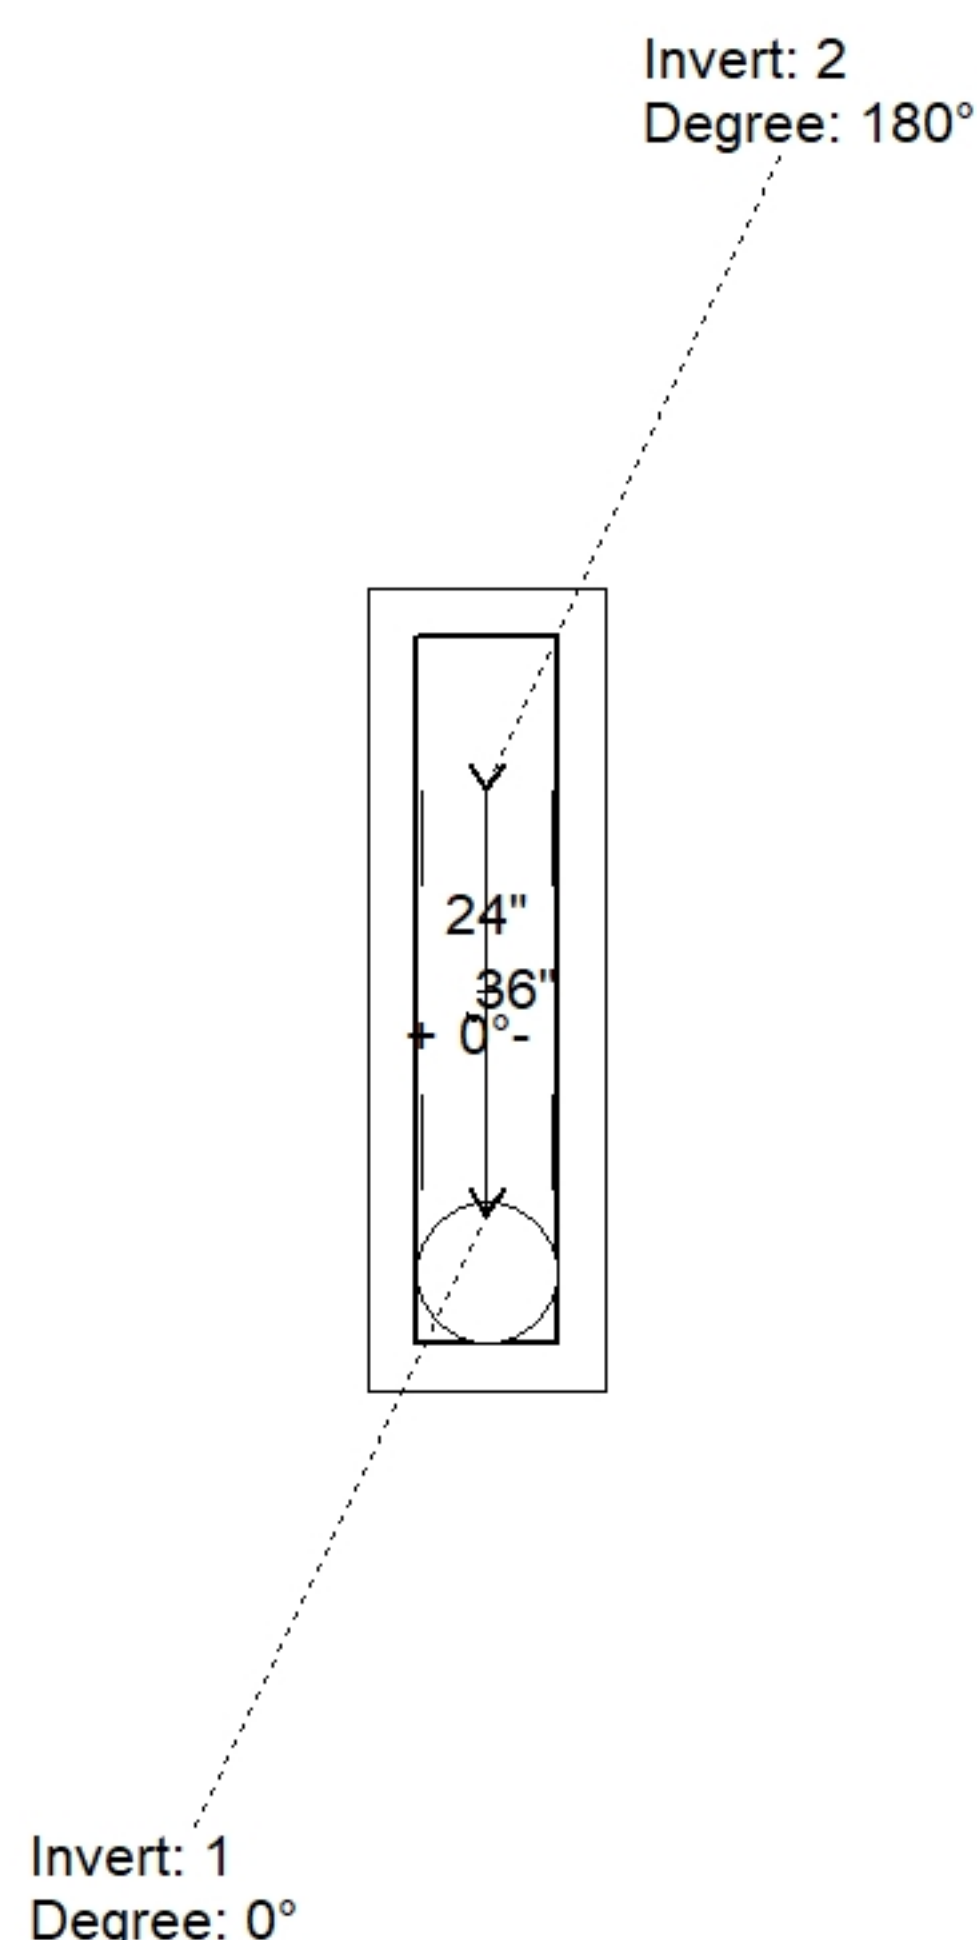


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (↓)	Ref
Rim	568.38'							
Reducer								
Invert 1	563.21'	0°	18" CMP	19"	22"	Hole 22	-2"	P1
Invert 2	563.29'	180°	18" CMP	19"	22"	Hole 22	-1.04"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 120" - CB INLET KY A 10' TOP LEFT - 10" - (P3)

24" x 120" - CB INLET KY A 10' BOTTOM LEFT - 18" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 31" - (P1)

Default - Interior Dimensions

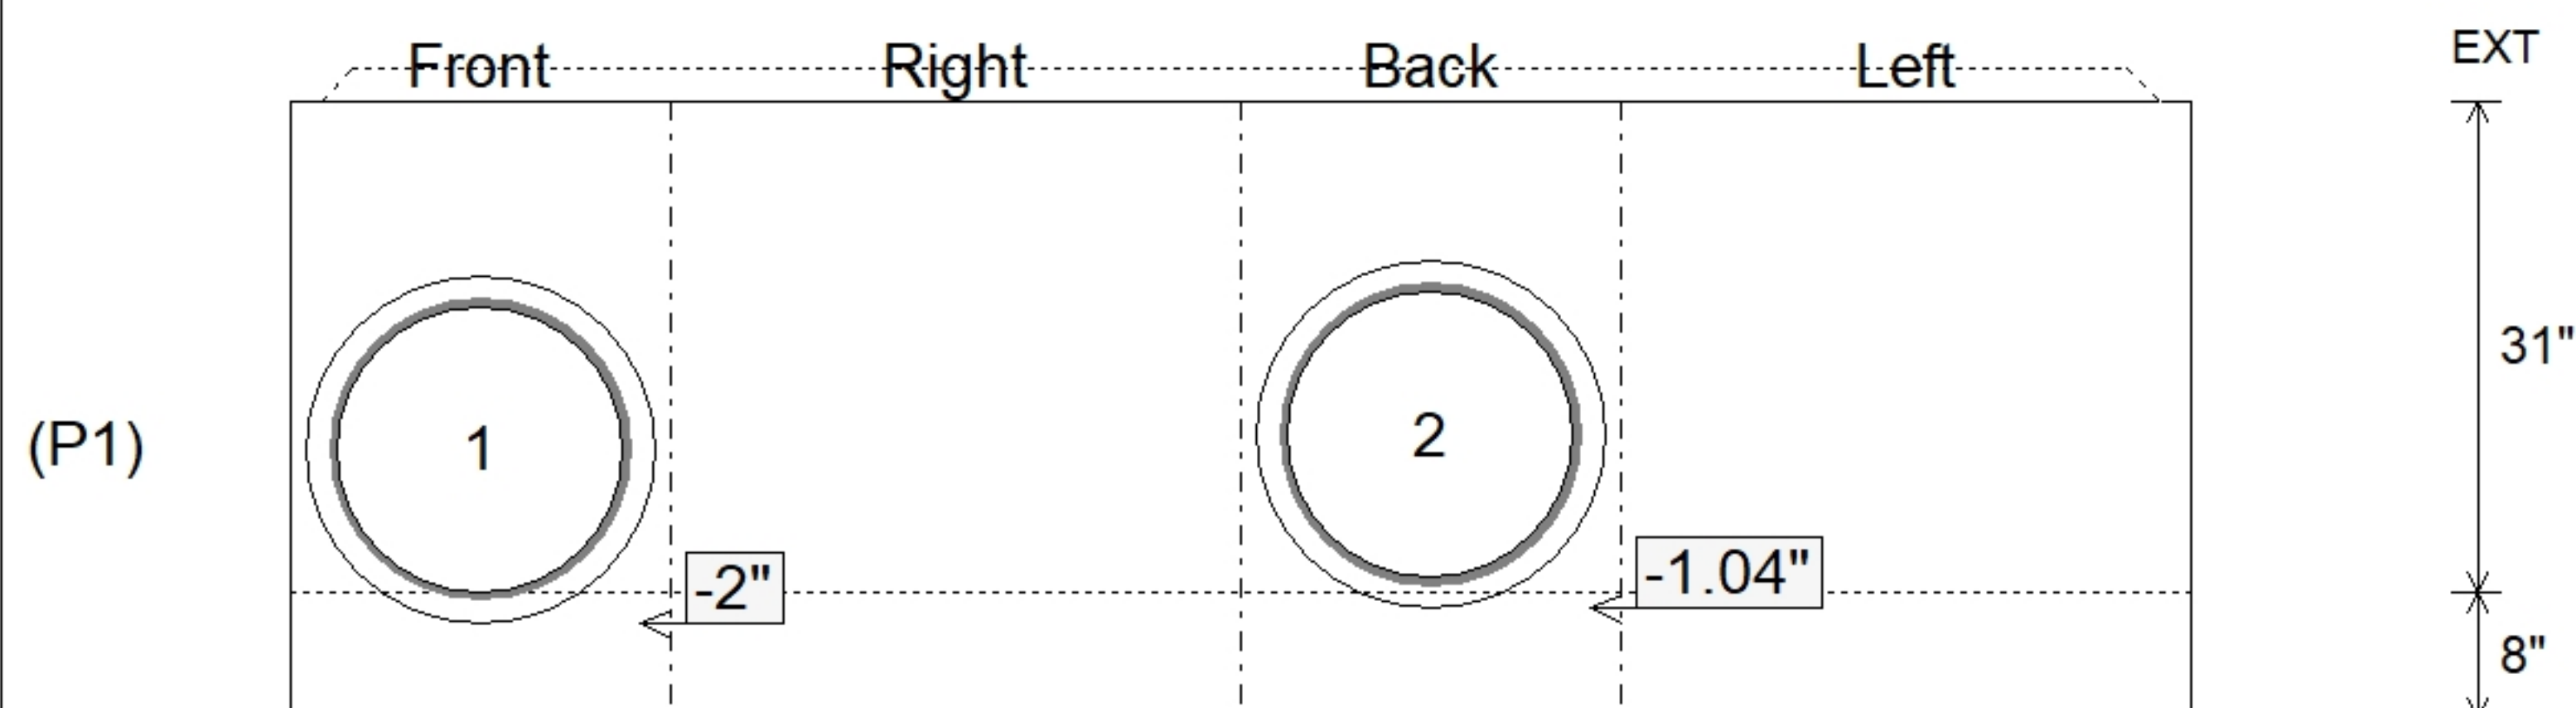

Submittal Drawing
8/27/2026 12:40:47 PM

SUBMITTAL
APPROVED BY:
