

Contractor: Mick-Murf Construction Inc.

TECH: Jared - F

Plant: 100



Size: 36" x 36"

Rim to Invert: 3'

Floor Height: 8"


Slack: 1"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W

P2) 36" x 36" - P.I.P. - BY OTHERS - 8"
P1) 36" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 27"
1) CASTING - HOE KY-328 SET (DBI 3)
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 18



0 lb
4834 lb
328 lb
0 lb
0 lb

Structure Total: 5162 lb

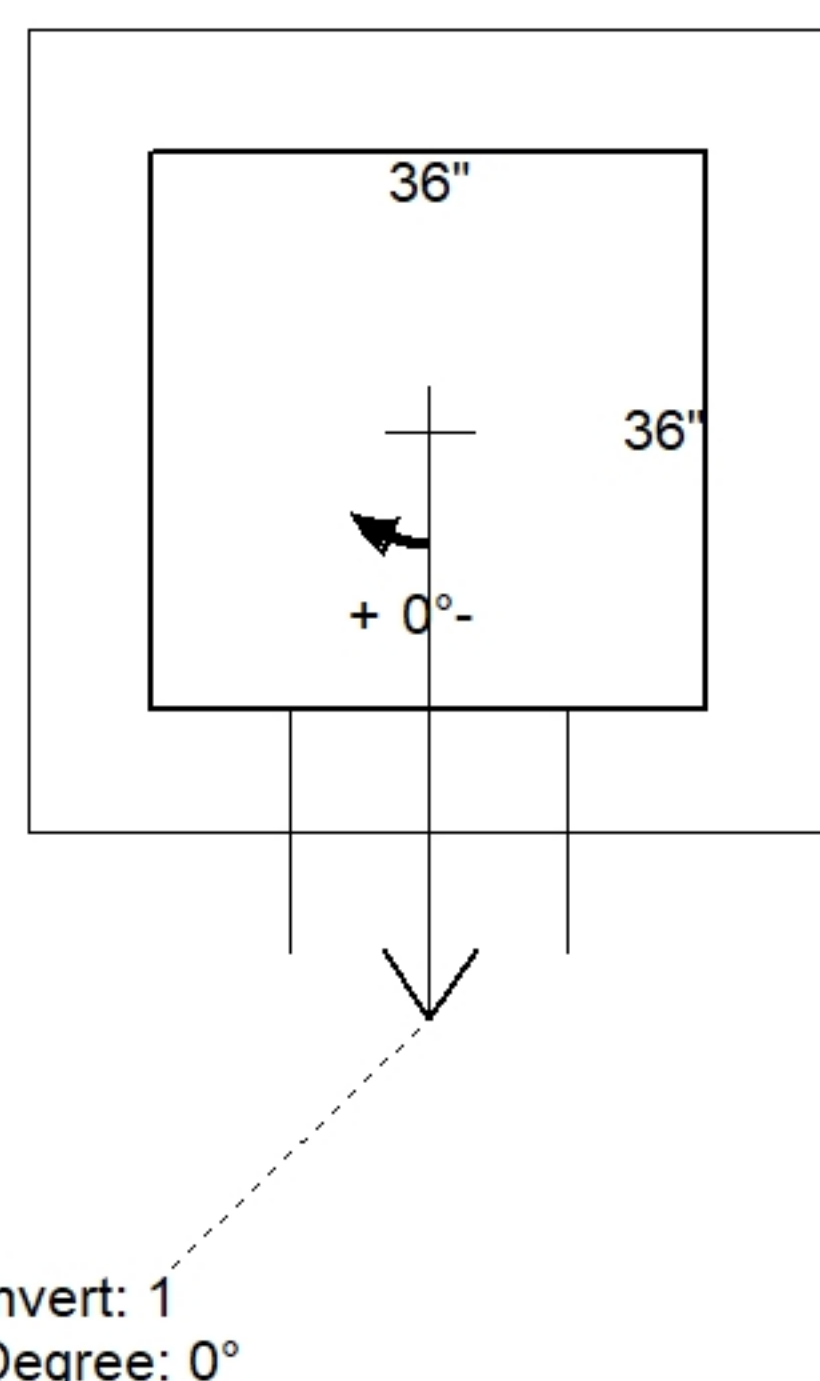

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	566'							
Reducer								
Invert 1	563'	0°	15" CMP	16"	18"	Hole 18	-1.5"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

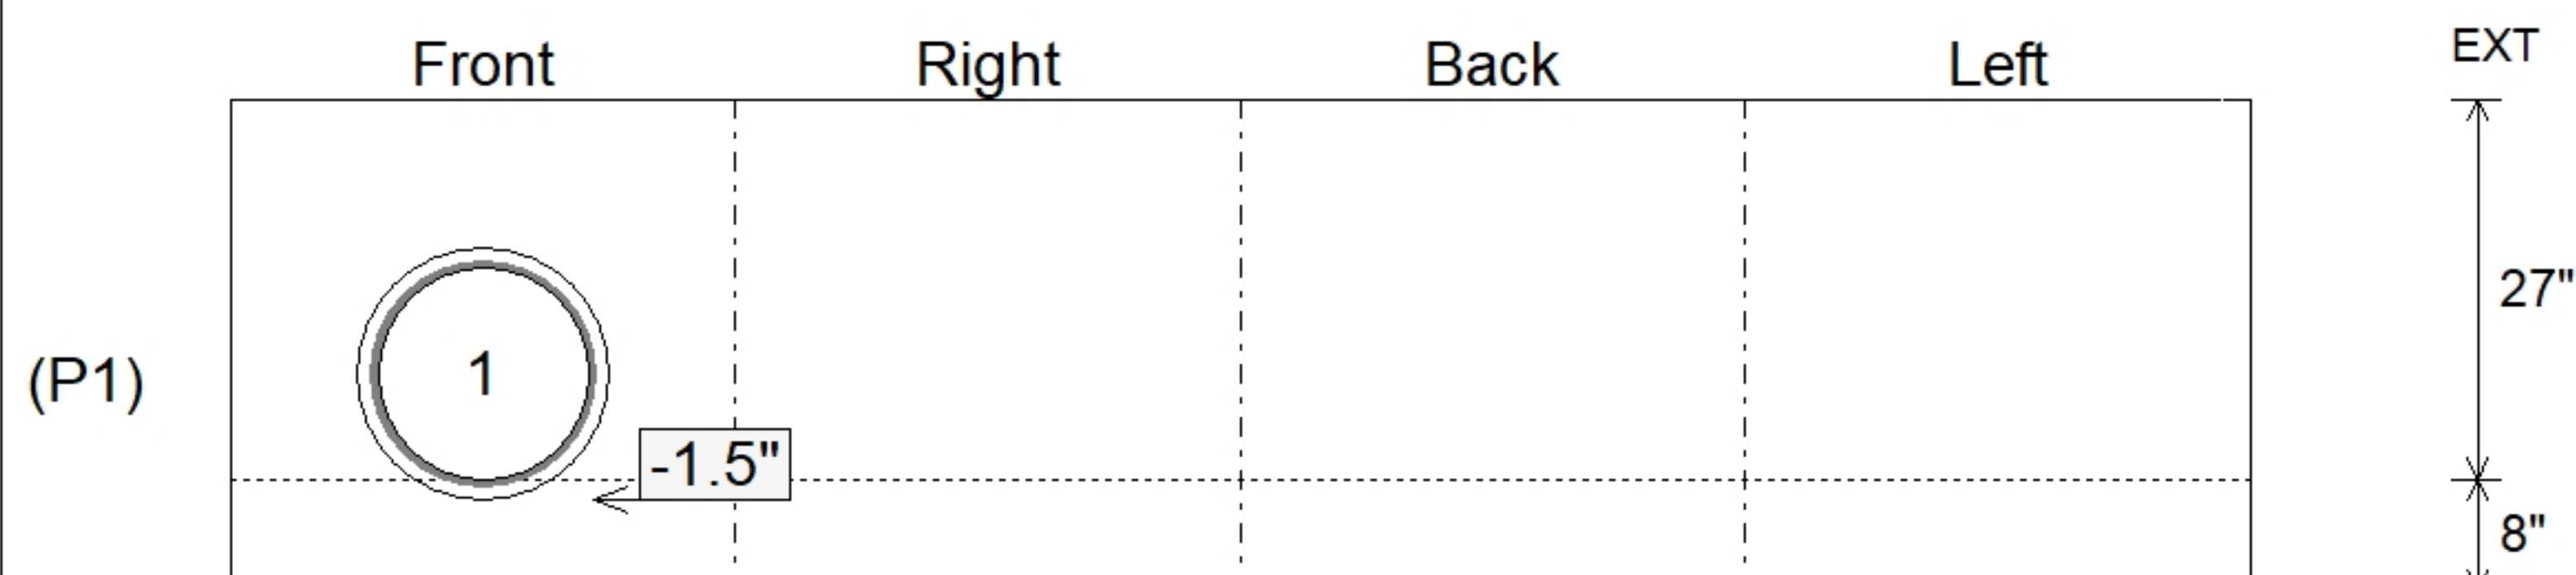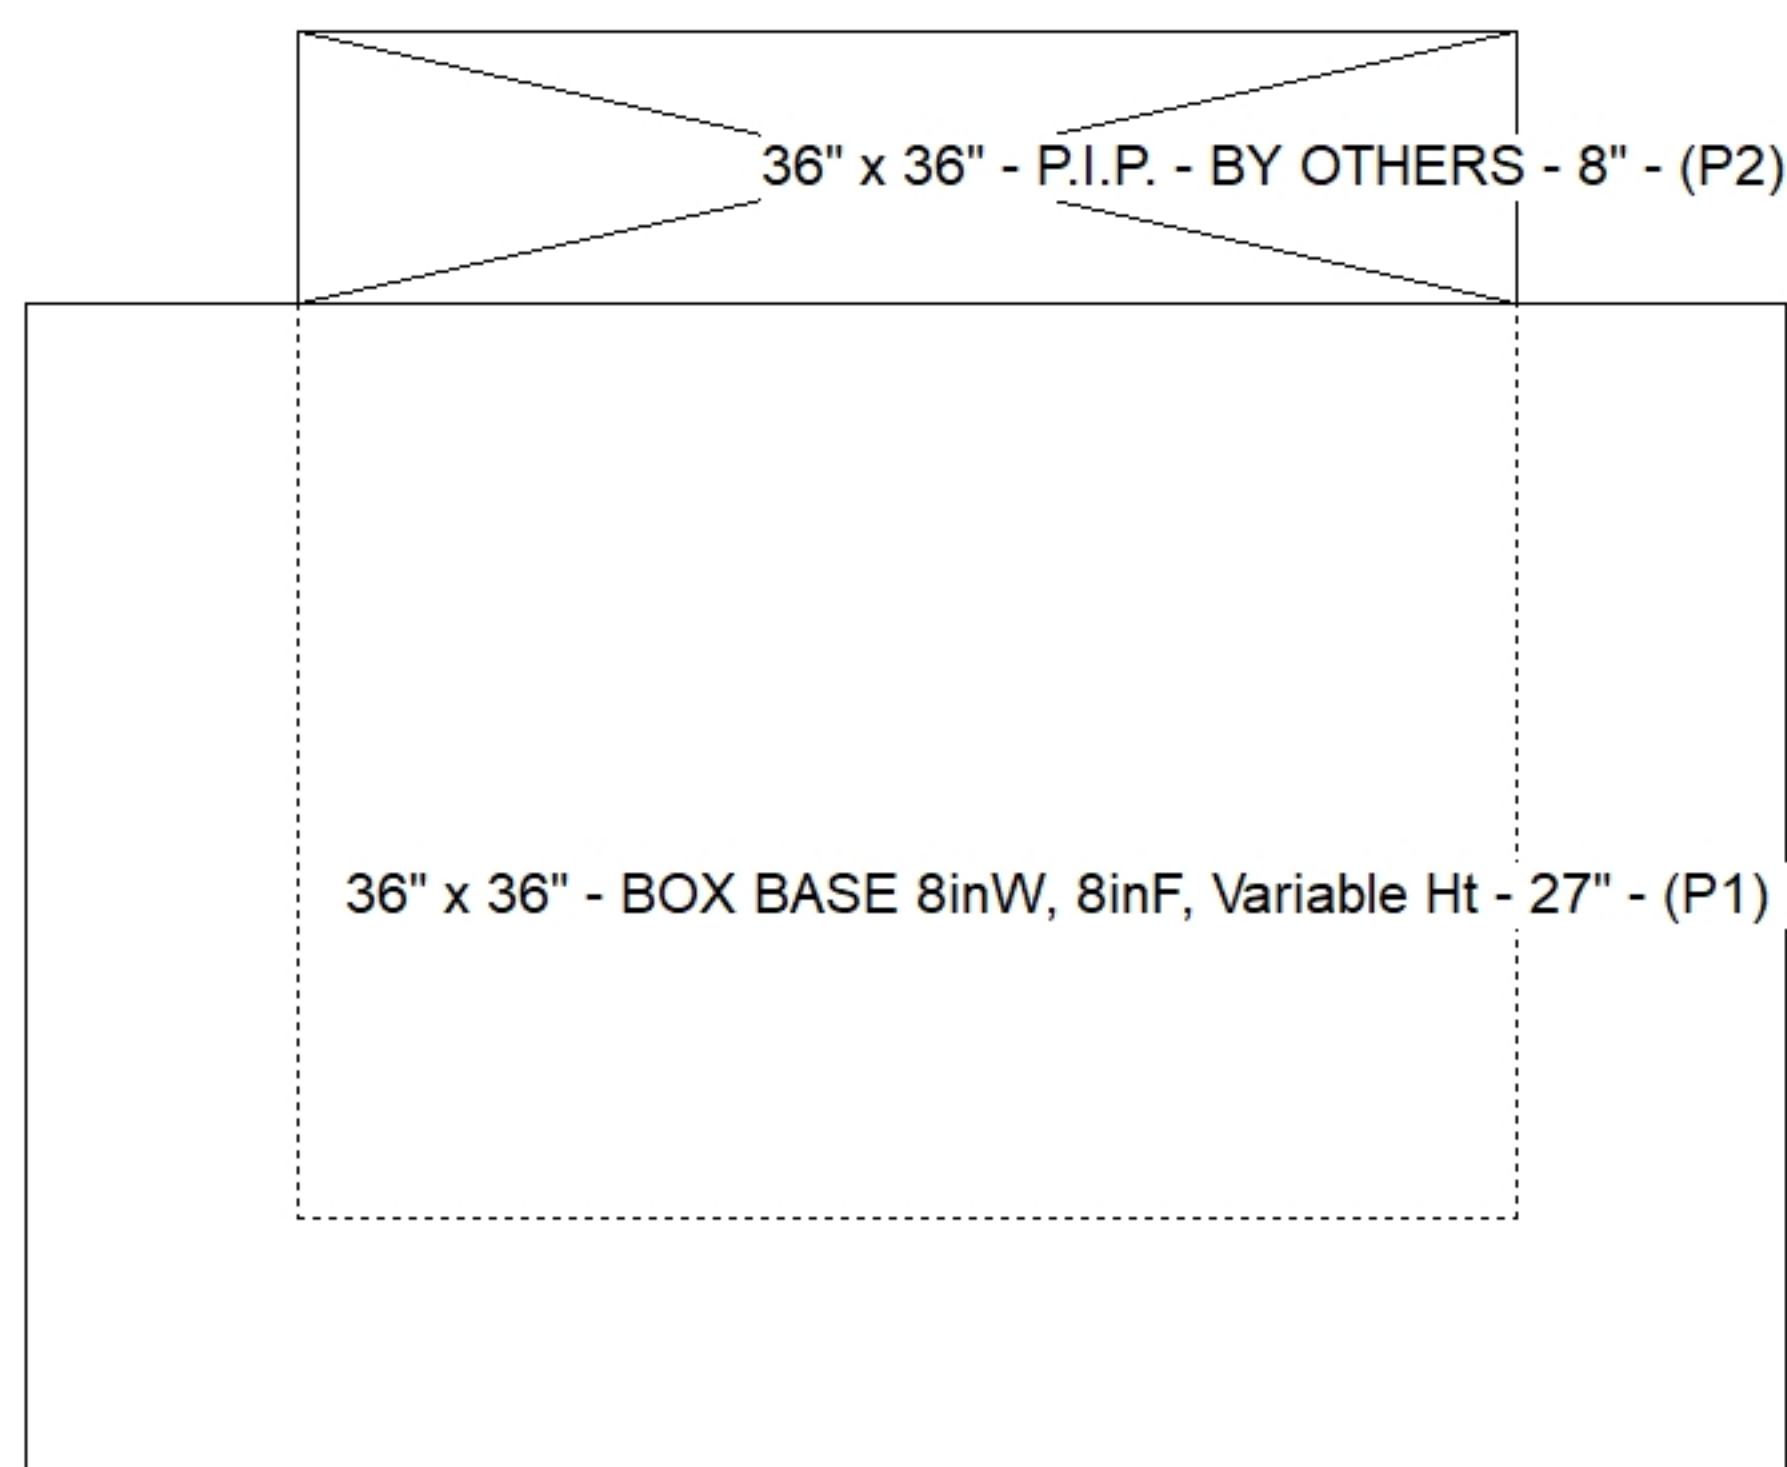

Submittal Drawing
8/27/2026 12:40:54 PM

SUBMITTAL
APPROVED BY:
