




Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 31"	Weight (Net): 3401 lb
Coating (Ext):	Seam Dn: n/a	Floor Height: 6"	Height (Ext): 37"	Volume (Net): 0.87cu.yd

Job Name: 26-2080 - The Cumberland Job Location: Bowling Green, KY Contractor: J & J Concrete & Excavating, LLC					Plant: 100 6/22/2026 6:23:31 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: A2 SS-MH											
P1		MH048BAVF		MH BASE Custom Ht T/n							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 24" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE Custom Ht T/n - 31" 2) JOINT WRAP - 12" WD x 048" MAC WRAP 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) A-Lok - 0285 7) MH Step ML-10-TDS-NCR - 10"					0 lb 1550 lb 2515 lb 3401 lb 0 lb 1440 lb 271 lb 0 lb 0 lb 0 lb 3 lb 0 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. INVERT CHANNEL REQUIRED 5. STEPS AT 0 DEGREES 6. HOE MC-375 FRAME & COVER "SANITARY" SUPPLIED BY ICAST				
Structure Total:					9180 lb						
Rim: 531.37' Rim to Invert: 8.2' Slack: 2.4" Sump: 2" Step Position: 0°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	523.17'	0°	0"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	1.125"	0"	
Invert 2	523.27'	150°	75.875"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	2.375"	0"	
Invert 3	523.27'	270°	136.625"	8" PVC SDR35	8.5"	A-Lok 0285	9.75"	9.818"	2.375"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

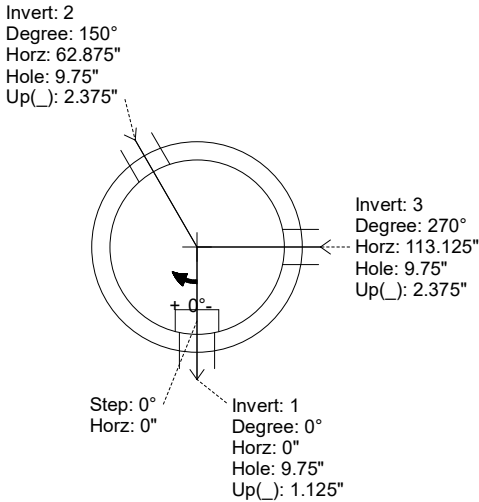

UPSIDE-DOWN VIEW (int. dimensions)

INVERT CHANNEL DRAWING

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 31" Height (Ext): 37"	Weight (Net): 3401 lb Volume (Net): 0.87cu.yd
----------------------------------	---------------------------------	--	--	--
