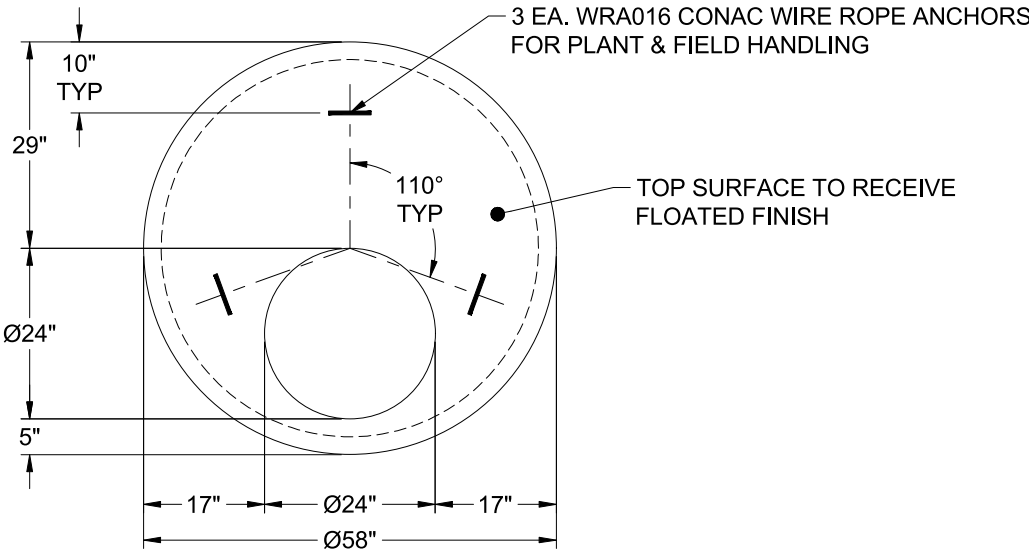



Job Name: 26-2104 - Jeffersonville High School Parking Lot		Plant: 100	Tech: Jared - A	
Job Location: Jeffersonville, IN		6/27/2026 7:13:17 PM	PC: T. Lewis	
Contractor: Mac Construction & Excavating, Inc.				
Structure ID: 20 ST-MH				
P2 MH048LD12ECC		MH FLAT TOP w/ 24" ECC Hole F/G		
P4) 24" - CASTING HEIGHT - 4" P3) 24" - GRADE RING F/F - 4" P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12" P1) 48" - MH BASE T/n - 42" 1) 48" - Conseal CS-102 1.00" 2) 24" - Conseal CS-102 1.00" 2) Hole - 32 3) MH Step ML-10-TDS-NCR - 10"		0 lb 270 lb 1561 lb 3537 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 5368 lb Structure Total: 5368 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: #4 BAR @ 10" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. HOE MC-285 FRAME & COVER "STORM" SUPPLIED BY OTHERS 5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS FOR PLANT & FIELD HANDLING 6. TOP SURFACE TO RECEIVE FLOATED FINISH	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 12"	Weight (Net): 1561 lb Volume (Net): 0.42cu.yd
