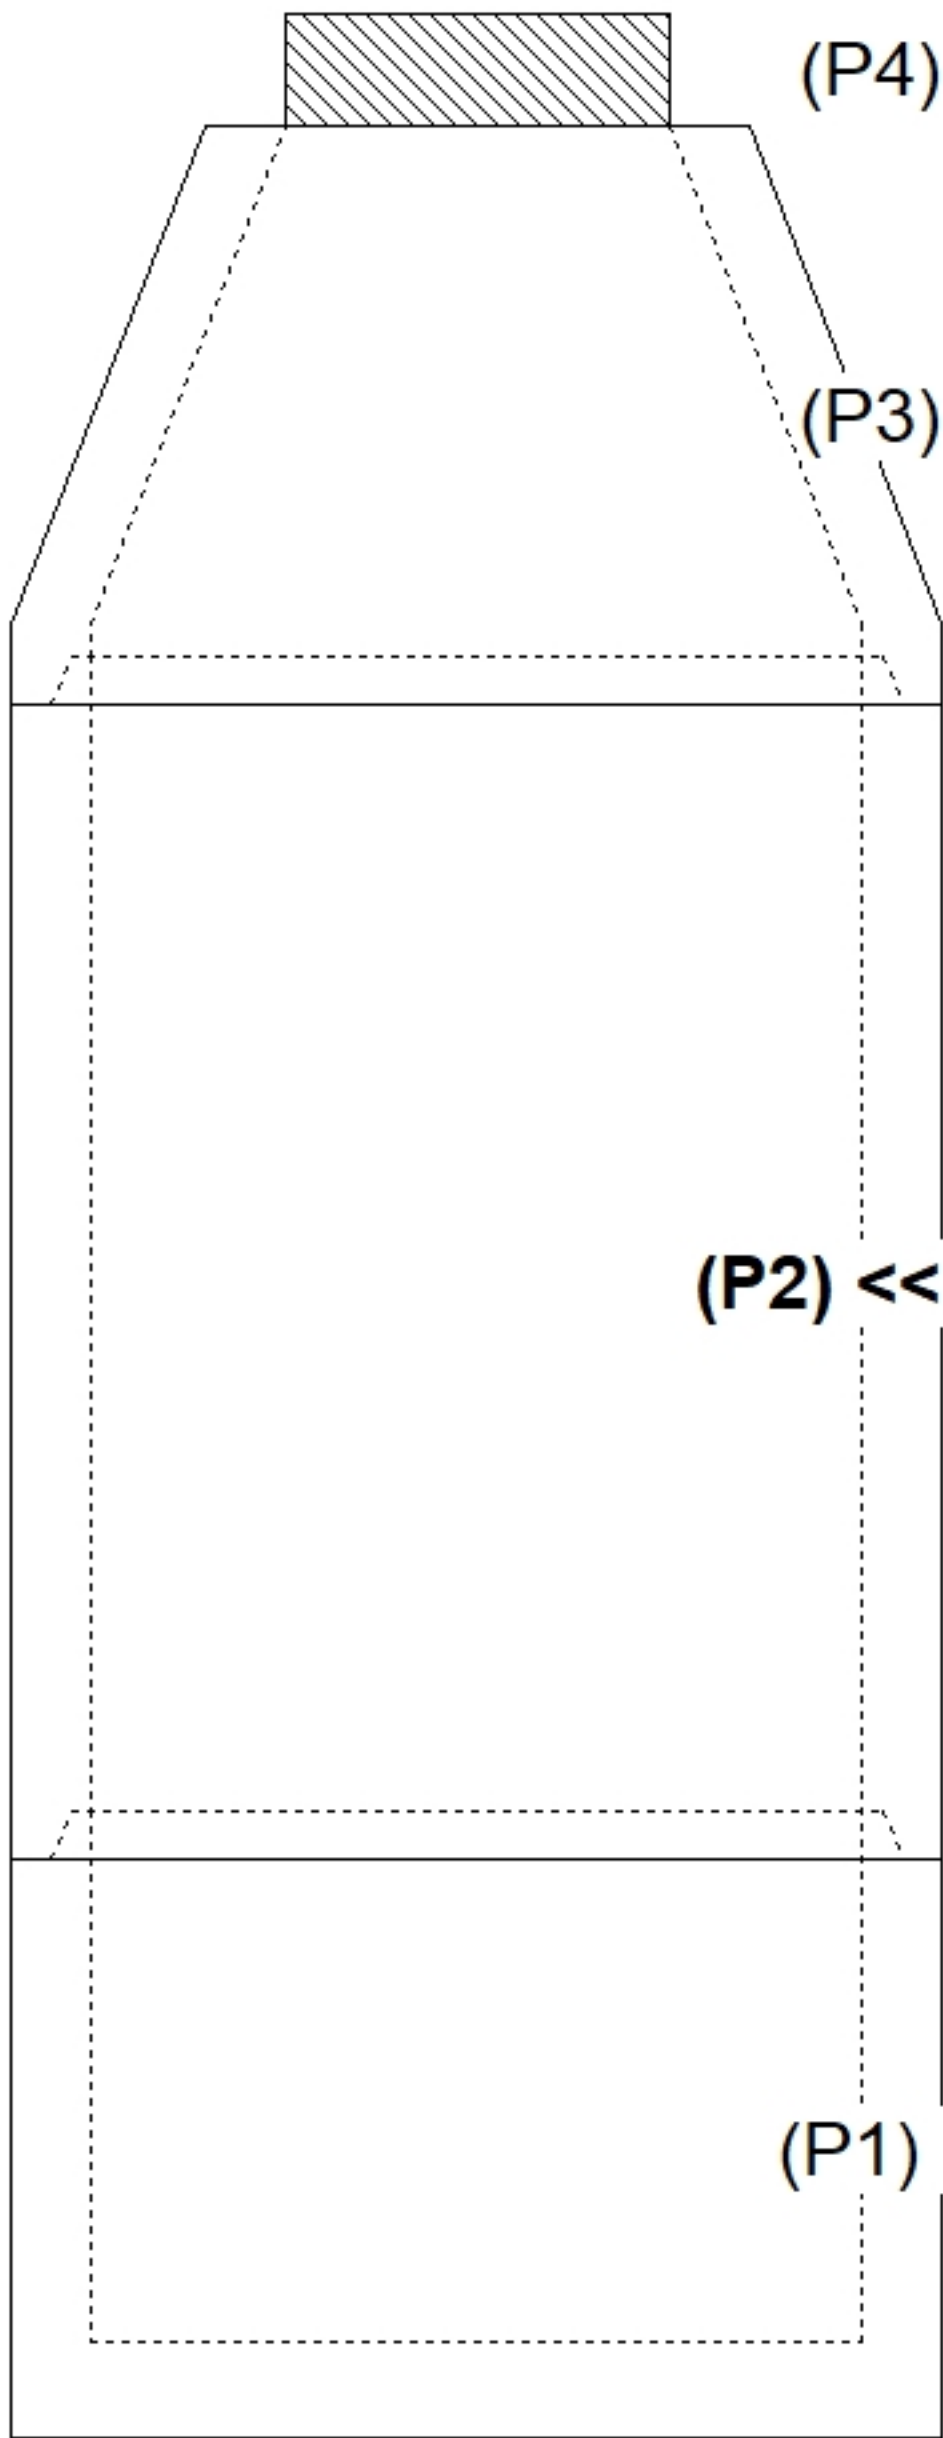
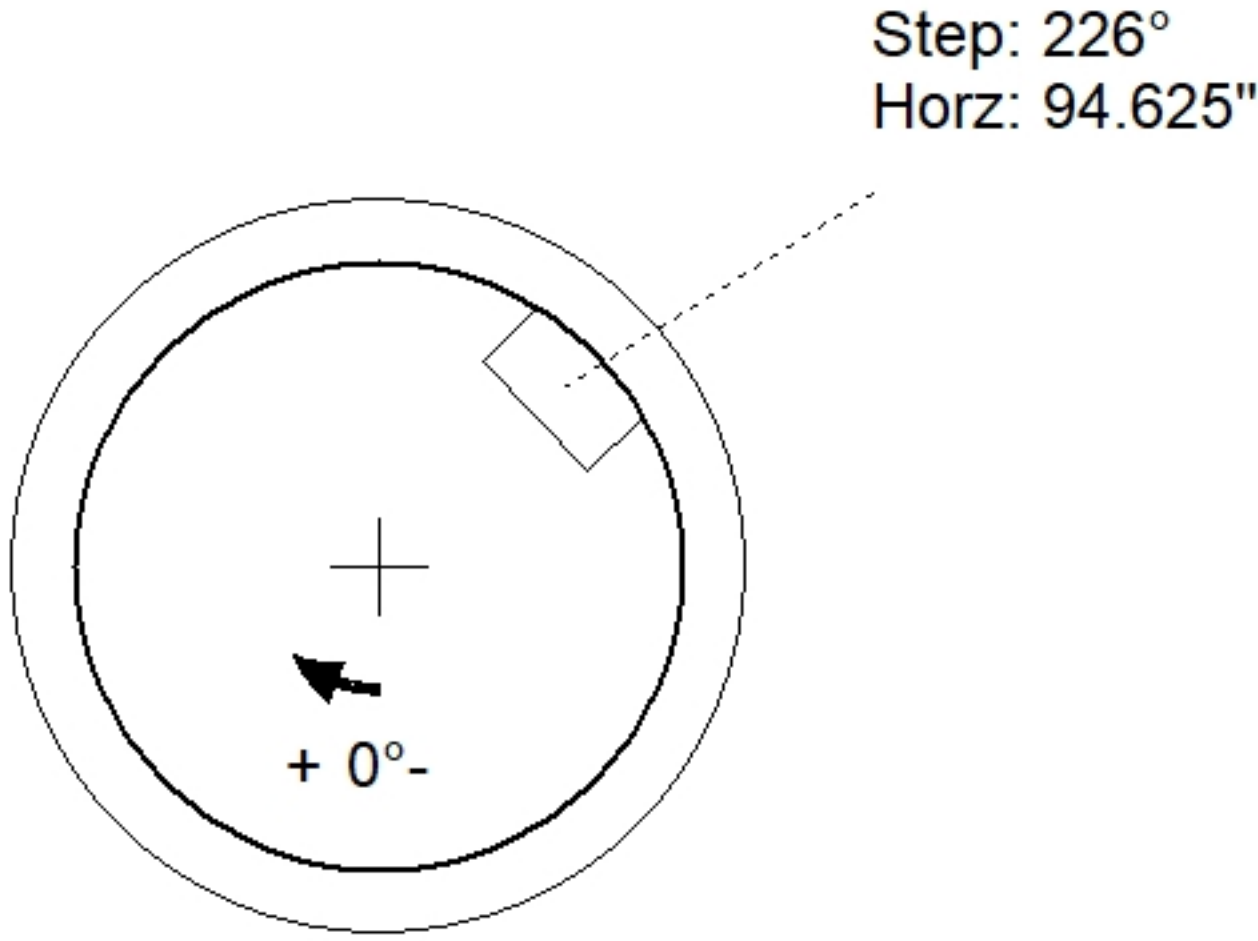
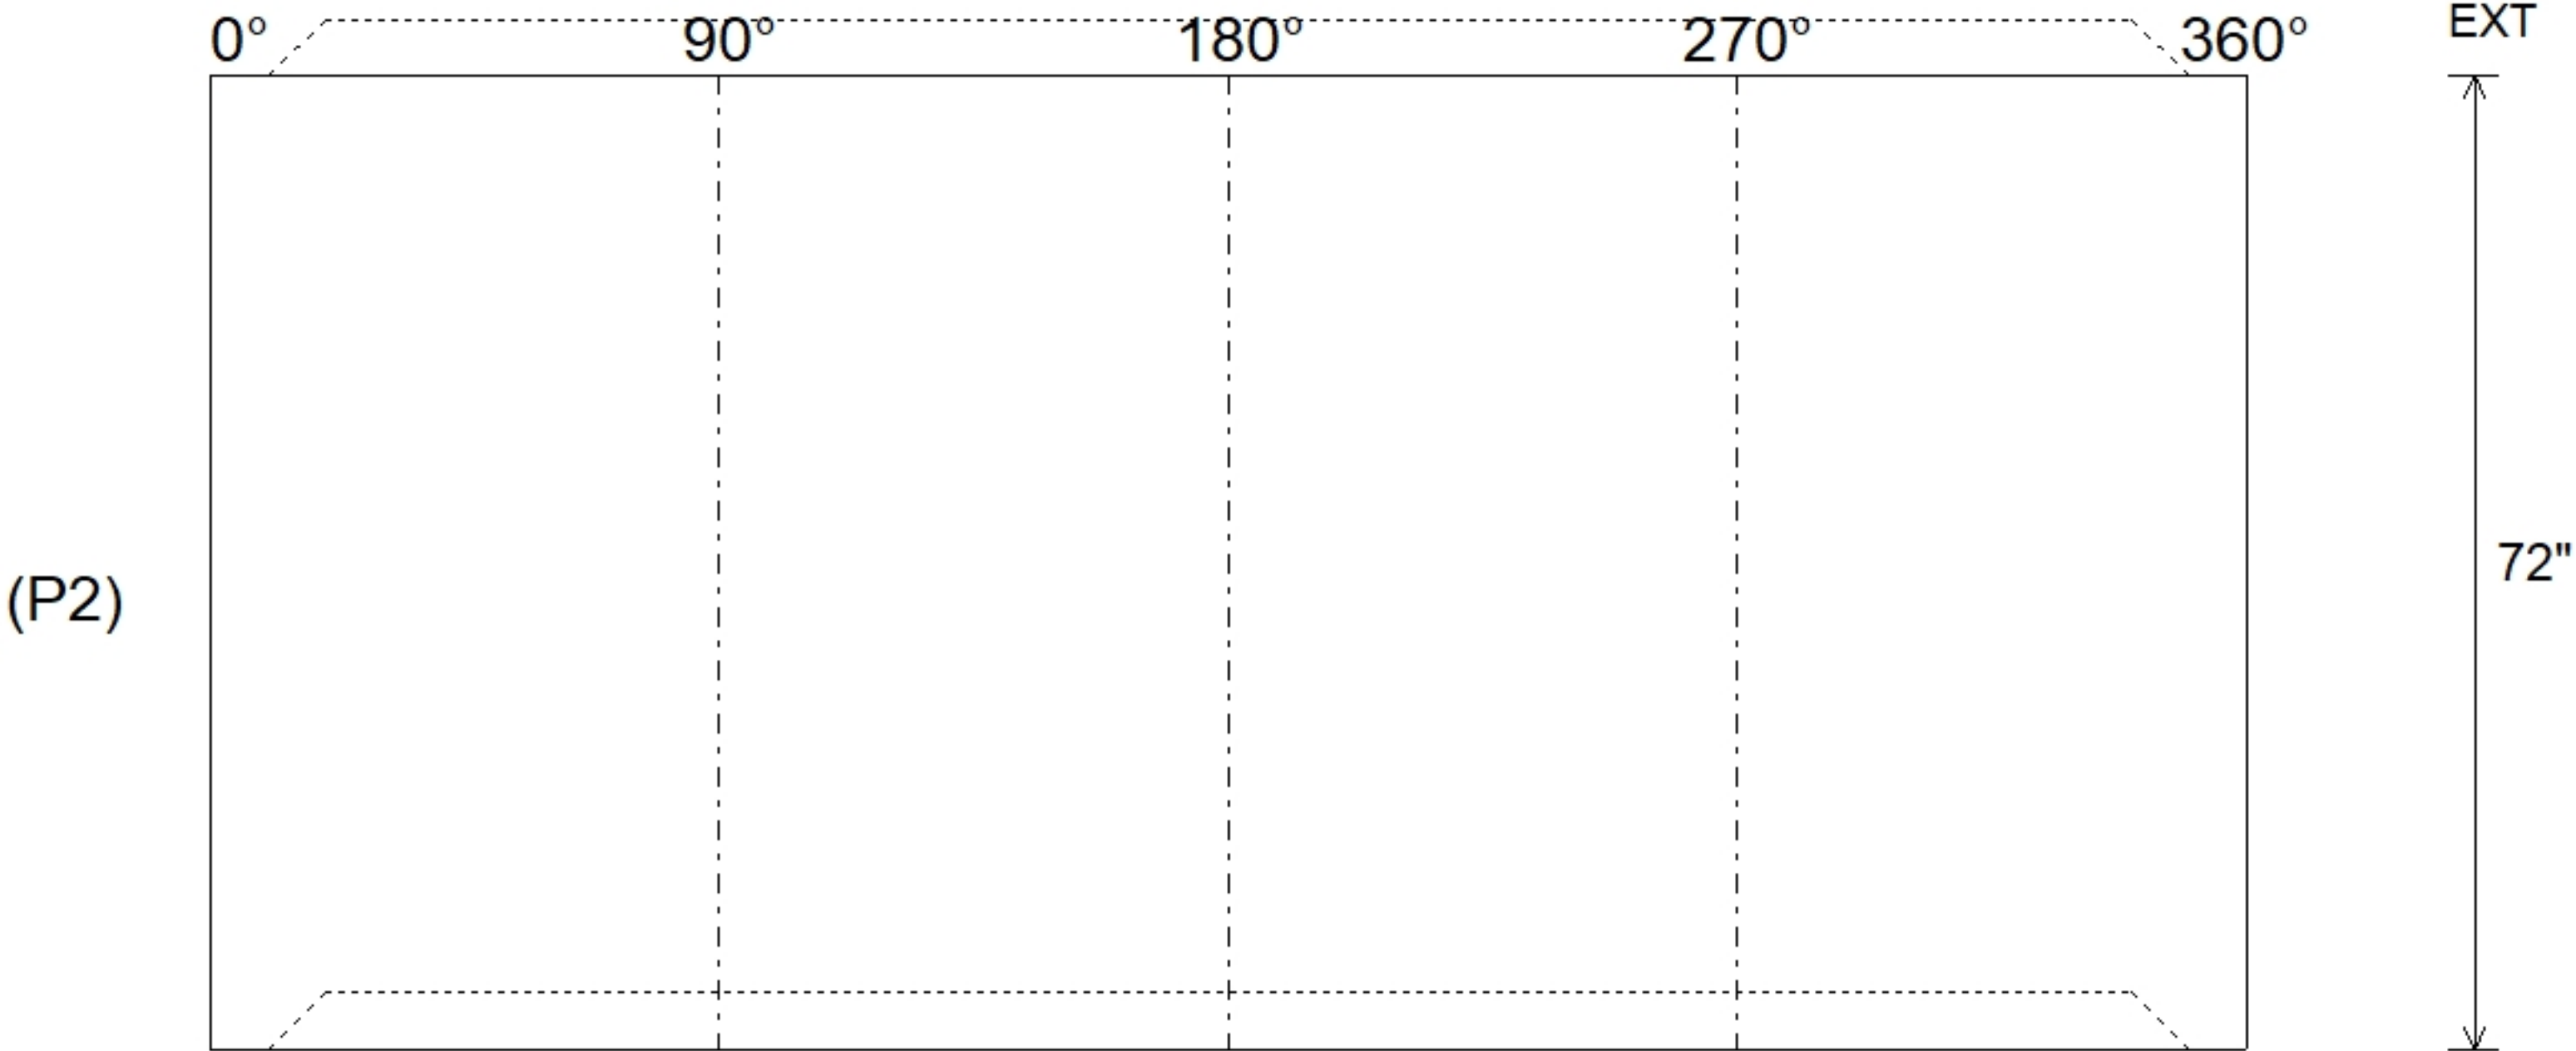


Job Name: 26-2117 - The Preserve at Priest Lake Job Location: Nashville, TN Contractor: Bear Construction LLC					Plant: 100 8/27/2026 2:55:52 PM		Tech: J. Horsley PC: T. Ryan						
Structure ID: 8 SS-MH													
P2			MH048RS72CDARED			MH RISER w/ConBlock-CDA Red T/G							
P4) 24" - CASTING HEIGHT - 7" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 36" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 72" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) CASTING - JBS 1150 F/C PLAIN 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 8) MH Step ML-10-TDS-NCR - 10"						0 lb 2251 lb 5030 lb 3330 lb 0 lb 0 lb 1440 lb 250 lb 0 lb 16 lb 0 lb ----- 12317 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING BY ICAST (JBS 1150 F/C) . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 537.29' Rim to Invert: 11.99' Slack: 0.884" Sump: 2.004" Step Position: 226°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset			
Invert 1													
Invert 2													
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													
RIGHT-SIDE UP VIEW (int. dimensions)													
													
INSIDE WALL DIMENSIONS													
													
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 72" Height (Ext): 72"		Weight (Net): 5030 lb Volume (Net): 1.28cu.yd			
