


Contractor: Bear Construction LLC

Plant: 100



Slack: 0.596"


Structure Total: 3636 lb

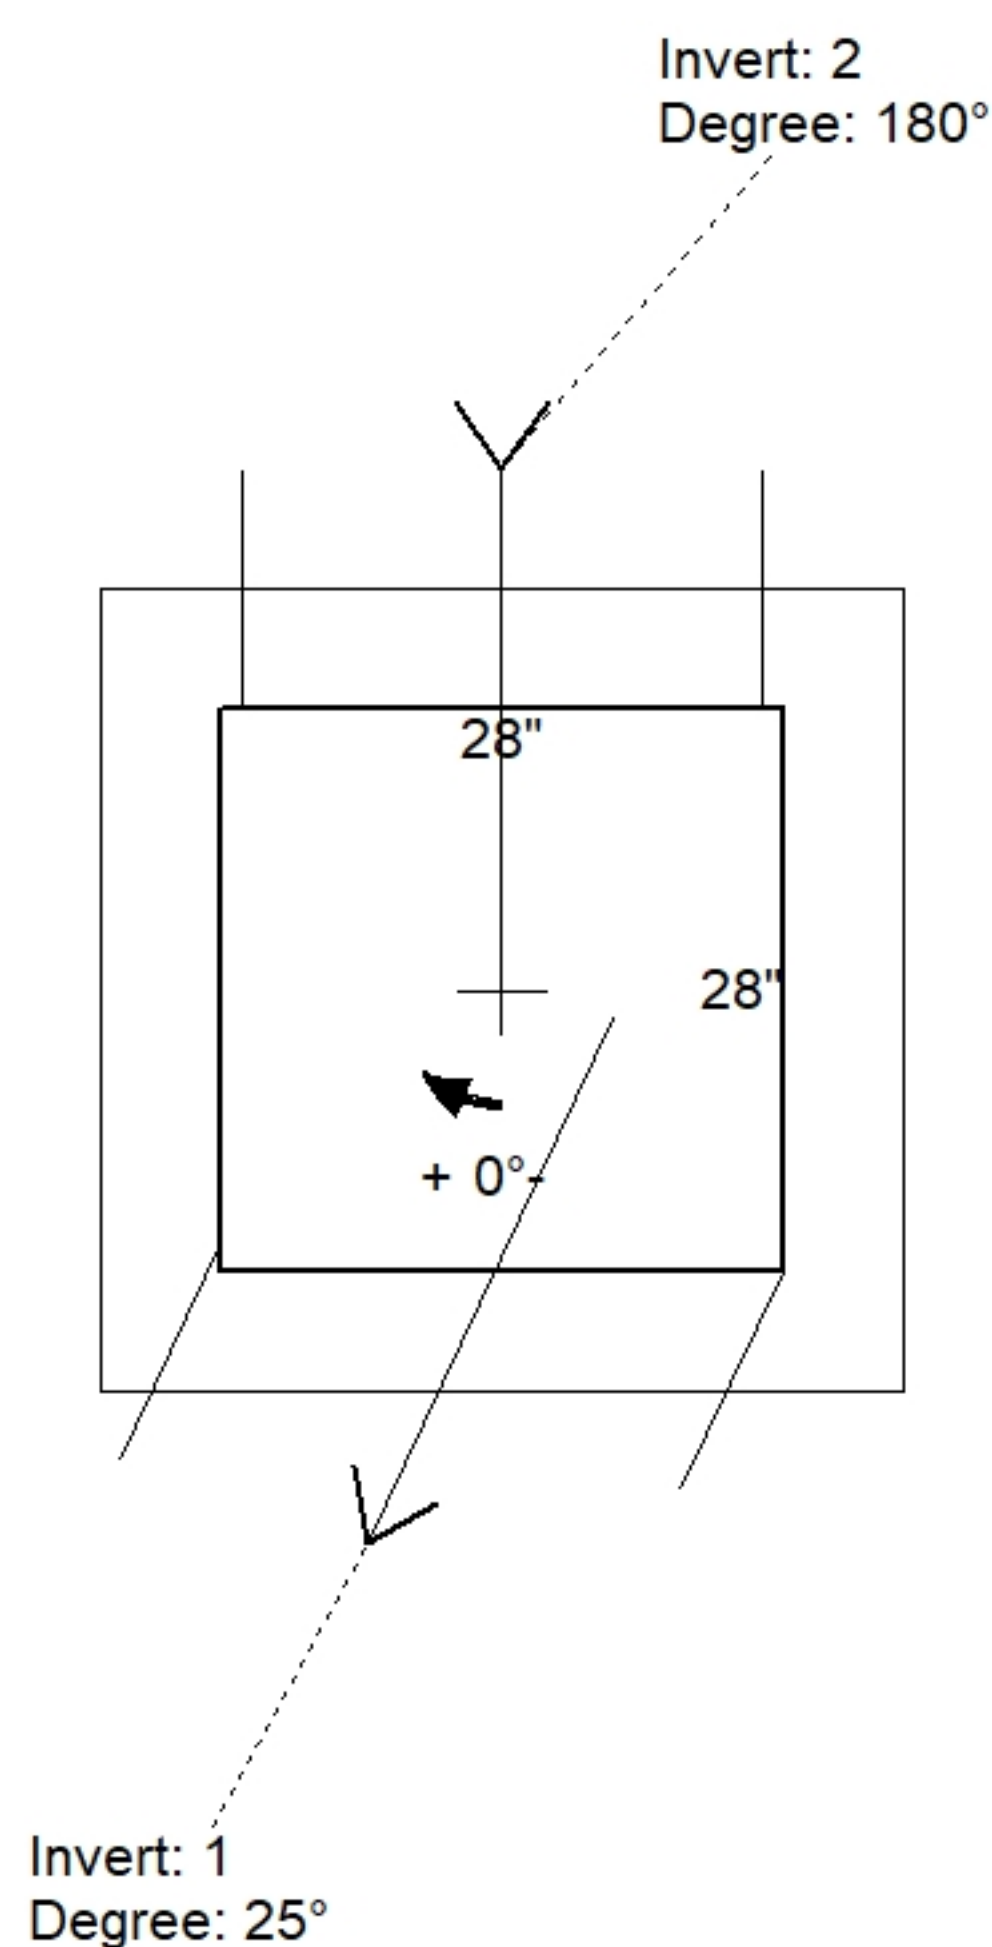

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	529.68'							
Reducer								
Invert 1	526.38'	25°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	526.48'	180°	18" RCP B WALL	23"	26"	Hole 26	1.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

28" x 28" - CASTING HEIGHT - 7.50" - (P2)

28" x 28" - BOX BASE 6inW, 6inF, Variable Ht F/n - 34" - (P1)

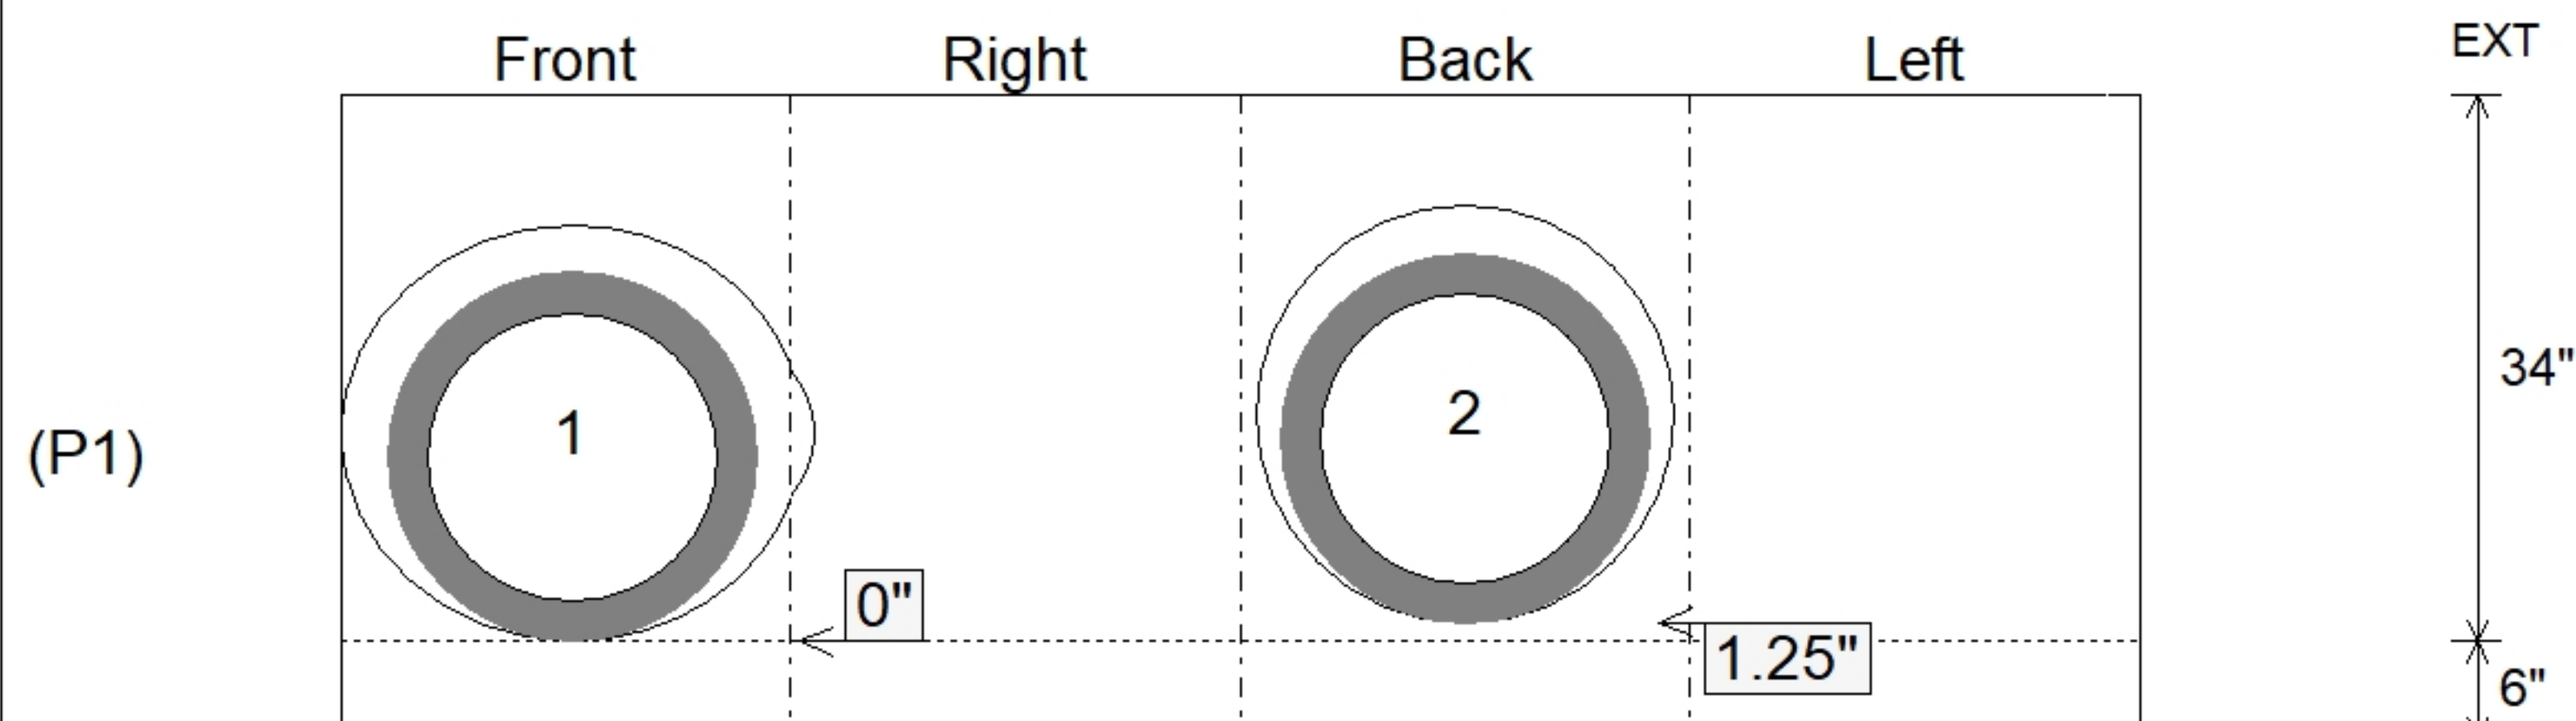

SUBMITTAL
APPROVED BY:
