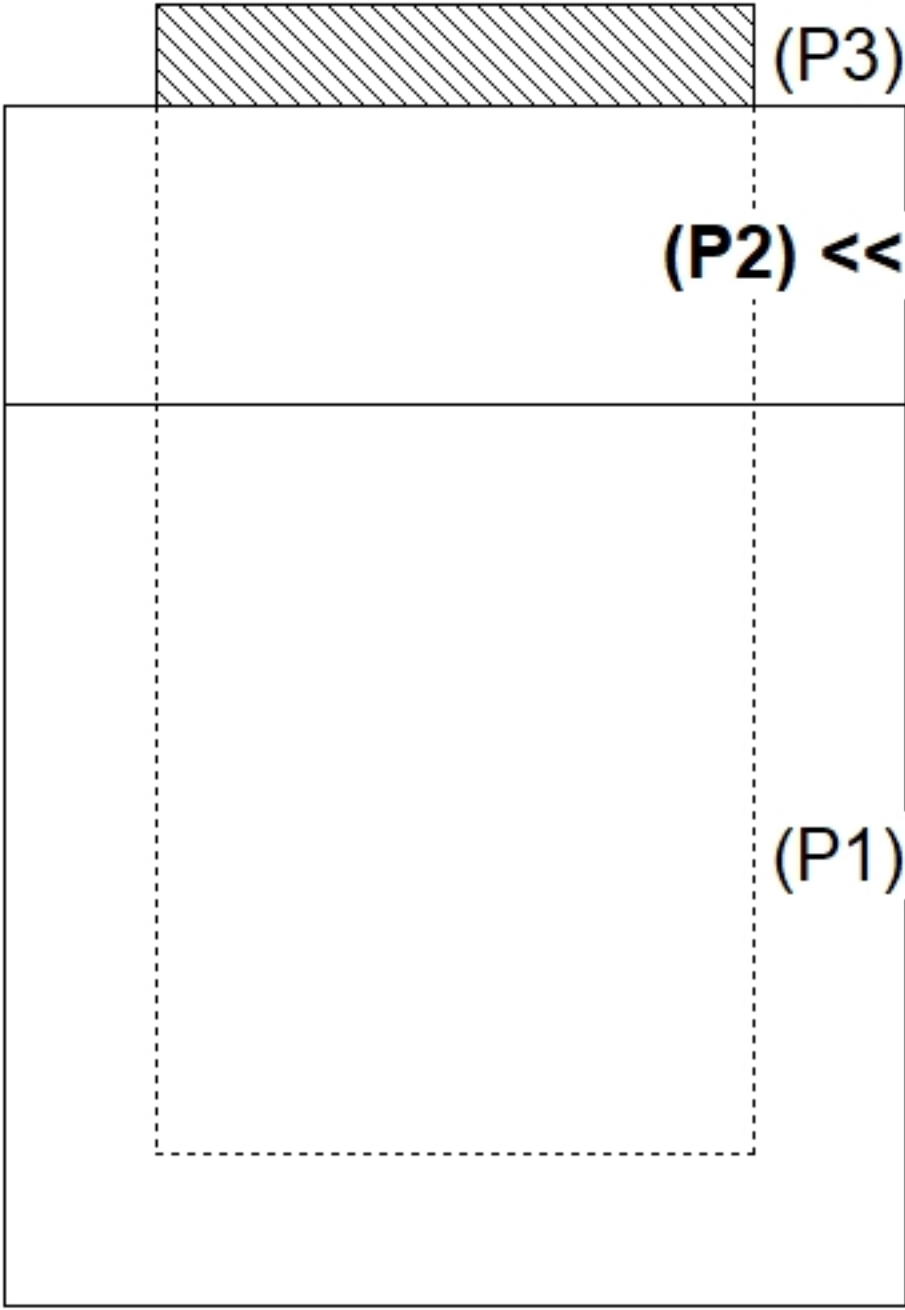
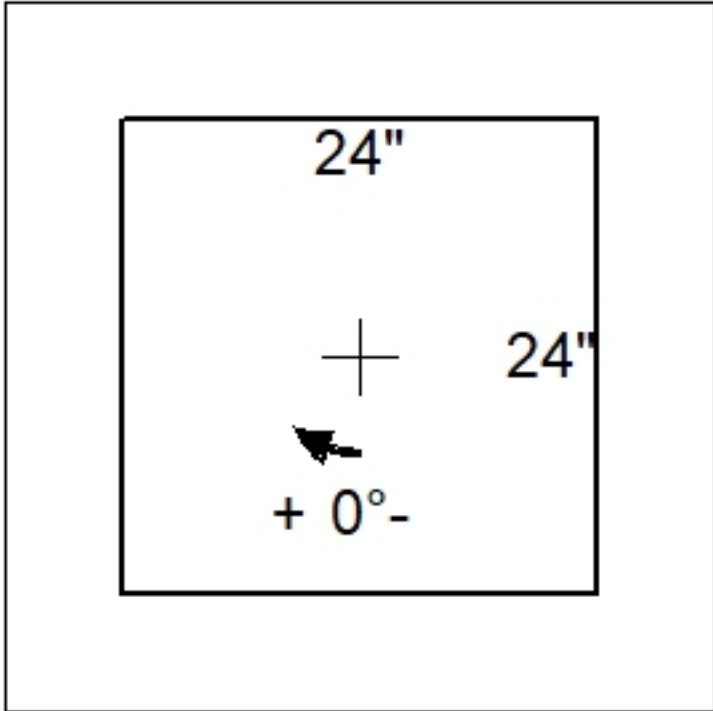



Job Name: 26-2119 512 W Kingston Ave MSD Job Location: Louisville, KY Contractor: TRC, LLC					Plant: Beaver Dam 7/16/2026 3:43:36 PM		Tech: S. Felletter PC: T. Lewis				
Structure ID: QL2 ST-CB 1											
P2		BX2424-06R12		BOX RISER 6inW F/F							
P3) 24" x 24" - CASTING HEIGHT - 4" P2) 24" x 24" - BOX RISER 6inW F/F - 12" P1) 24" x 24" - KNOCKOUT BASE 6"W/F - STOCK F/n - 30" 1) CASTING - HOE 280T F/G 2) 24" x 24" - Conseal CS-102 1.00"						0 lb 725 lb 2465 lb 182 lb 0 lb ----- 3372 lb Structure Total:		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G). . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 3.833'		Rim to Invert: 0'		Slack: 0"		Sump: 46"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
(P2)		FrontRight (24")Back (24")Left				EXT12"					
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Flat		Wall Thickness: 6" Floor Height: 0"		Height (Int): 12" Height (Ext): 12"		Weight (Net): 725 lb Volume (Net): 0.18cu.yd	
