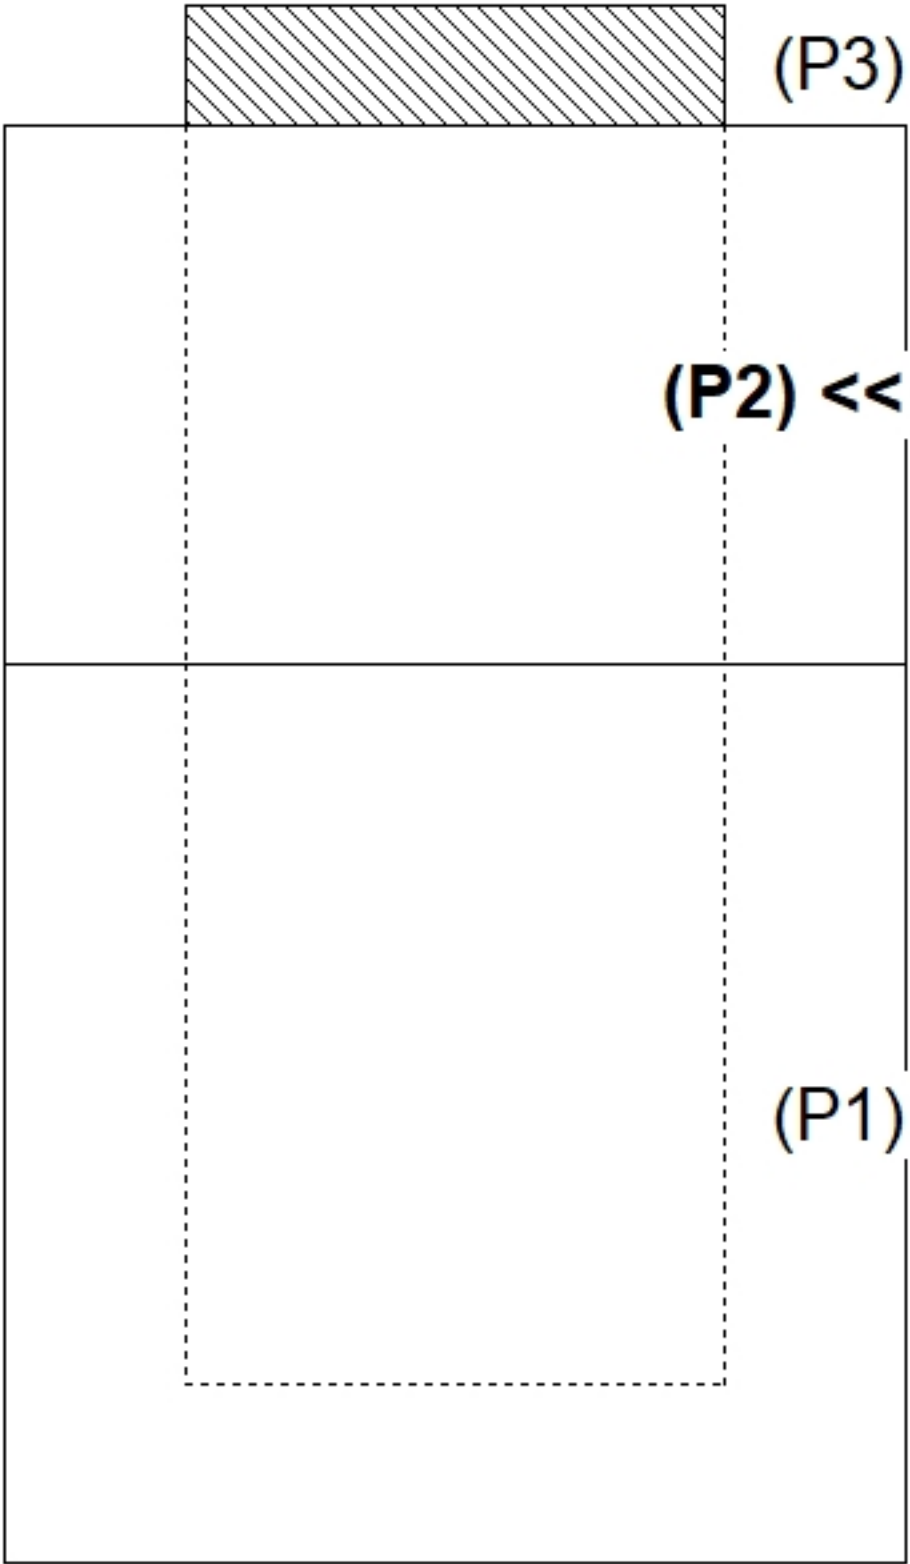
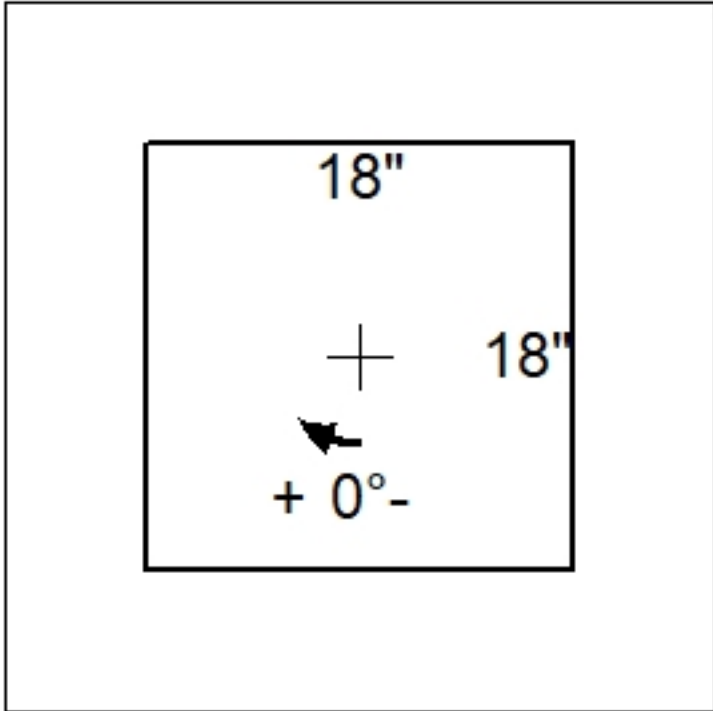



Job Name: 26-2119 512 W Kingston Ave MSD Job Location: Louisville, KY Contractor: TRC, LLC					Plant: Beaver Dam 7/16/2026 3:43:39 PM		Tech: S. Felletter PC: T. Lewis				
Structure ID: QL3 ST-CB 7											
P2		BX1818-06R18			BOX RISER 6inW F/F						
P3) 18" x 18" - CASTING HEIGHT - 4" P2) 18" x 18" - BOX RISER 6inW F/F - 18" P1) 18" x 18" - KNOCKOUT BASE 6"W/F - STOCK F/n - 24" 1) CASTING - HOE 165A F/G 2) 18" x 18" - Conseal CS-102 1.00"						0 lb 870 lb 1613 lb 138 lb 0 lb ----- 2621 lb		Structure Notes: . 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 165-A F/G). . REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.			
Rim: 3.833' Rim to Invert: 0' Slack: 0" Sump: 46" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (┘)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
(P2)		FrontRight (18")Back (18")Left				18"					
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Flat		Wall Thickness: 6" Floor Height: 0"		Height (Int): 18" Height (Ext): 18"		Weight (Net): 870 lb Volume (Net): 0.22cu.yd	
