

Contractor: Winwater Hartford KY Co.

Plant: 100




Slack: 0.53"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.


P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"
1) CASTING - HOE 525 SET FLAT GRATE (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 18

0 lb
4105 lb
442 lb
0 lb
0 lb


Structure Total: 4547 lb

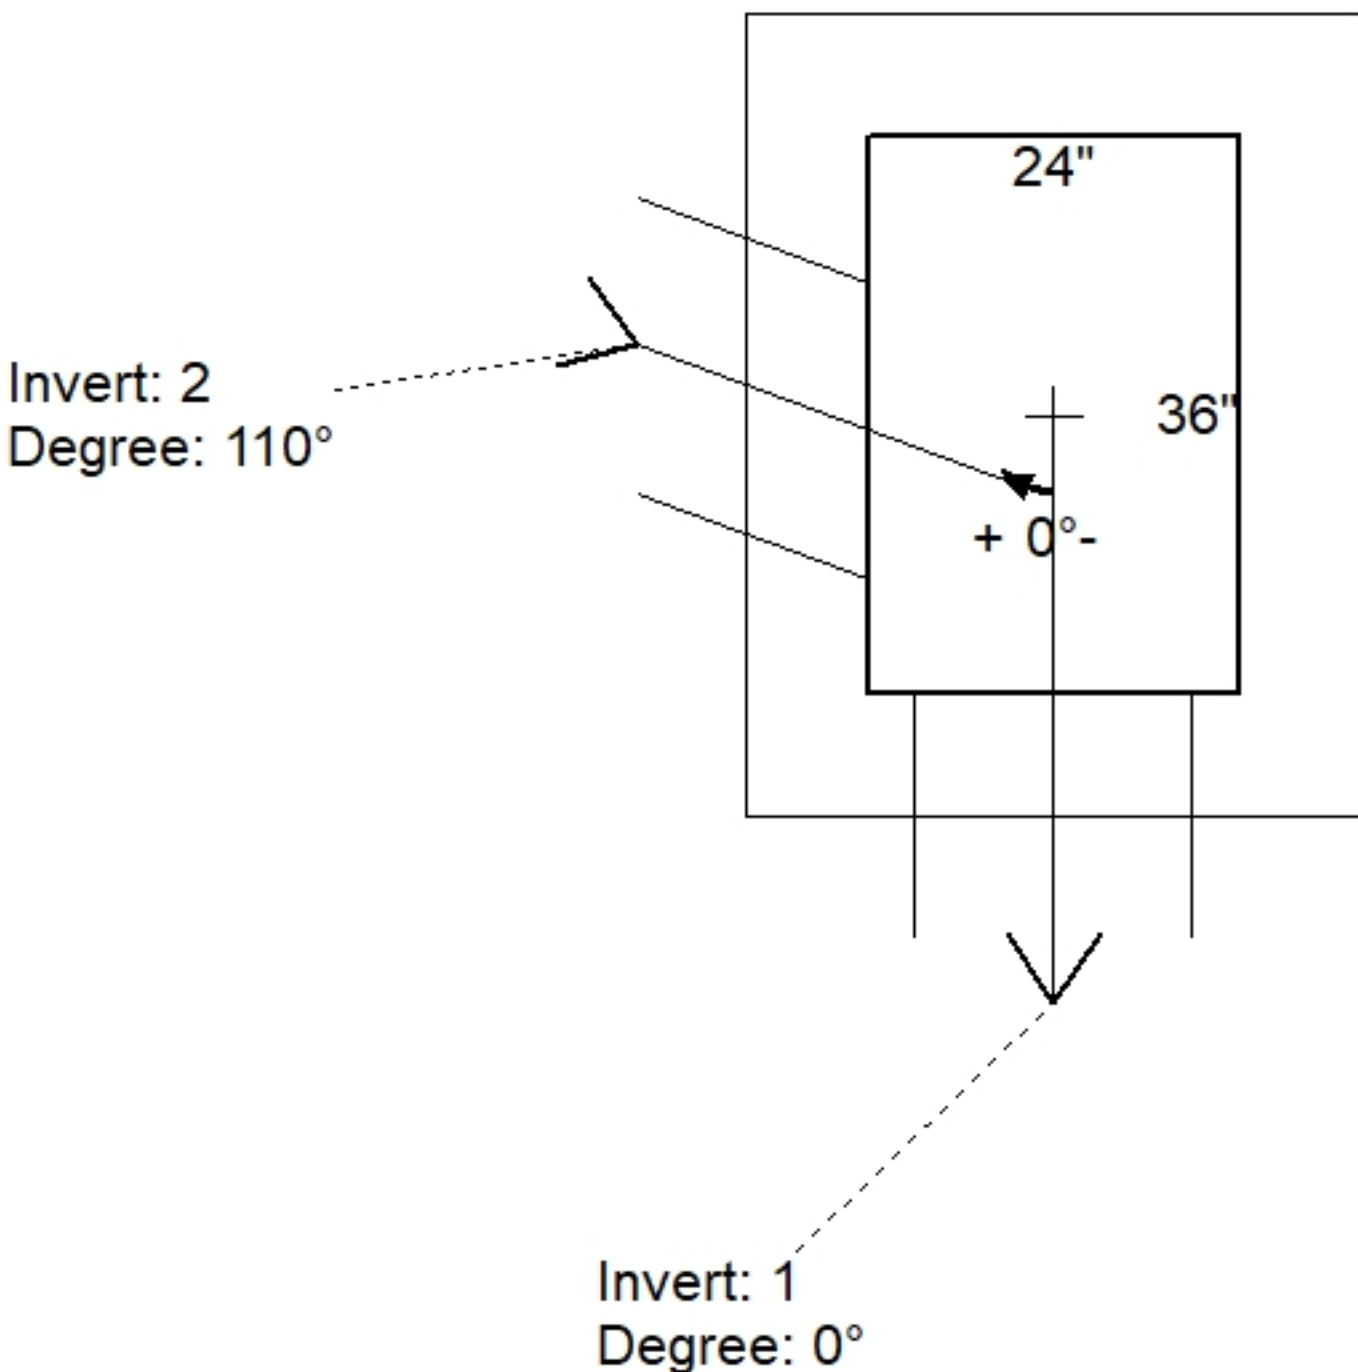

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	407.15'							
Reducer								
Invert 1	404.21'	0°	12" HDPE	14.5"	18"	Hole 18	0"	P1
Invert 2	404.21'	110°	12" HDPE	14.5"	18"	Hole 18	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

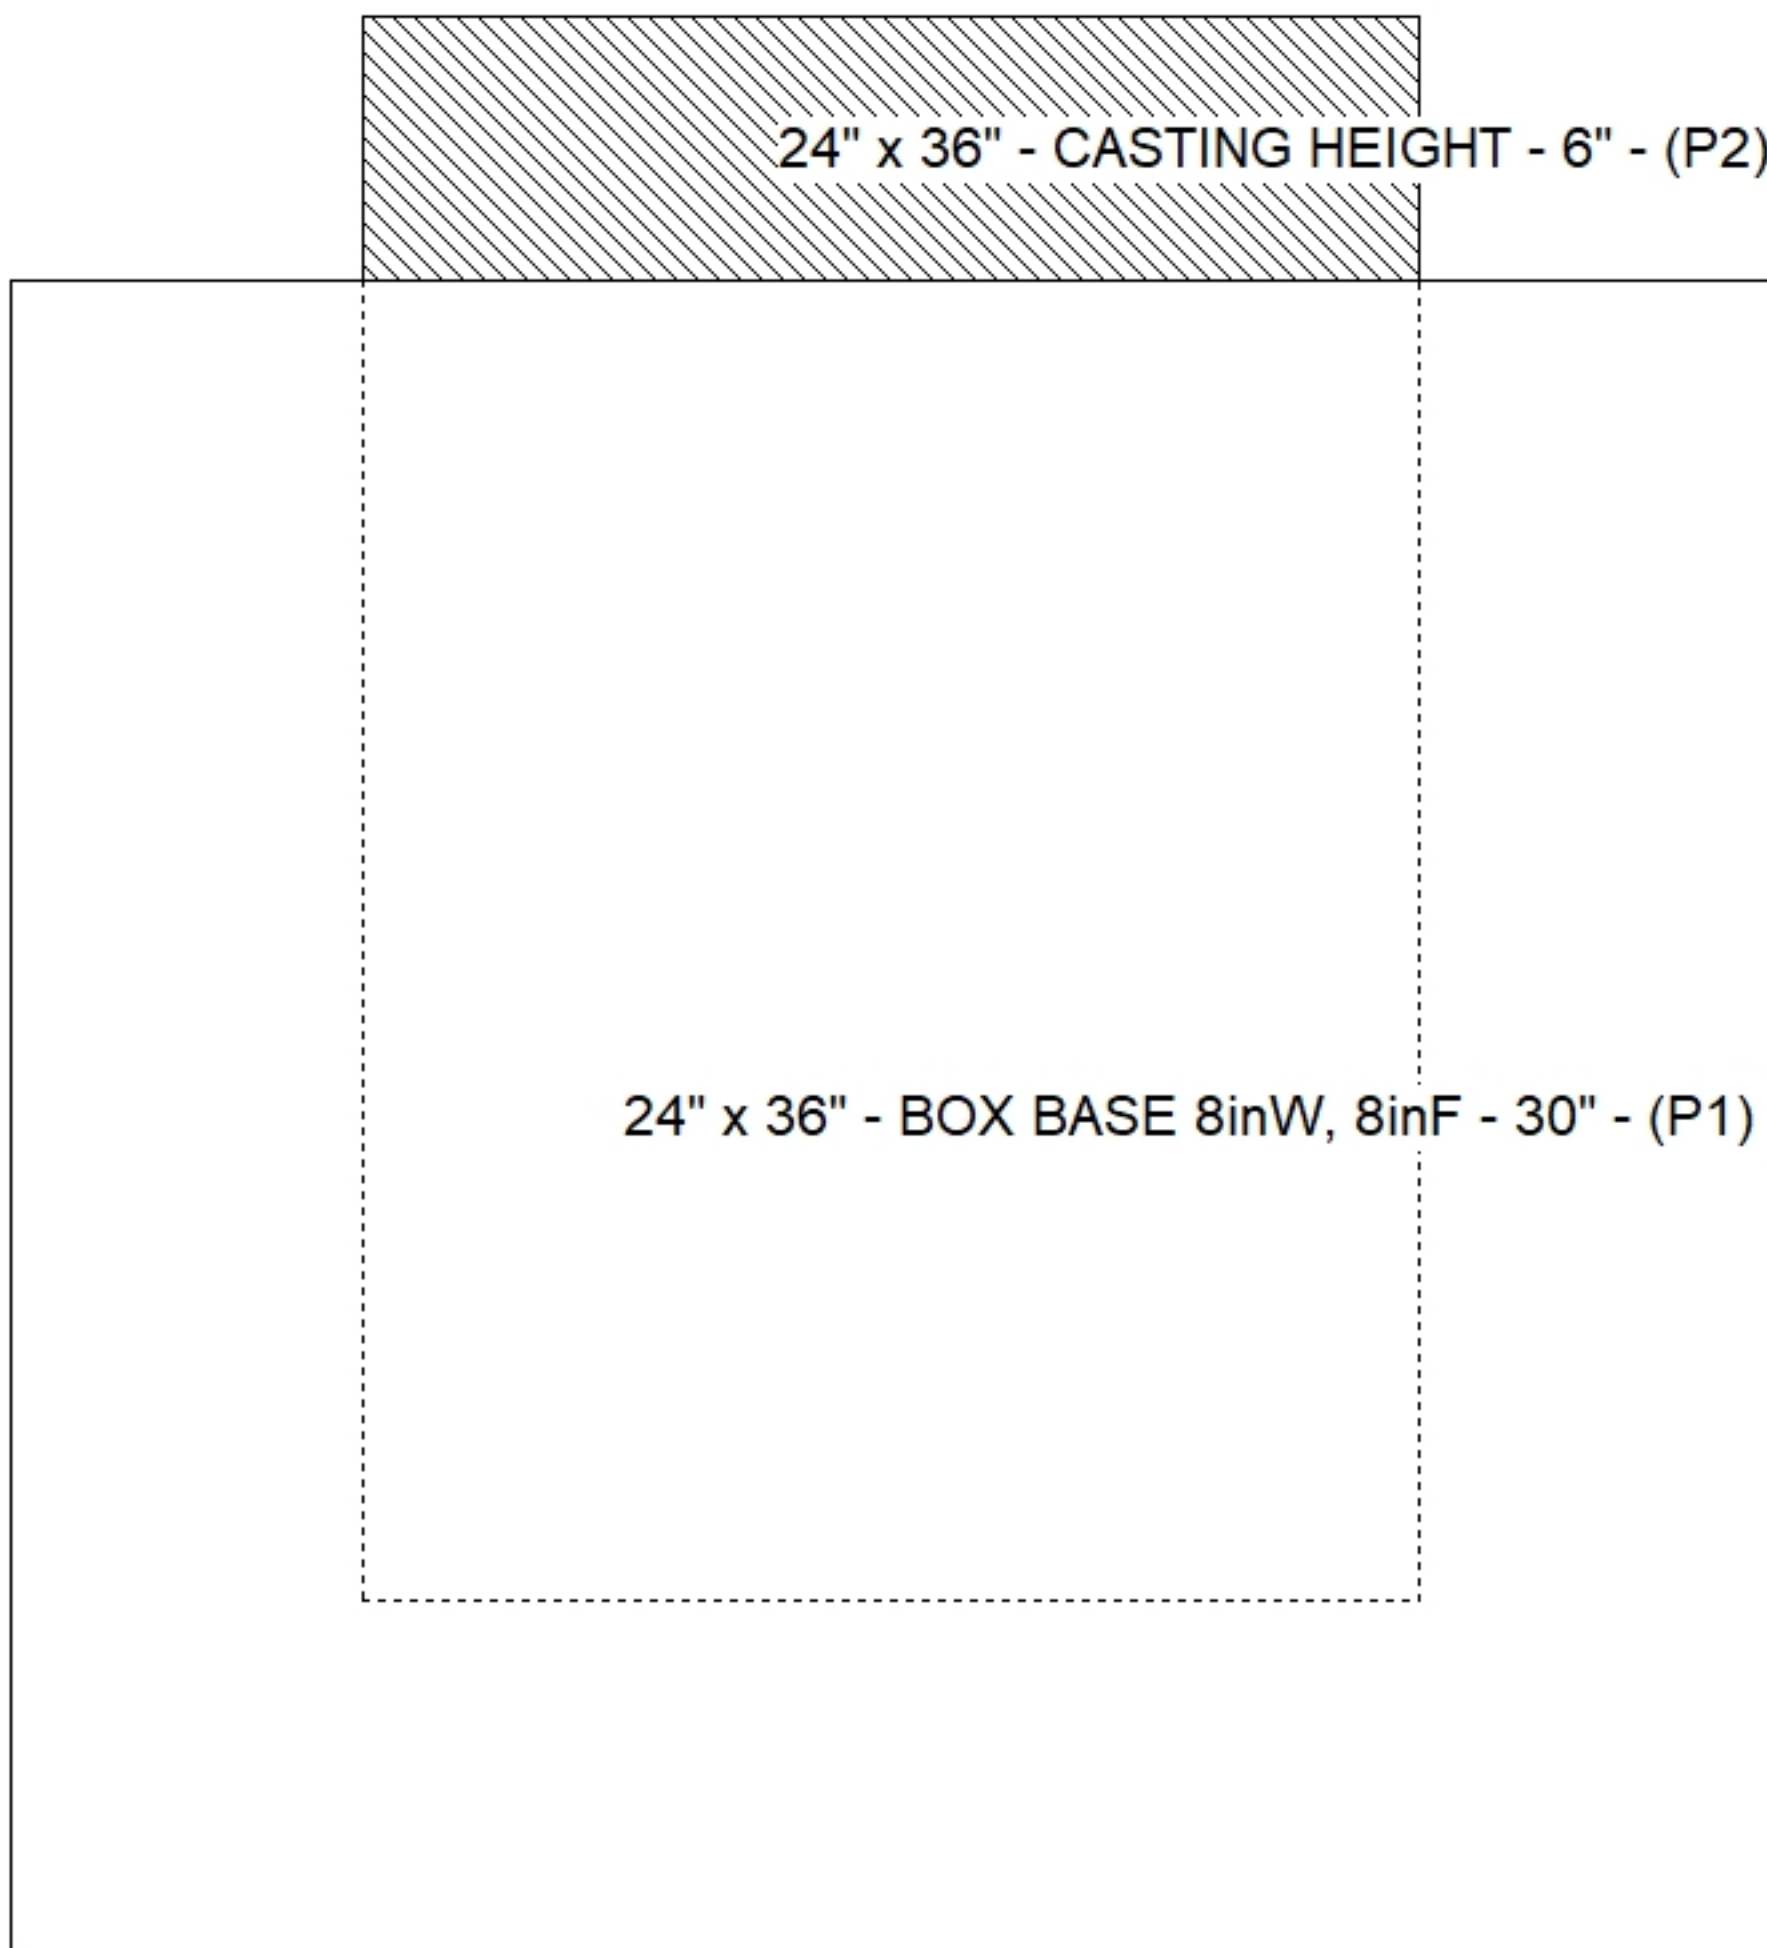

Default - Interior Dimensions

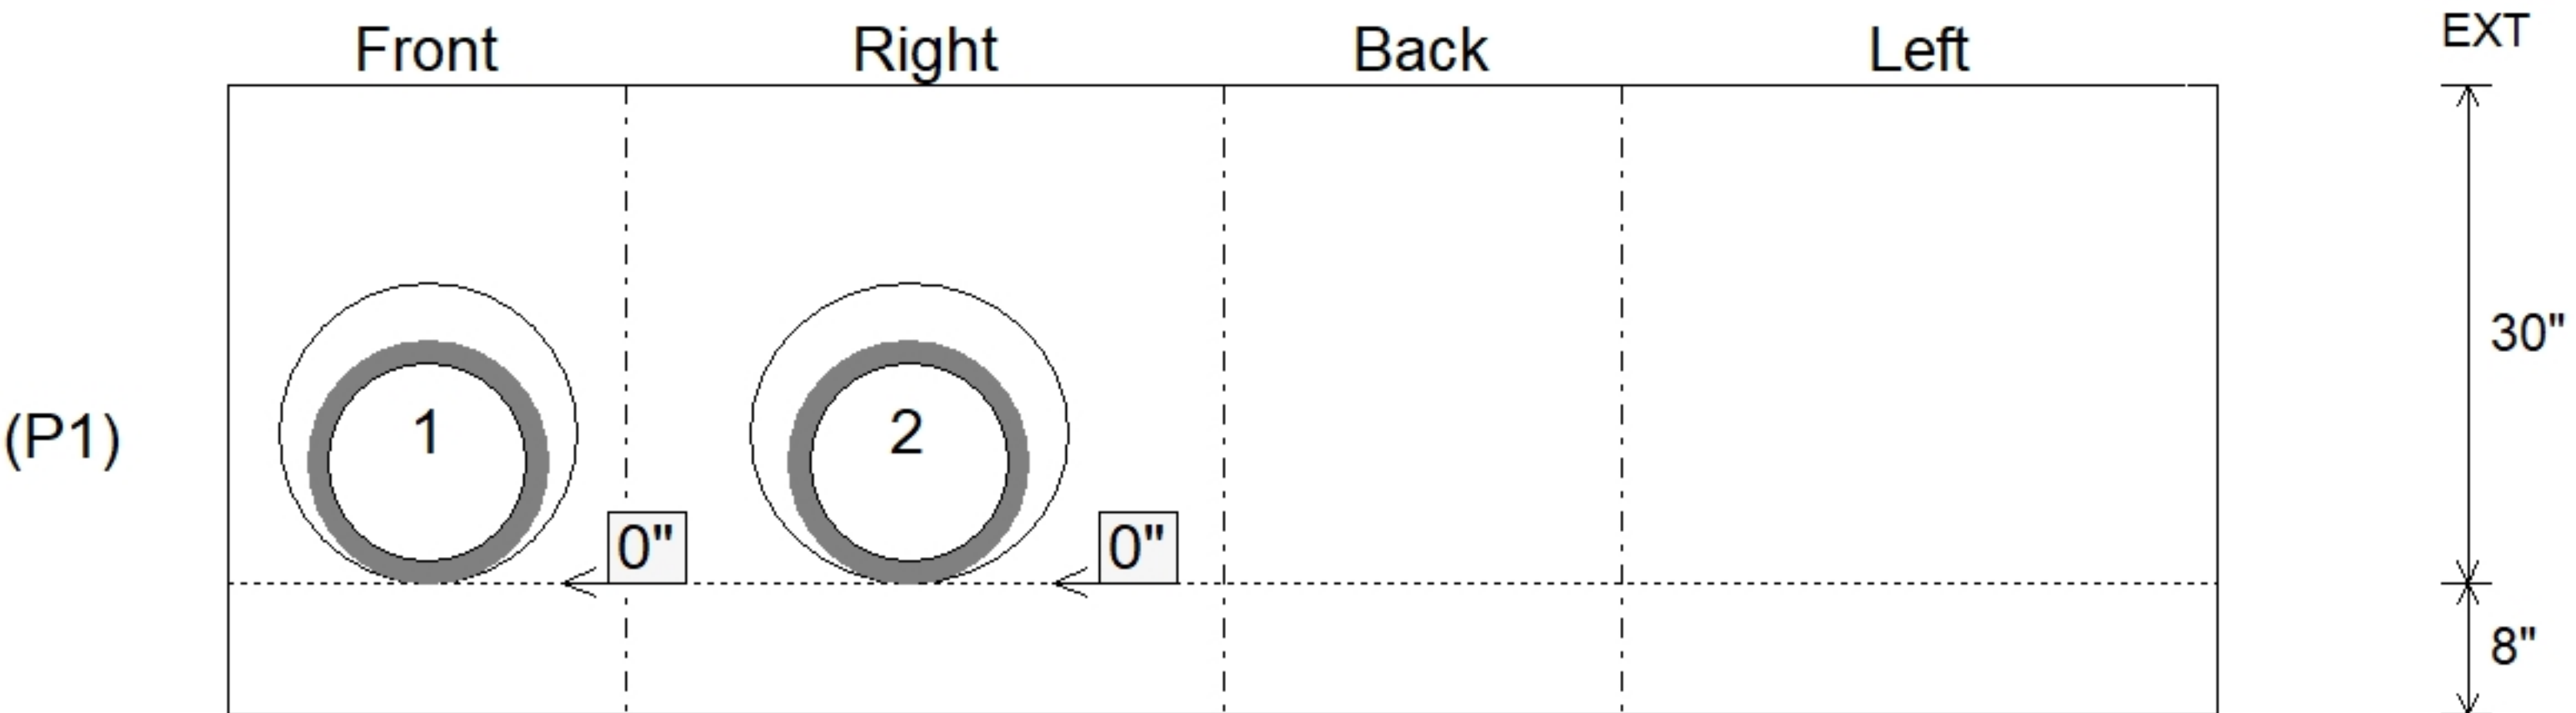

Submittal Drawing
6/2/2026 8:40:51 AM

SUBMITTAL
APPROVED BY:
