

Contractor: Sensabaugh Design & Construction, LLC

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 9.59'


Floor Height: 0"

Slack: 2.08"


- RISER/WALLS (As .12)

0 lb


Structure Total: 9692 lb

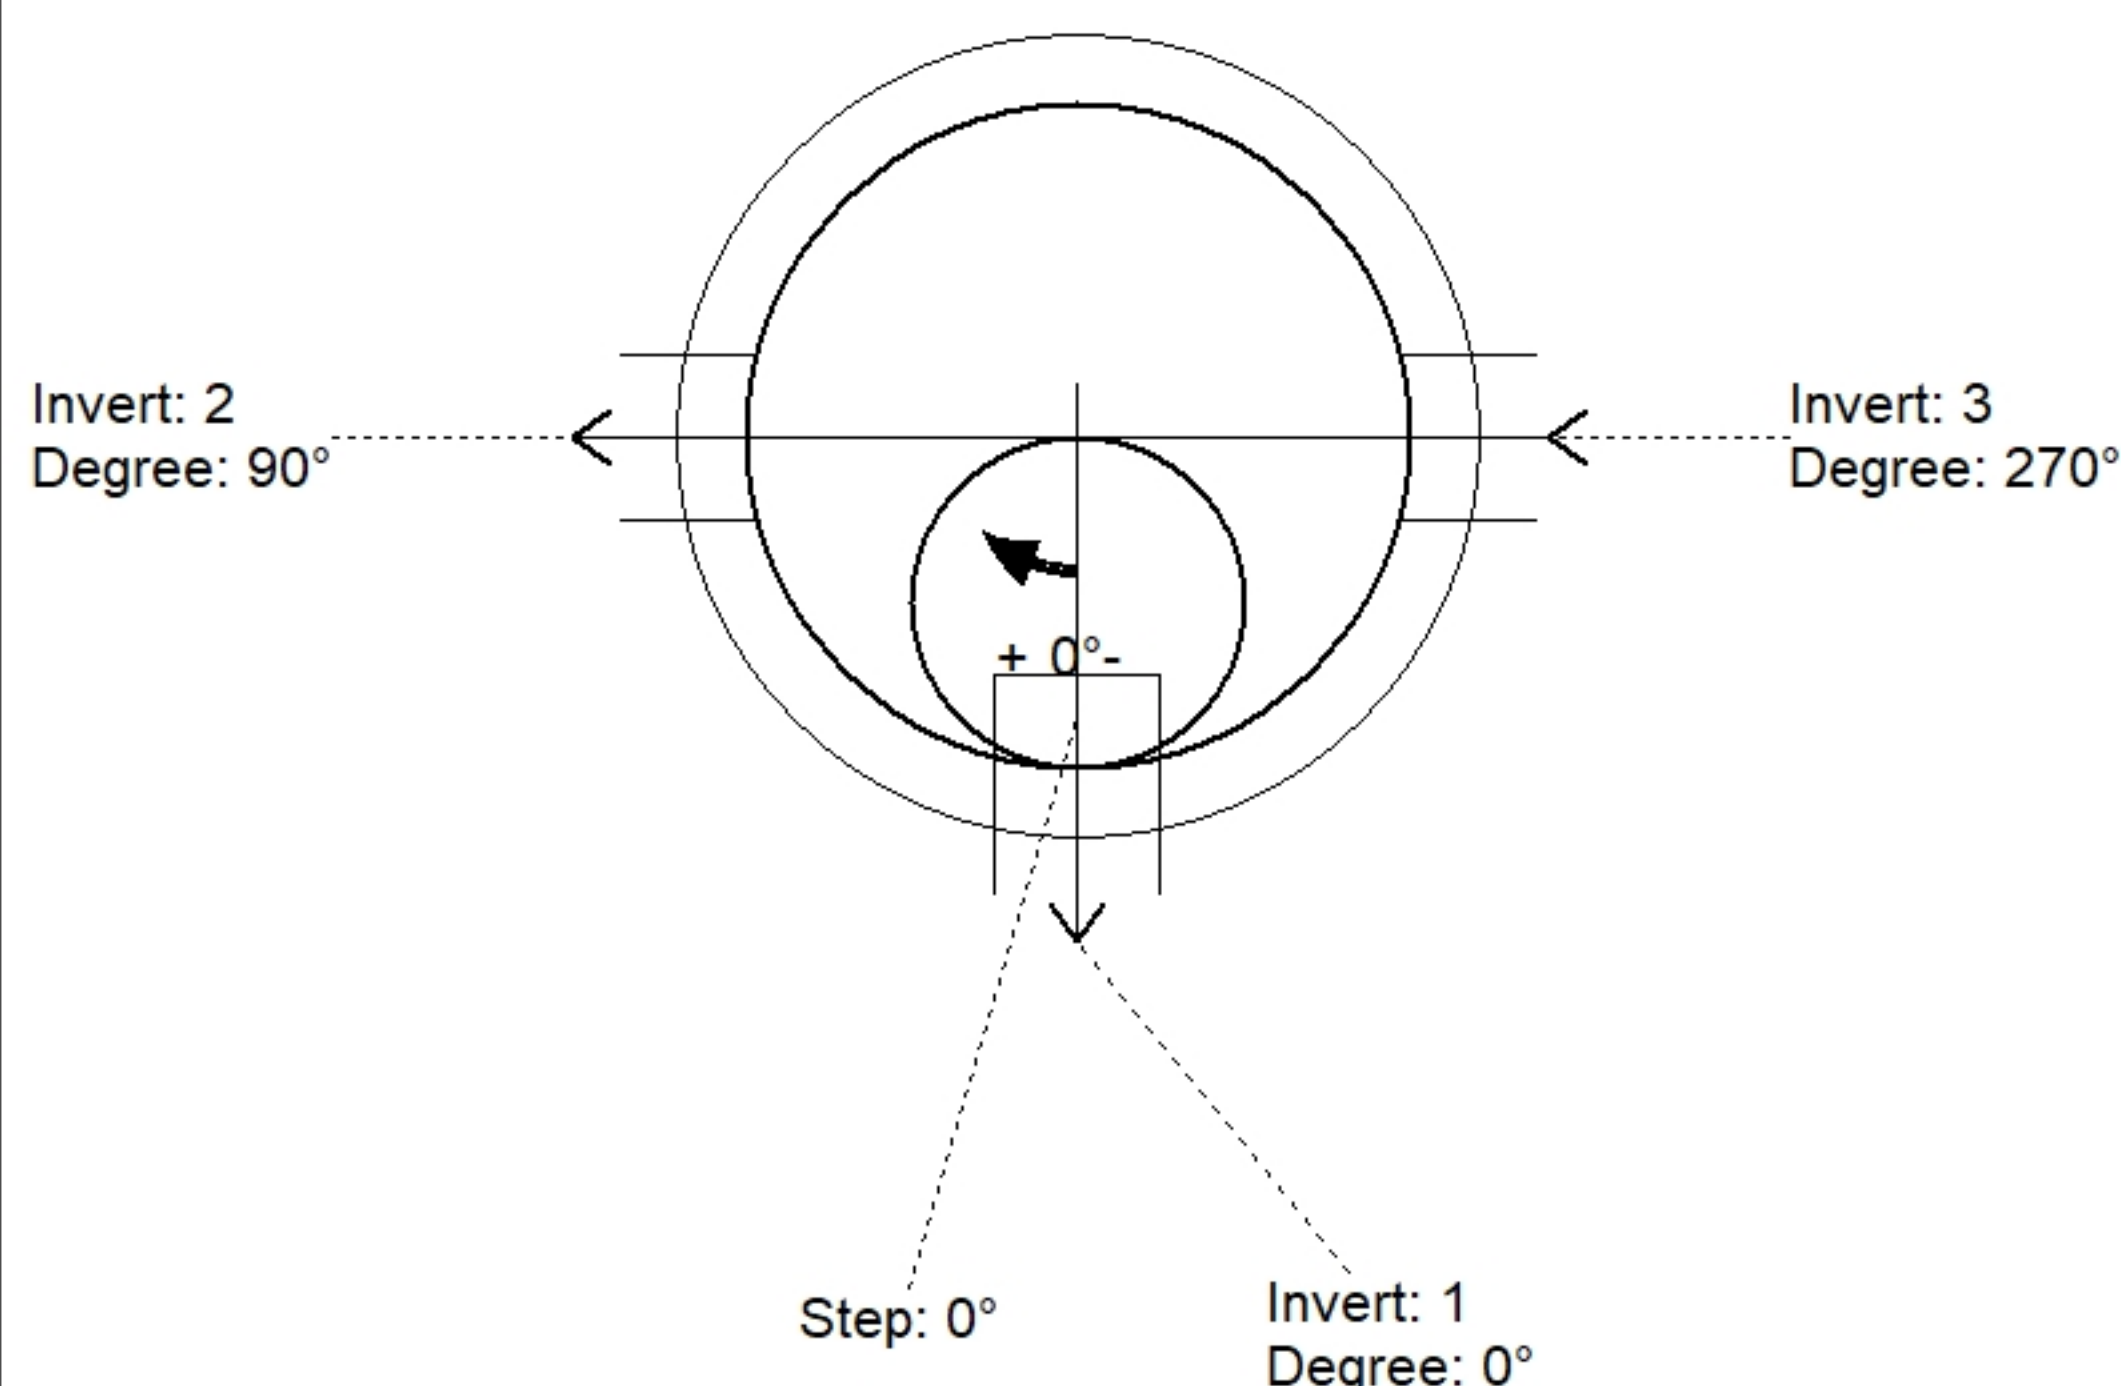

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (␣)	Re
Rim	570.36'							
Reducer								
Invert 1	560.77'	0°	6" PVC SDR35	6.25"	12"	PSX 12-06 NYLO	5"	P2
Invert 2	560.87'	90°	6" PVC SDR35	6.25"	12" x 18"	DOGHOUSE 12"x18"	3.2"	P2
Invert 3	560.87'	270°	6" PVC SDR35	6.25"	12" x 18"	DOGHOUSE 12"x18"	3.2"	P2
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

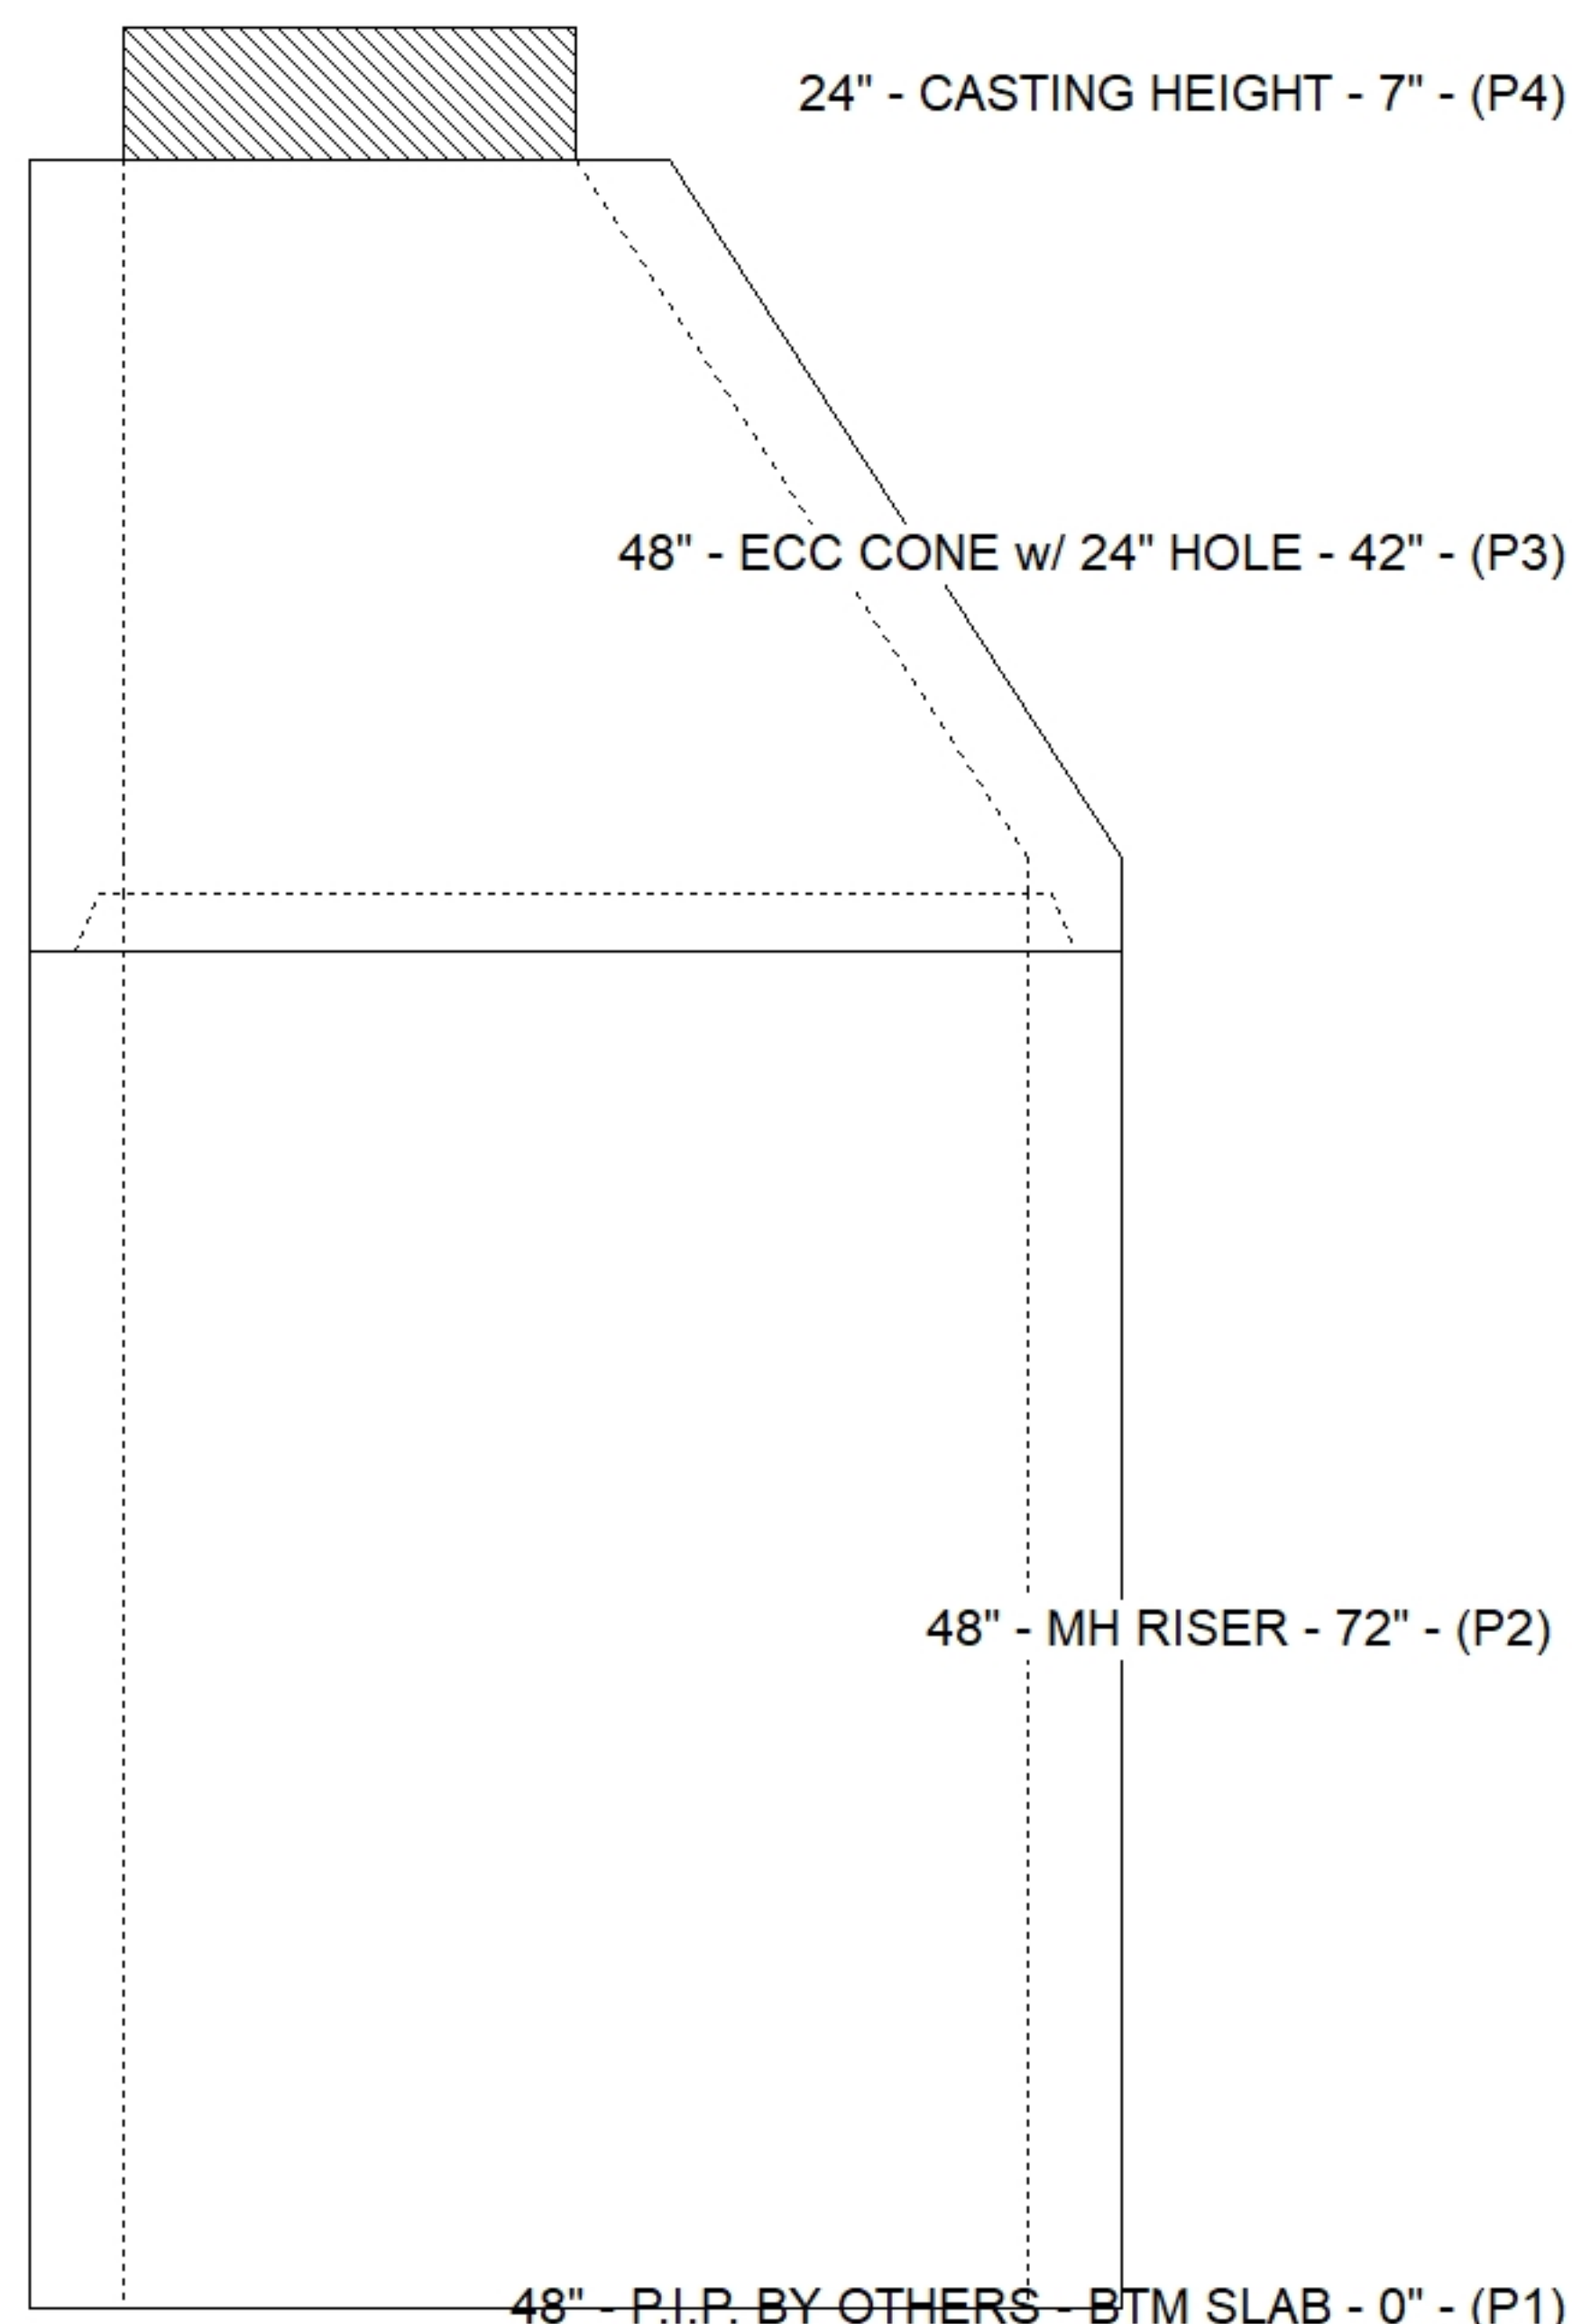

Default - Interior Dimensions

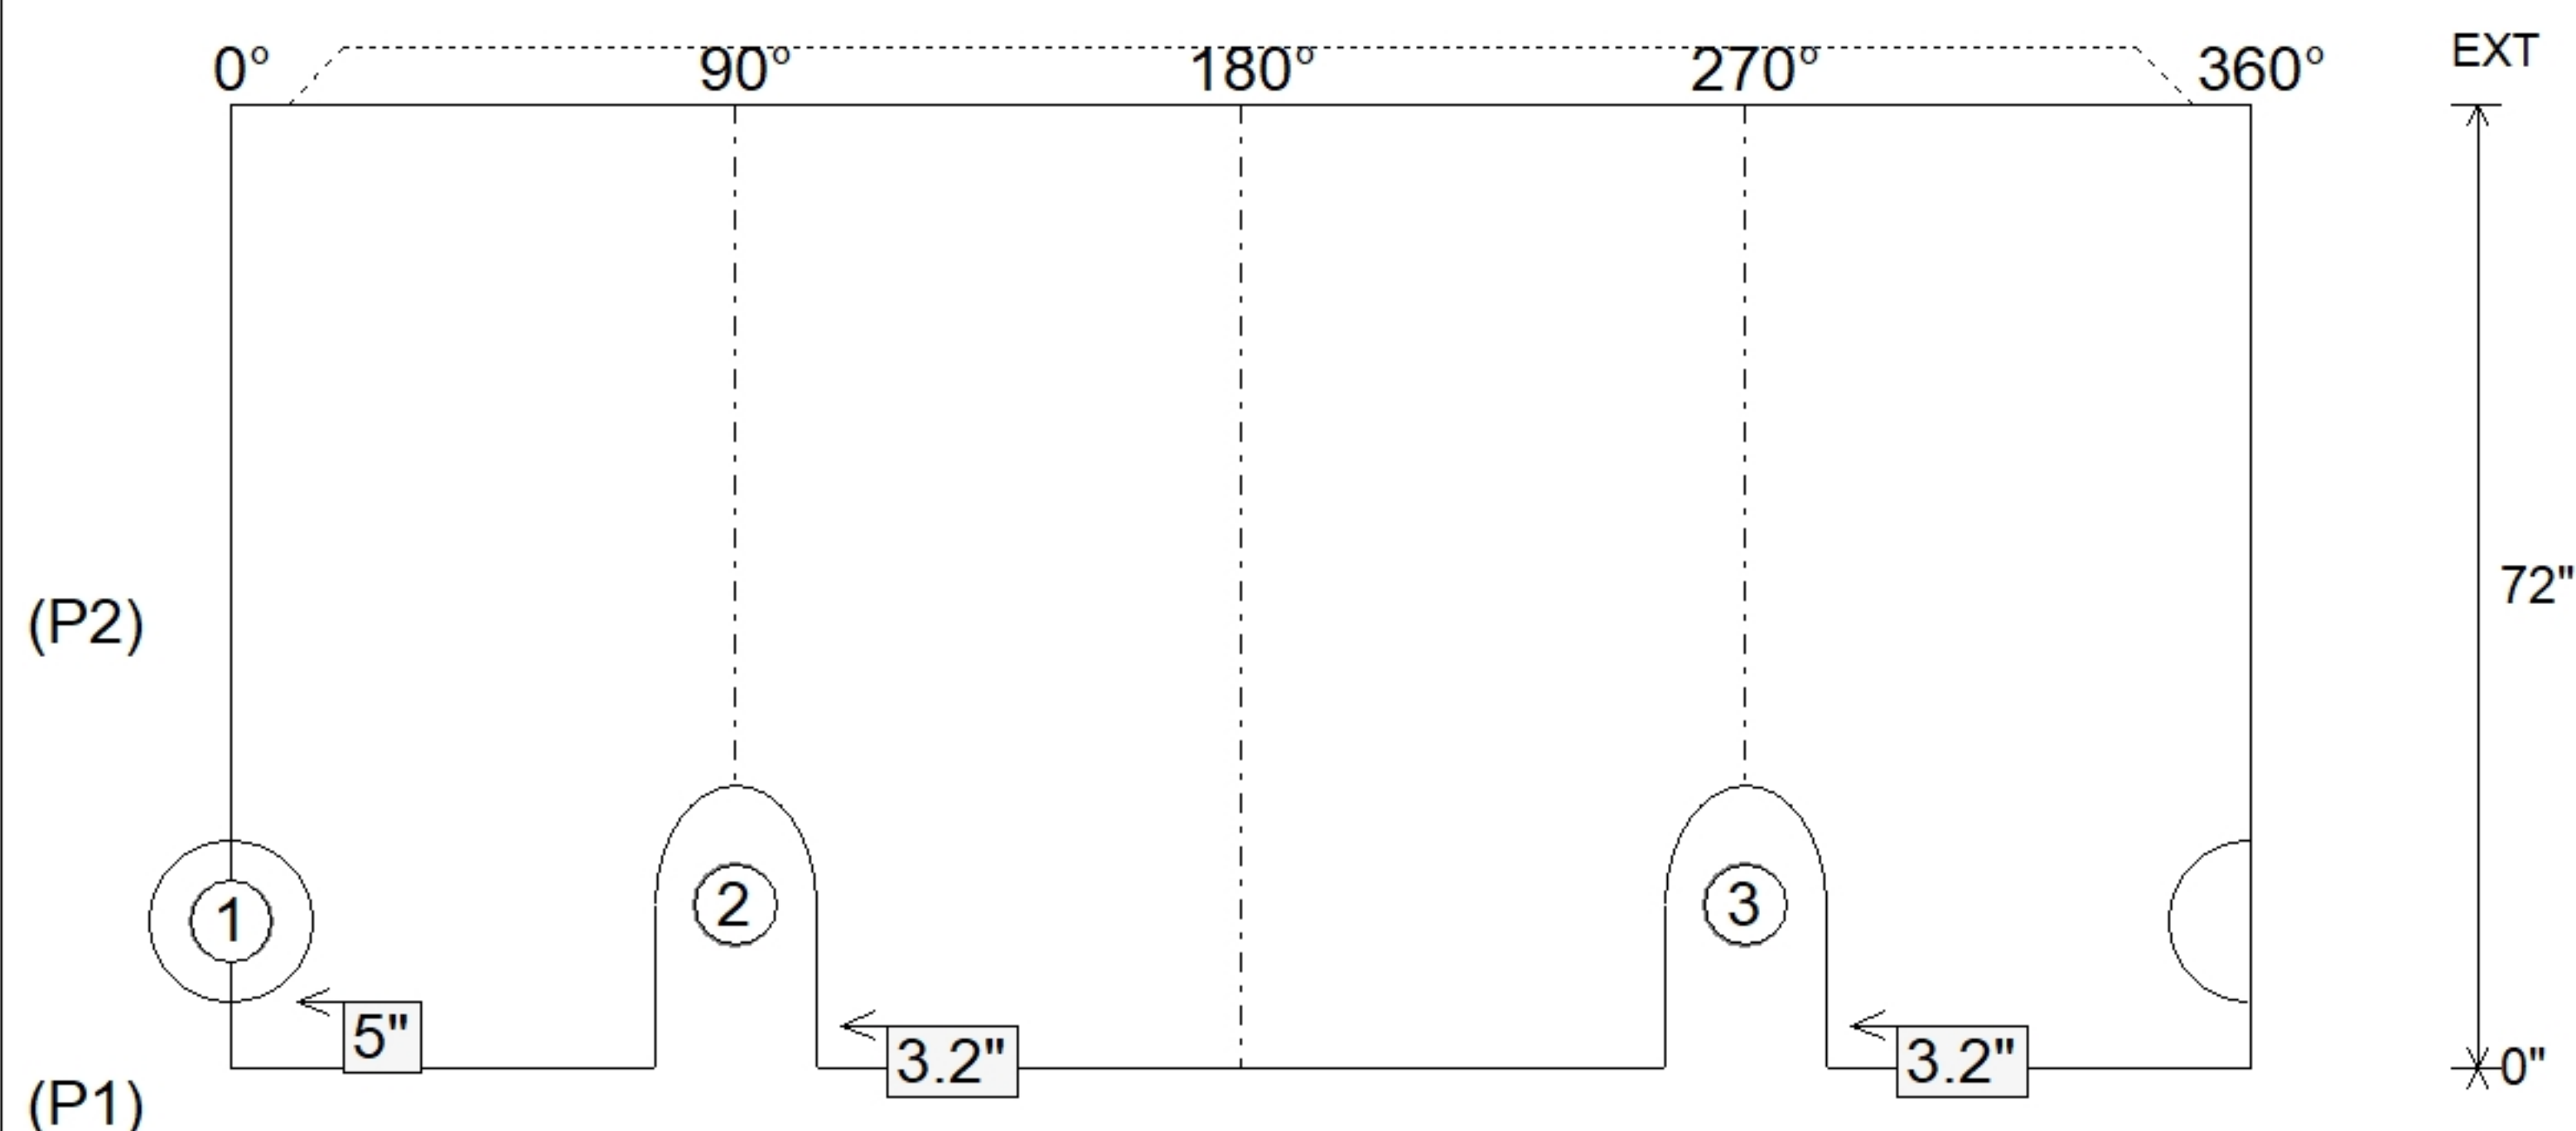

Submittal Drawing
6/19/2026 8:30:38 AM

SUBMITTAL
APPROVED BY:
