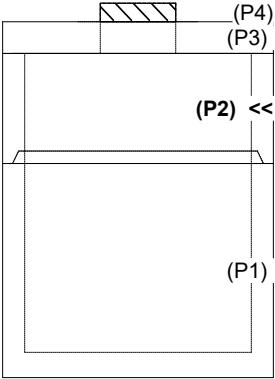




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.				Plant: Beaver Dam 8/18/2026 12:42:51 PM		Tech: J. Coppage PC: E. Bradley					
Structure ID: 107 ST-MH											
P2		MH072RSVF		MH RISER Custom Ht							
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 72" - MH FLAT TOP w/24"x36" Hole - 10" P2) 72" - MH RISER Custom Ht - 35" P1) 72" - MH BASE Custom Ht - 60" 2) 72" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 52 1) DOGHOUSE INVRTD - 30"x28" 5) MH Step ML-10-TDS-NCR - 10"						0 lb 3715 lb 4650 lb 9913 lb 0 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- 18278 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE K / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W.			
Rim: 606.5'						Rim to Invert: 9.11'		Slack: 1.47"		Sump: 3.15"	
Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2											
Invert 3	602.87'	270°	202.633"	24" HDPE KO PANEL - 3" THICK	27.8"	DOGHOUSE INVRTD 30"x28"	30" x 28"	30.944"	2.01"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: Groove		Wall Thickness: 7" Floor Height: 0"		Height (Int): 35" Height (Ext): 35"		Weight (Net): 4650 lb Volume (Net): 1.19cu.yd	
