




Job Name: 26-2212 - CDTI Building 1 Job Location: Charlestown, IN Contractor: Dan Cristiani Excavating Co. Inc.					Plant: Beaver Dam 8/18/2026 12:38:35 PM		Tech: J. Coppage PC: E. Bradley				
Structure ID: 201 ST-MH											
P1 MH048BA24		MH BASE Custom Ht									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/24"x36" Hole - 7" P1) 48" - MH BASE Custom Ht - 24" 1) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 1) DOGHOUSE INVRTD - 24"x24" 2) MH Step ML-10-TDS-NCR - 10"						0 lb 1044 lb 2783 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 3827 lb		Structure Notes: . **INDOT STATE PROJECT** 1. (GREEN HAT CI3158-F PROVIDED BY OTHERS) 2. INDOT MH TYPE C / ASTM C478 SPEC'S. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .62) #5 BARS AT 6" C.C.E.W. - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..			
Rim: 605.55' Rim to Invert: 3.24' Slack: 3.48" Sump: 1.6" Step Position: 180°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	602.31'	0°	0"	18" HDPE	21.2"	DOGHOUSE INVRTD 24"x24"	24" x 24"	25.133"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											




RIGHT-SIDE UP VIEW (int. dimensions)

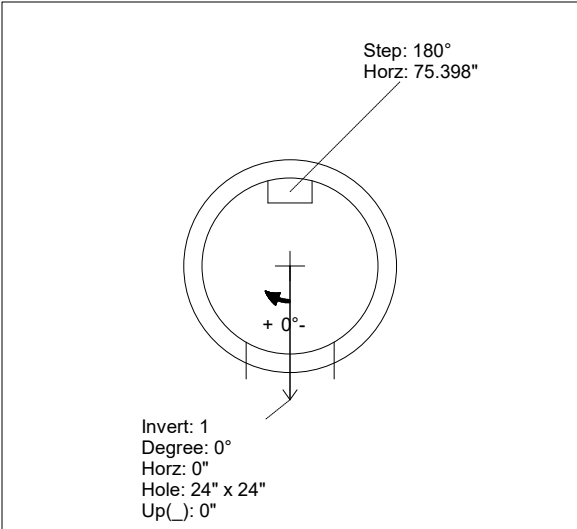

UPSIDE-DOWN VIEW (int. dimensions)

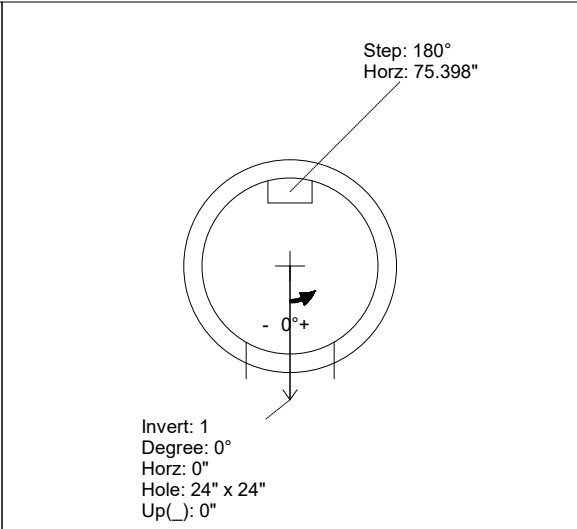

INSIDE WALL DIMENSIONS

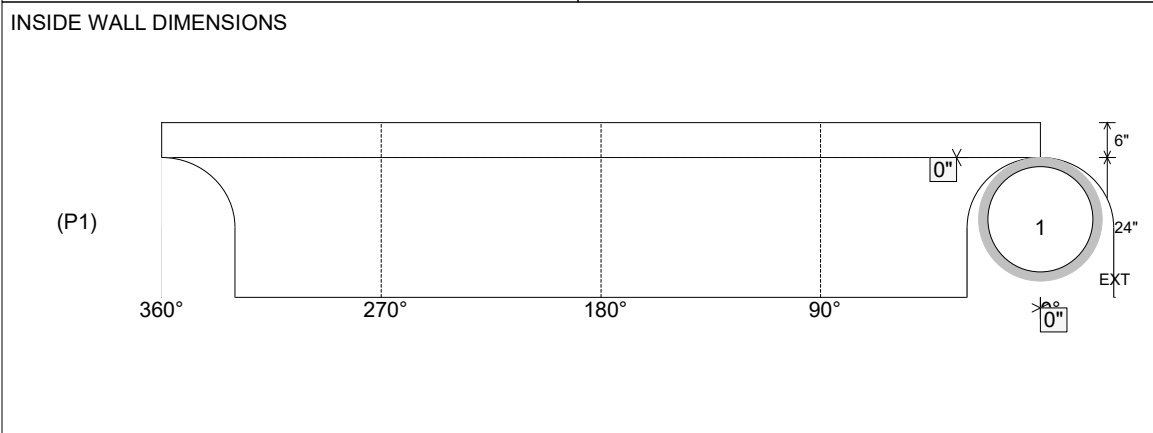

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 2783 lb Volume (Net): 0.71cu.yd
----------------------------------	-------------------------------	--	--	--
