

Job Name: 26-2217 Kroger COB
Job Location: Bowling Green, KY
Contractor: Stewart Richey

Plant: Beaver Dam

7/21/2026 8:13:04 AM

Tech: J. Coppage

PC: T. Lewis



Structure ID: INL1 ST-MH

P2 MH048LD12-24SQ



MH FLAT TOP w/24"x24" Hole

- P3) 24" x 24" - CASTING HEIGHT - 4"
P2) 48" - MH FLAT TOP w/24"x24" Hole - 12"
P1) 48" - MH BASE - 60"
1) CASTING - HOE 280T F/G
1) 48" - SGL 1"x14.5' Butyl (2x)
2) Hole - 24
5) MH Step ML-10-TDS-NCR - 10"

Structure Total:

- 0 lb
1500 lb
5127 lb
182 lb
0 lb
0 lb
0 lb

6809 lb
- Structure Notes:
1. JR HOE HOE-280T F/G PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,500 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

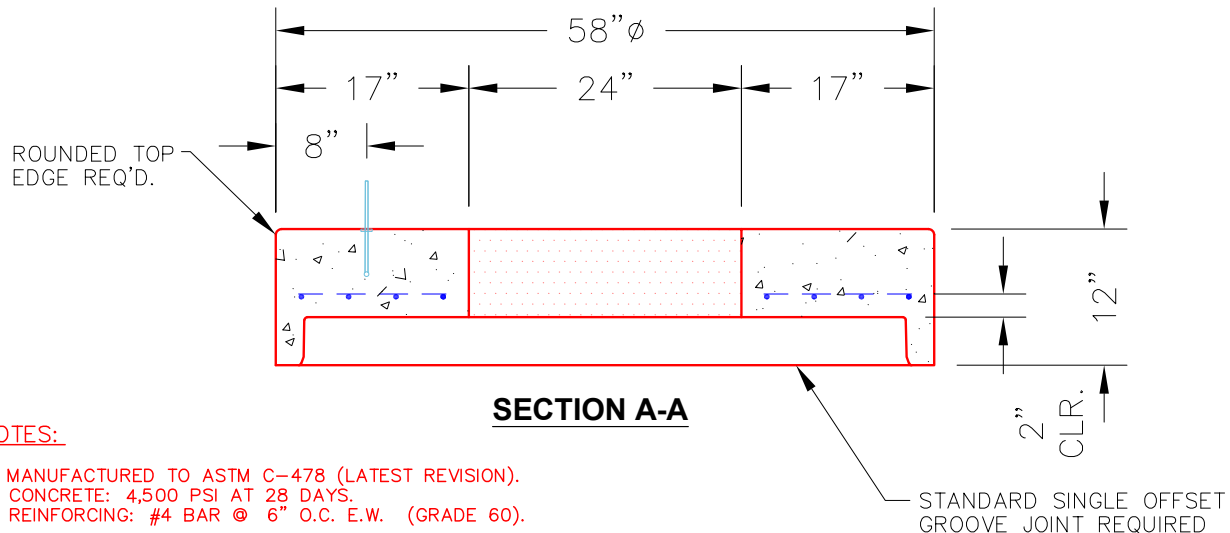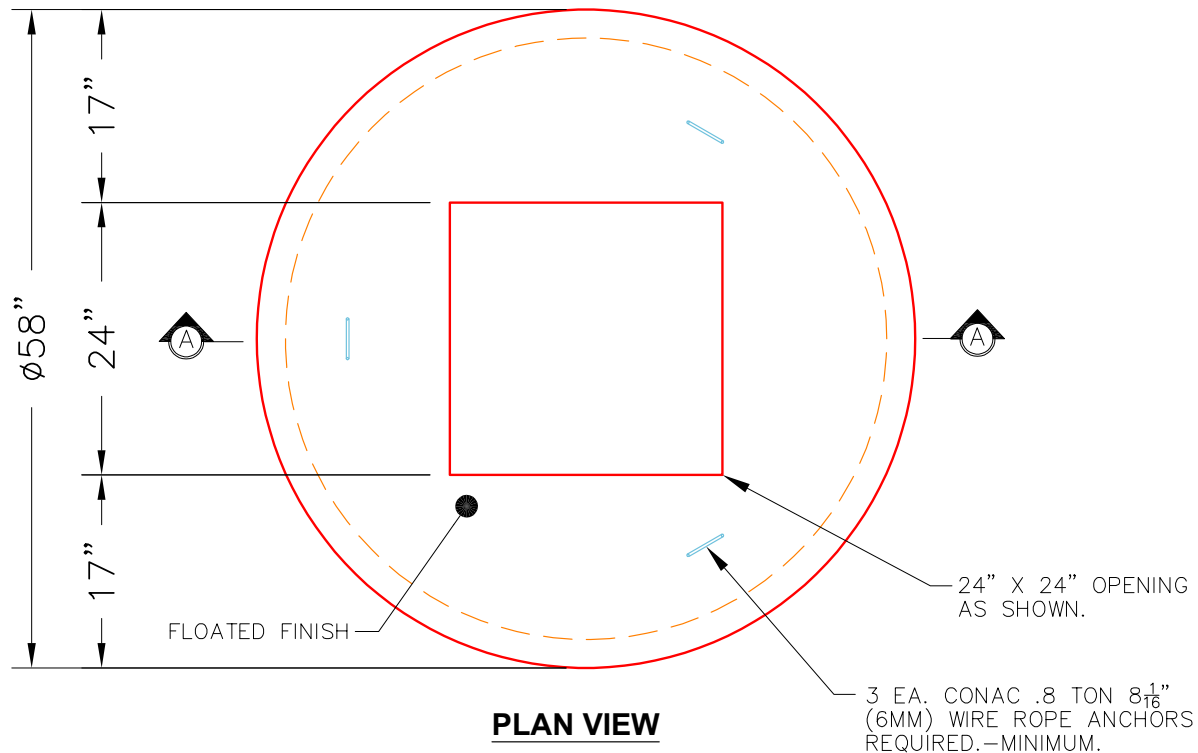

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,500 PSI AT 28 DAYS.
3. REINFORCING: #4 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1500 lb
Volume (Net): 0.37cu.yd
