

**Contractor: Hahn Excavating, Inc.**

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 5.2'

Floor Height: 10"

Slack: 0.7"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

3) MH Step ML-10-TDS-NCR - 10"



0 lb

Structure Total: 8351 lb

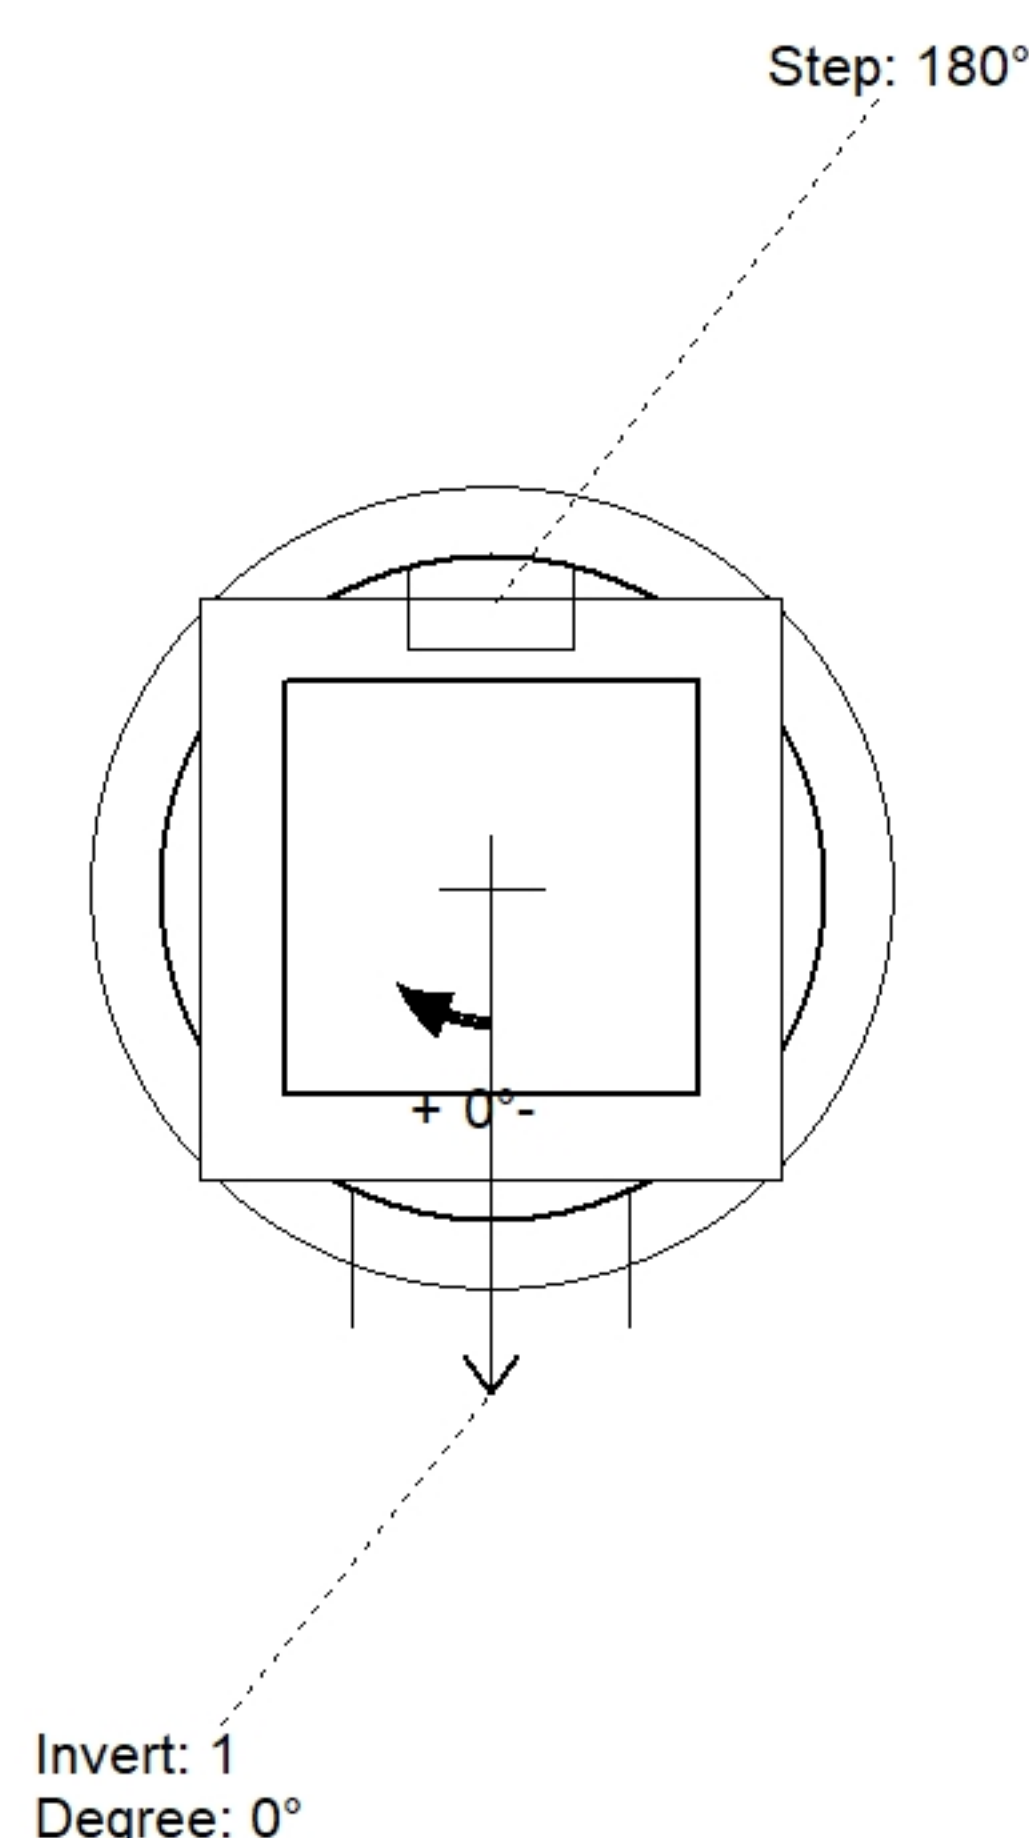

| Position | Elev    | Angle | Pipe     | Pipe OD | Hole | Connector | Up ( ) | Ref |
|----------|---------|-------|----------|---------|------|-----------|--------|-----|
| Rim      | 394.68' |       |          |         |      |           |        |     |
| Reducer  |         |       |          |         |      |           |        |     |
| Invert 1 | 389.48' | 0°    | 15" HDPE | 17.6"   | 20"  | Hole 20   | 0"     | P1  |
| Invert 2 |         |       |          |         |      |           |        |     |
| Invert 3 |         |       |          |         |      |           |        |     |
| Invert 4 |         |       |          |         |      |           |        |     |
| Invert 5 |         |       |          |         |      |           |        |     |
| Invert 6 |         |       |          |         |      |           |        |     |
| Invert 7 |         |       |          |         |      |           |        |     |
| Invert 8 |         |       |          |         |      |           |        |     |

### Default - Interior Dimensions

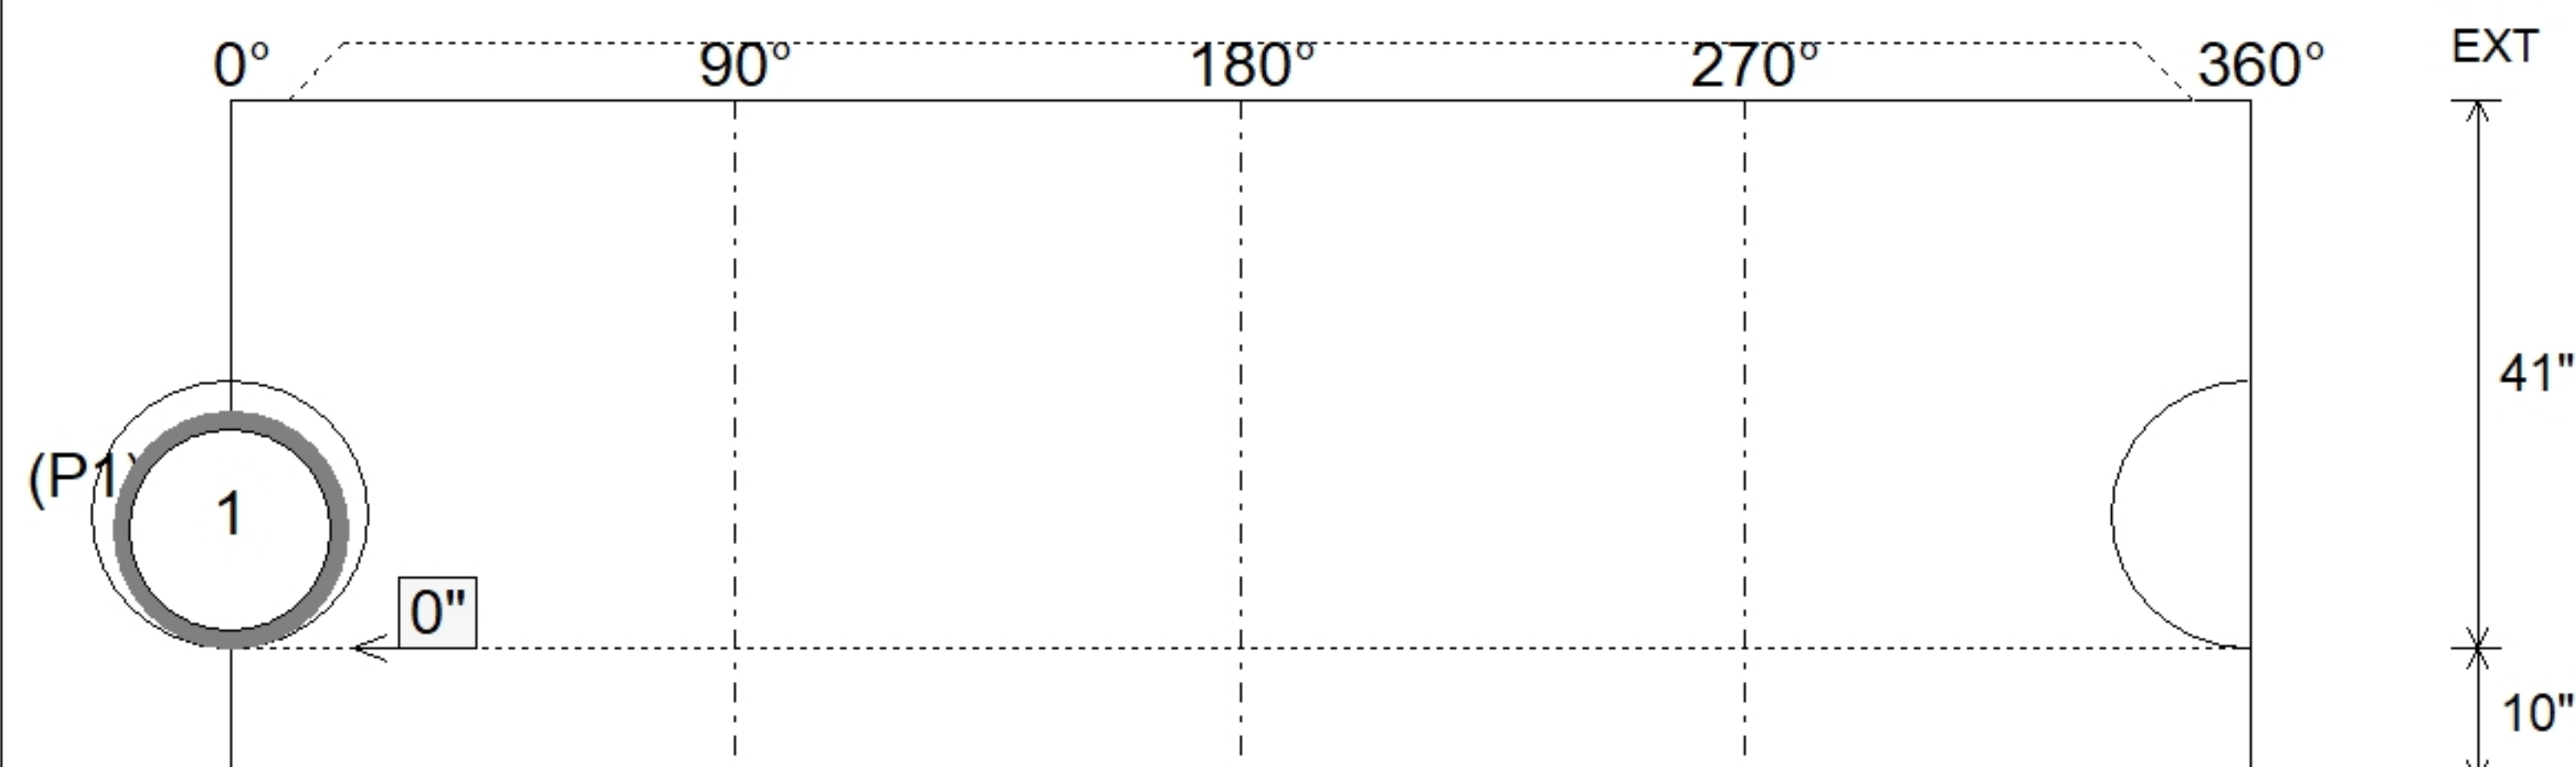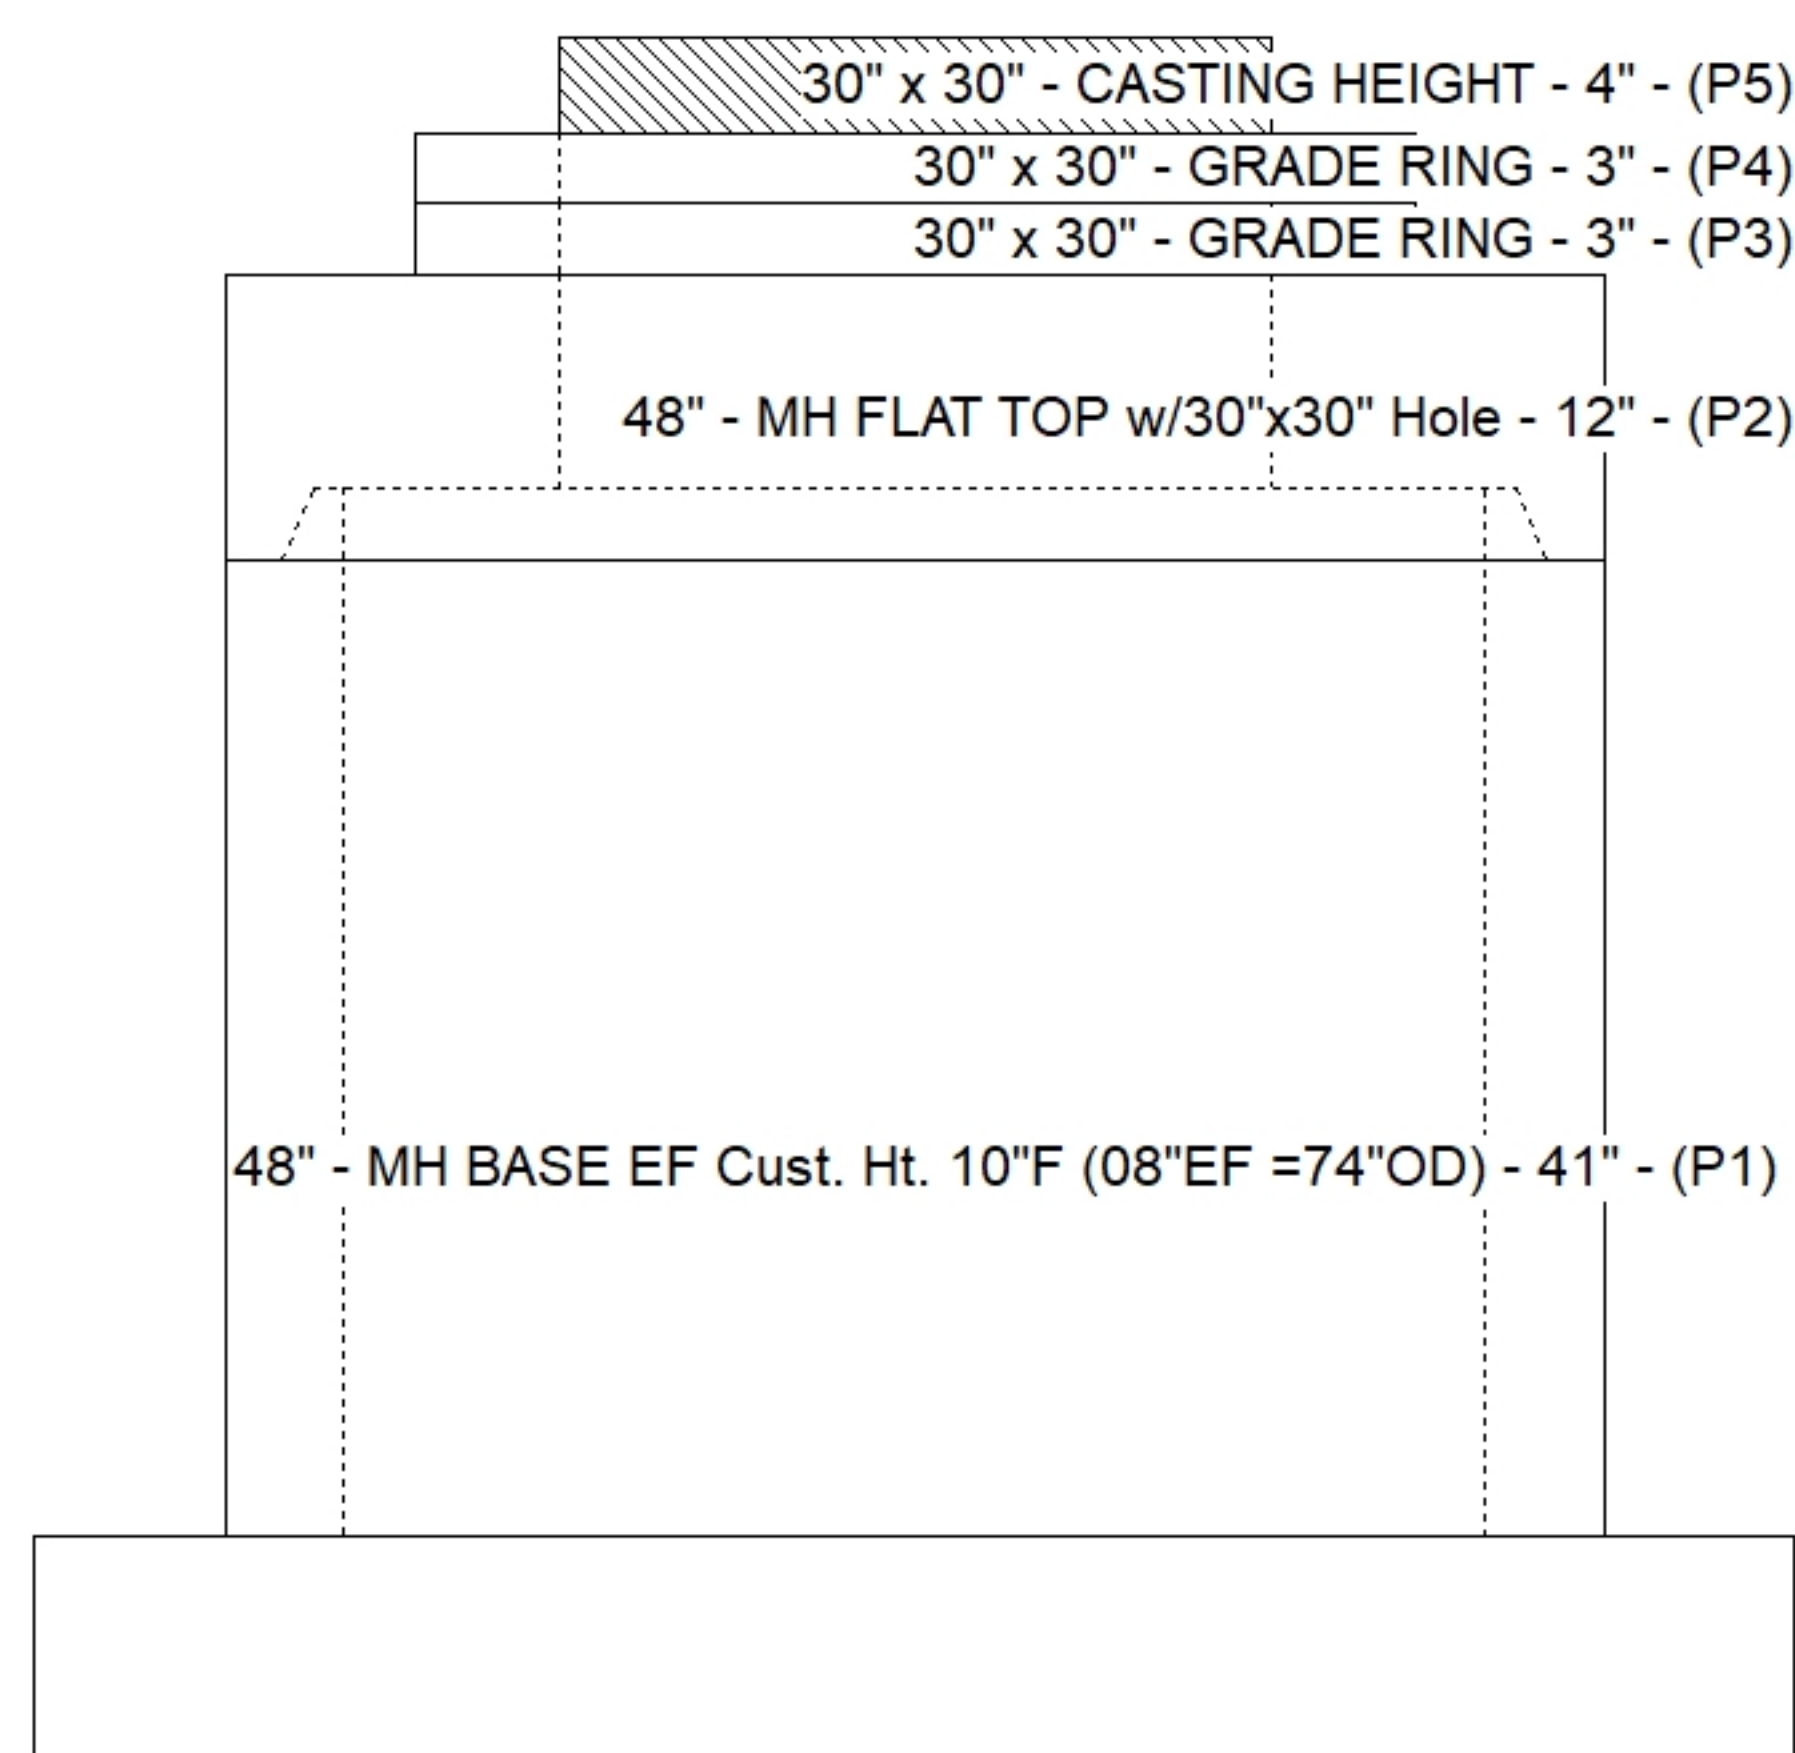

Submittal Drawing  
10/2/2026 8:53:26 AM

SUBMITTAL  
APPROVED BY:
