

Contractor: Hahn Excavating, Inc.

TECH: Jared - F

Plant: 100



Size: 48"

Rim to Invert: 6.47'

Floor Height: 10"


Slack: 1.94"

- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


5) MH Step ML-10-TDS-NCR - 10"

0 lb


Structure Total: 8975 lb

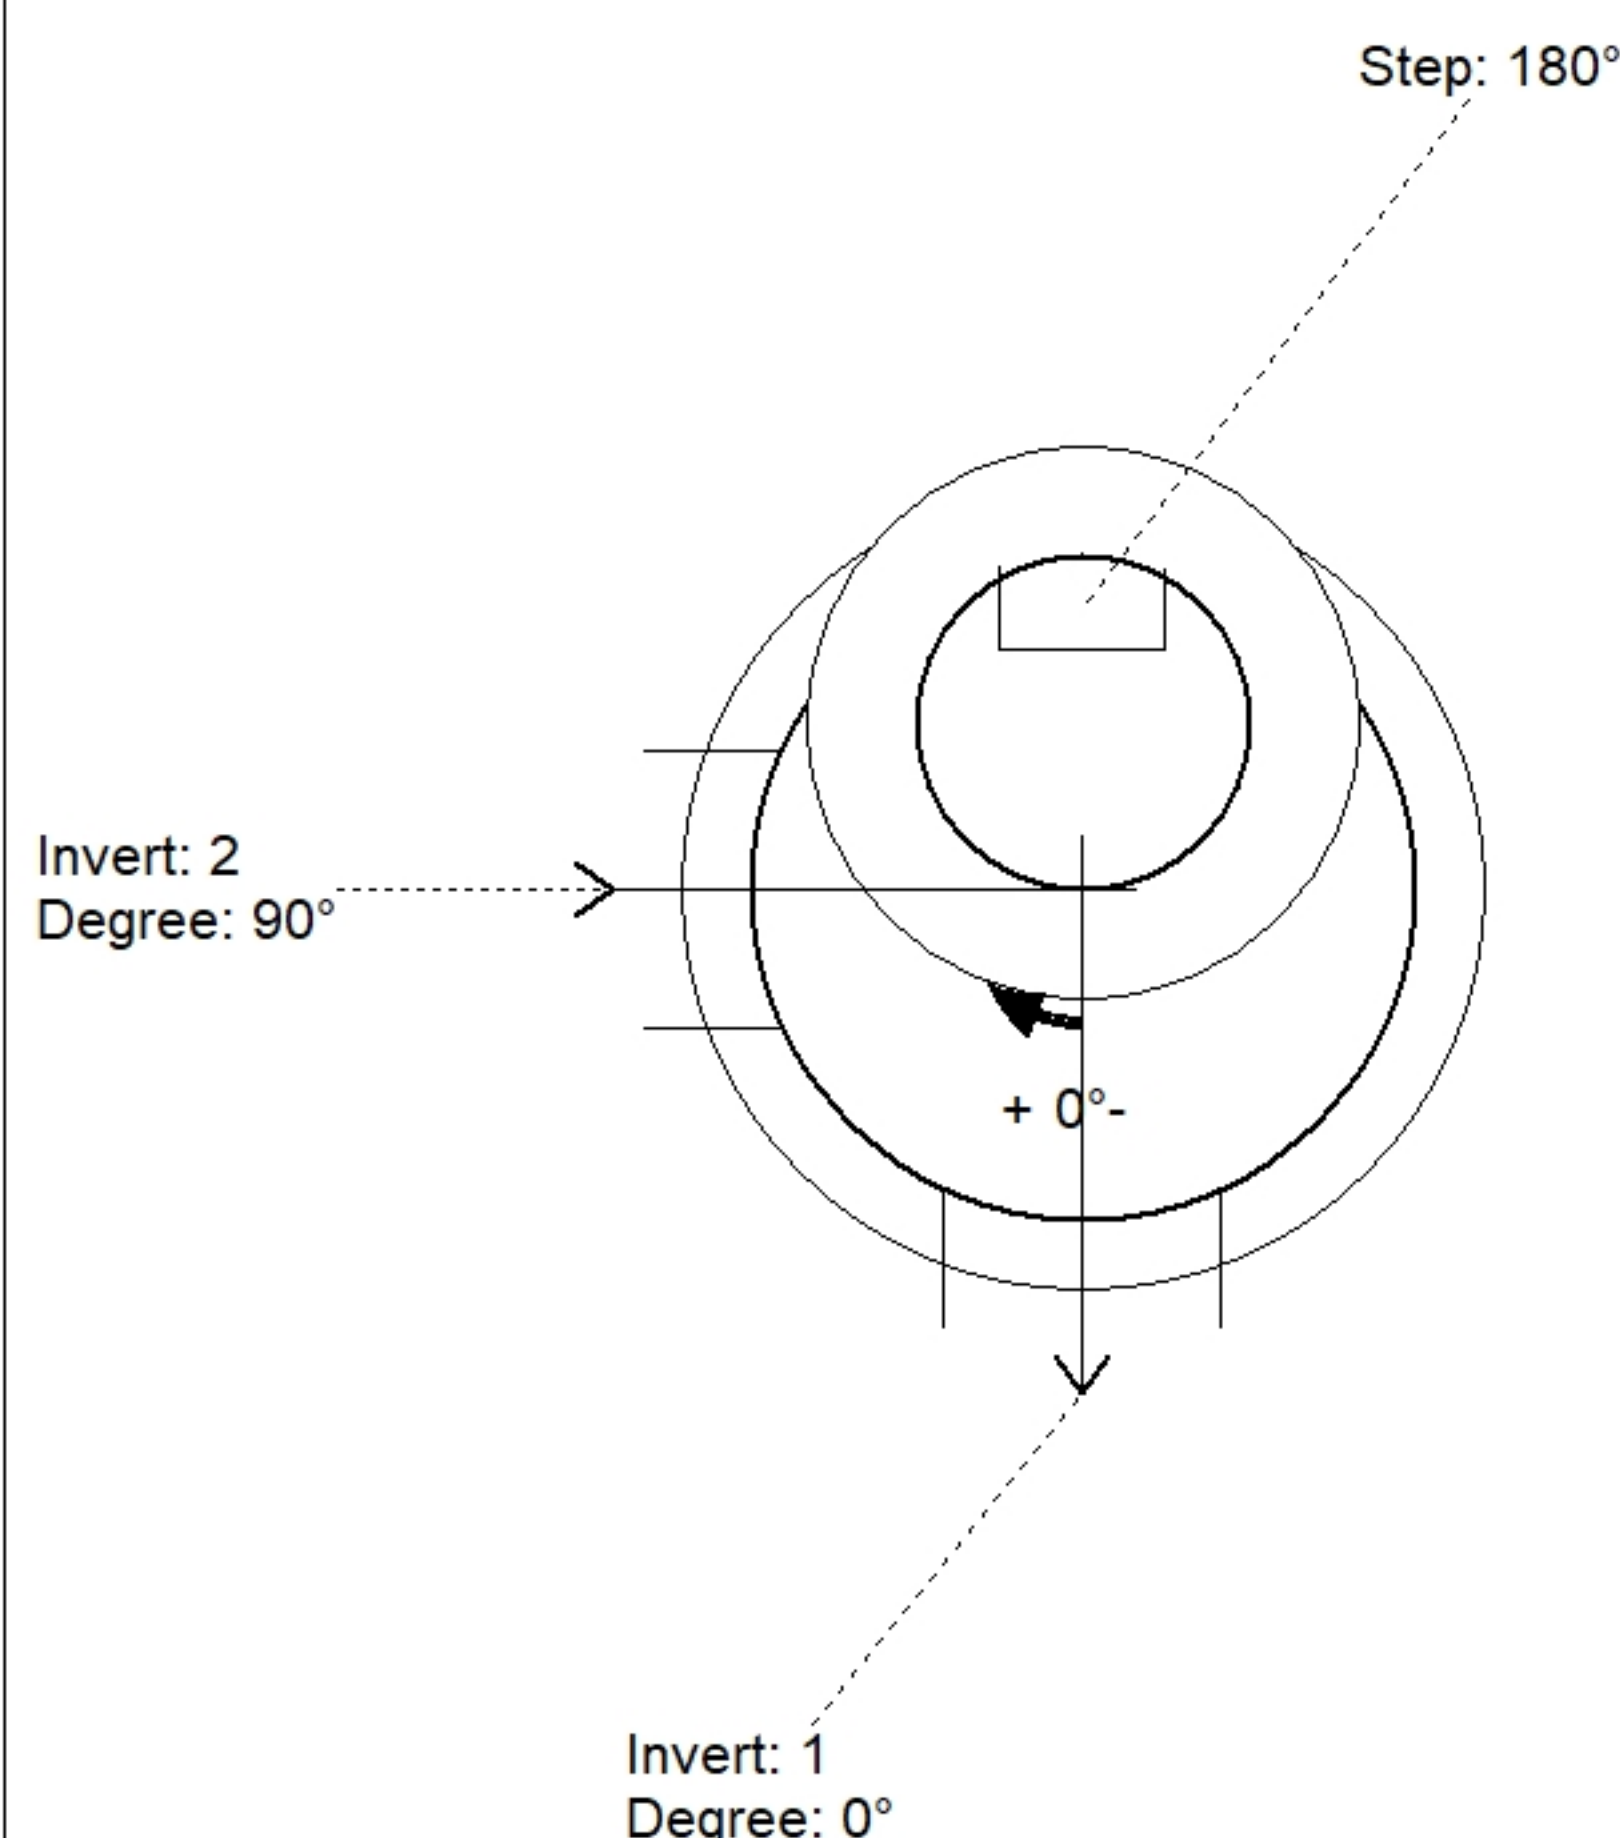

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	395.67'							
Reducer								
Invert 1	389.2'	0°	15" HDPE	17.6"	20"	Hole 20	0"	P1
Invert 2	389.3'	90°	15" HDPE	17.6"	20"	Hole 20	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

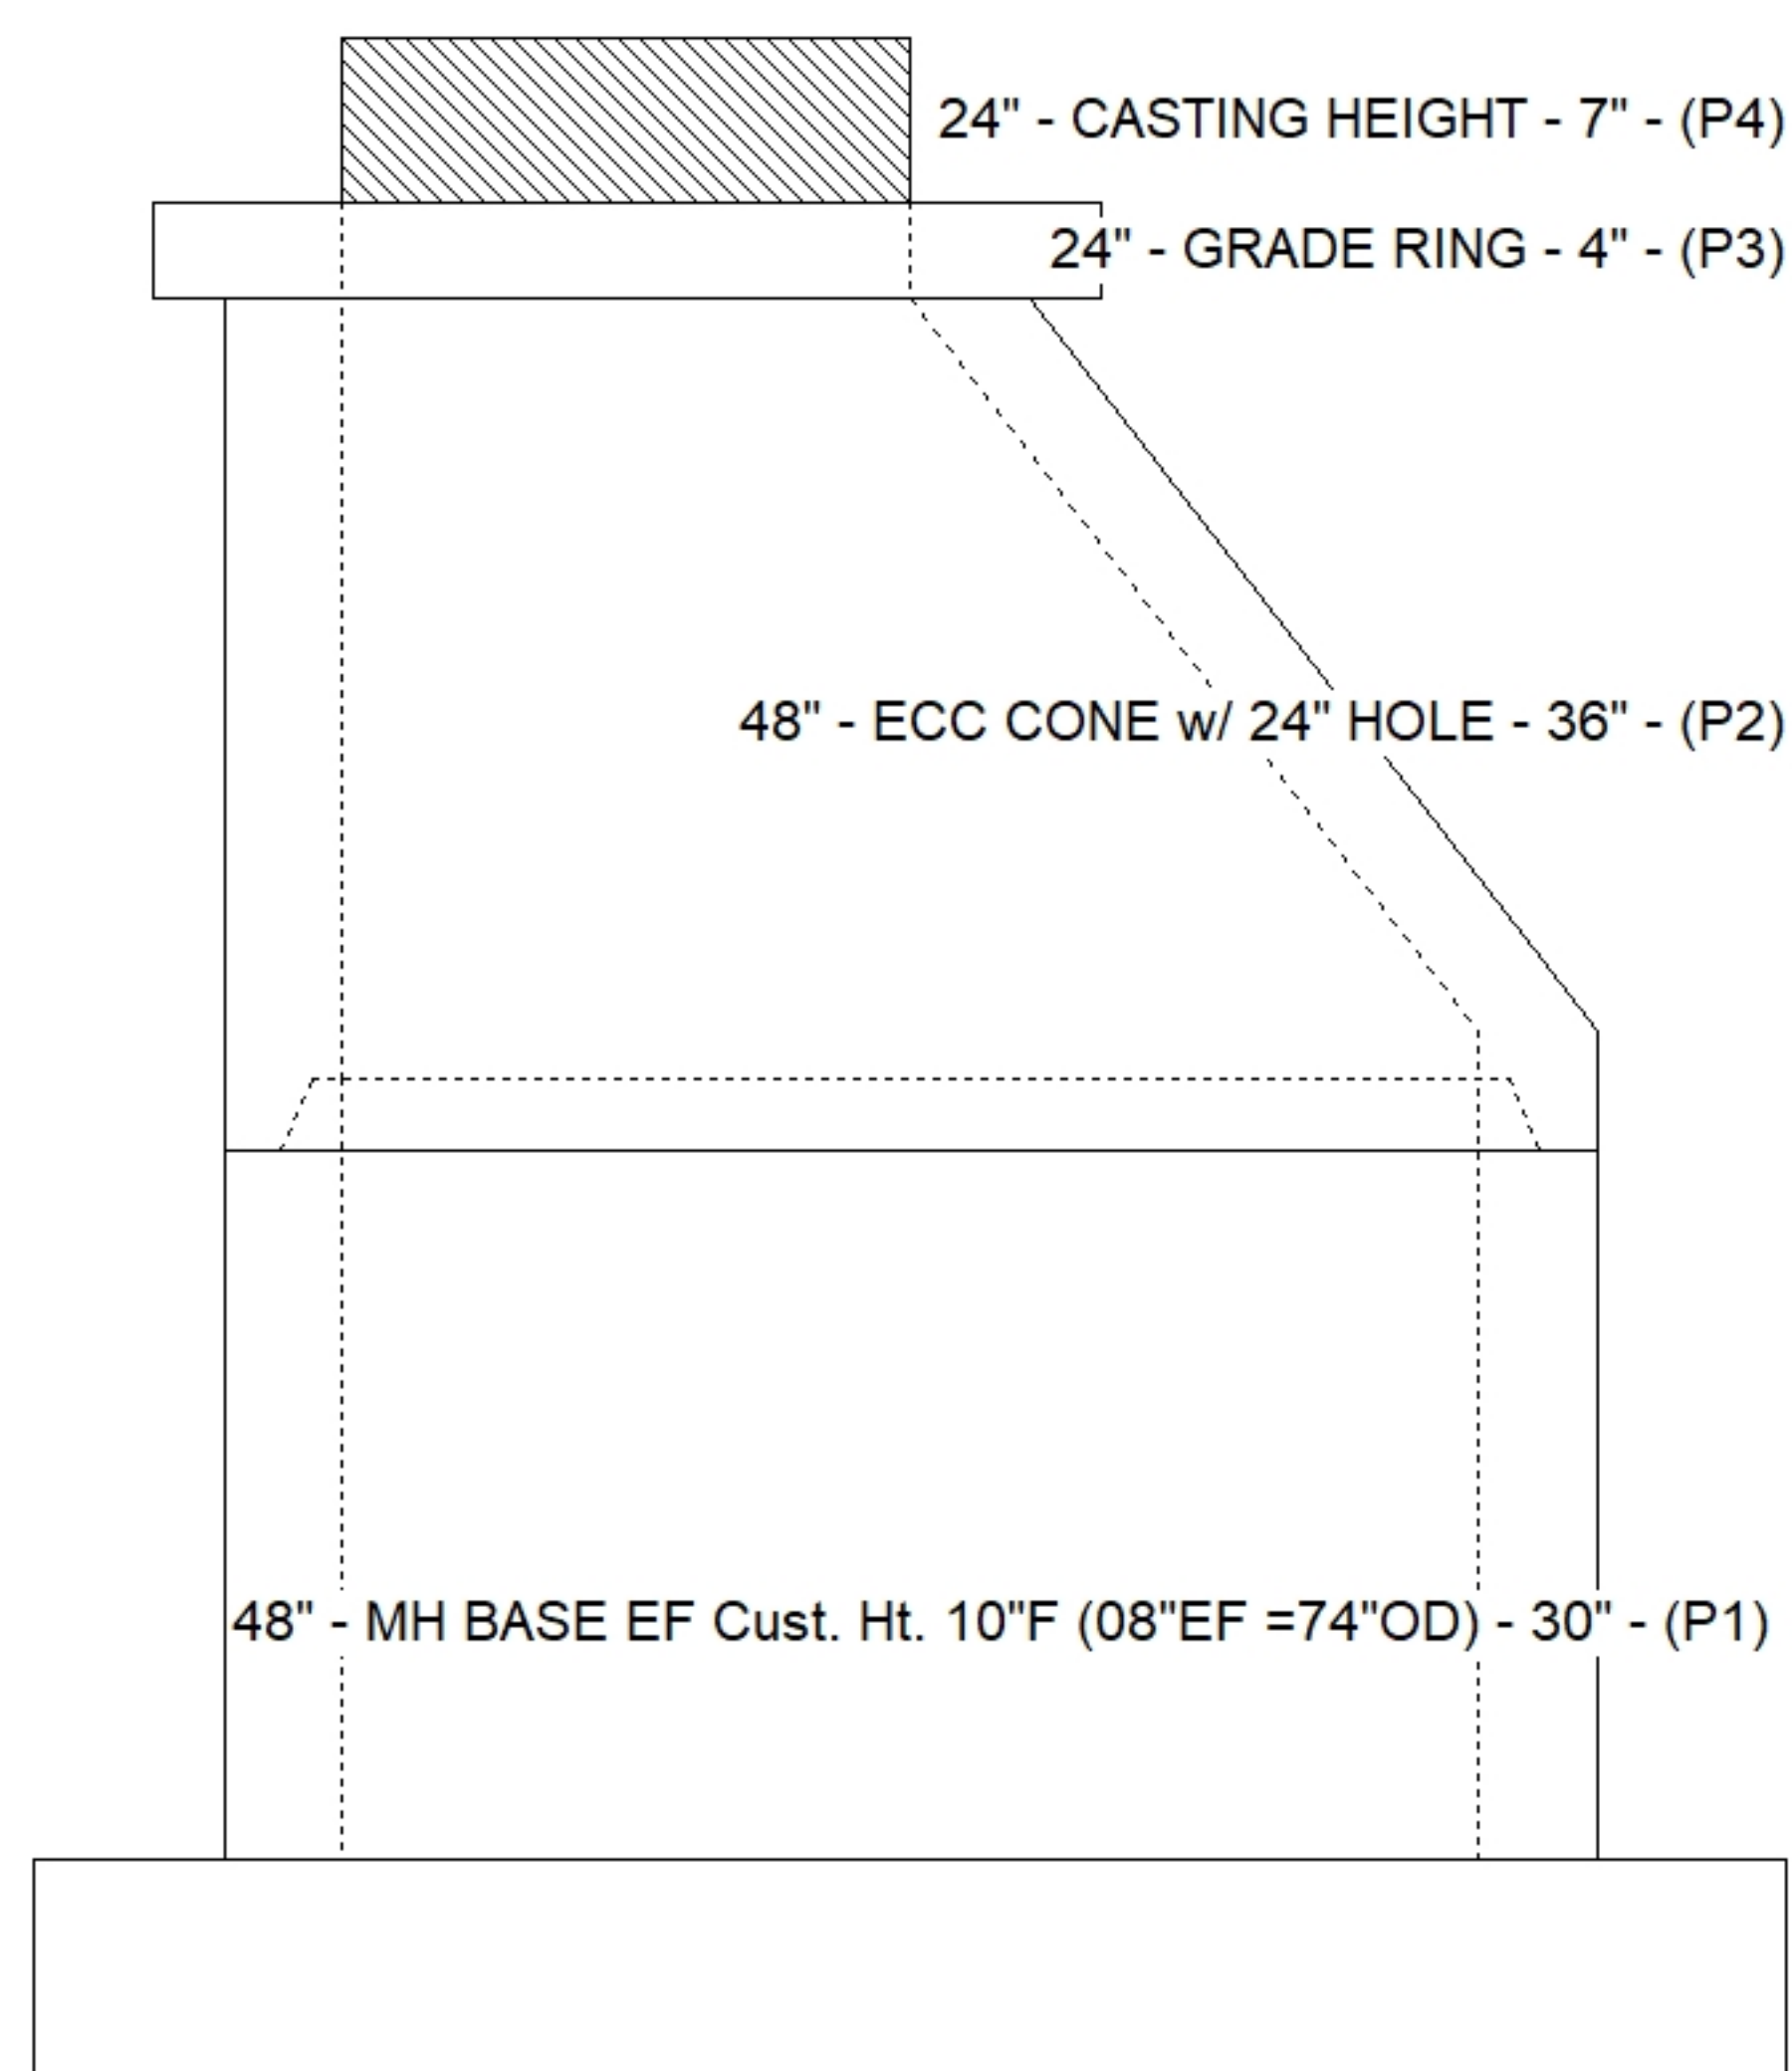

Default - Interior Dimensions

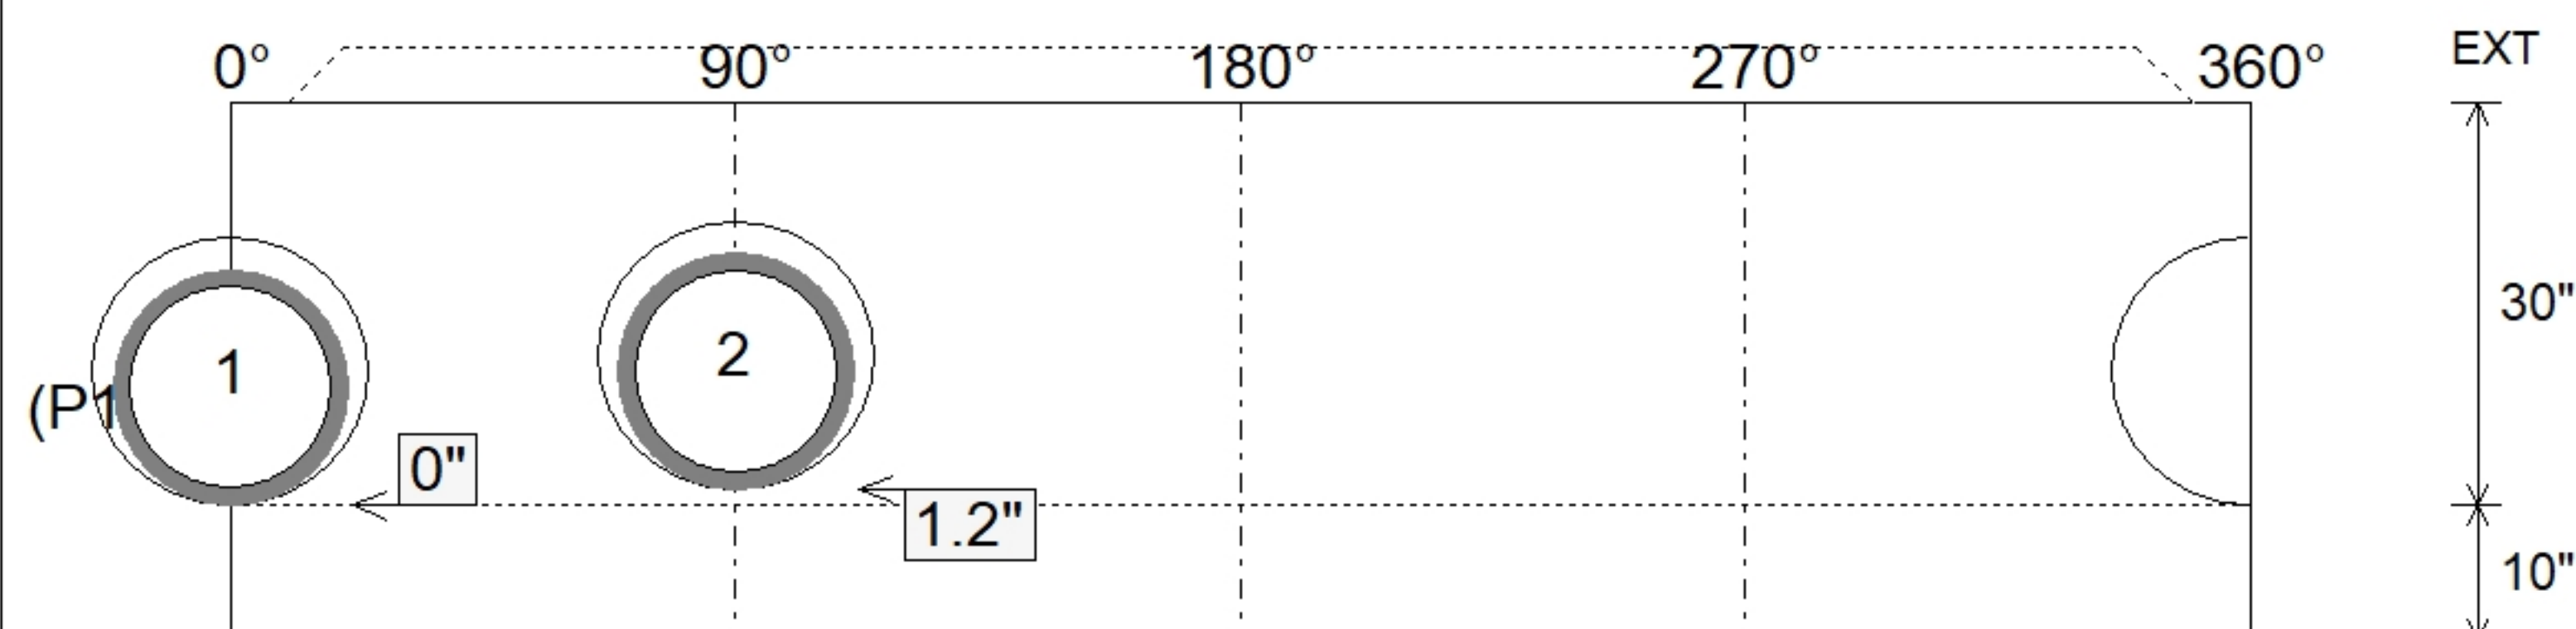

Submittal Drawing
10/2/2026 8:53:28 AM

SUBMITTAL
APPROVED BY:
