

Job Name: 26-2279 - Keenland Trace Unit 14
Job Location: Owensboro, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

7/29/2026 2:00:09 PM

Tech: Jared - F
PC: A. Chambers



Structure ID: 43 SS-MH

P2 MH048CN30X

ECC XYPEX CONE w/ 24" HOLE



- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - ECC XYPEX CONE w/ 24" HOLE - 30"
P1) 48" - MH BASE w/XYPEX - 18"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) ADMIXTURE XYPEX C-500 NF RED
1) 48" - MH INVERT CHANNEL w/XYPEX - FULL HEIGHT
1) CASTING - HOE MC-315 F/C RWRA
1) 48" - Conseal CS-102 1.00" (Double)
1) 24" - Conseal CS-102 1.00" (Double)
1) PSX - 12-08 NYLO
1) PSX - 8QRS-S NYLO
4) MH Step ML-10-TDS-NCR - 10"

0 lb
1981 lb
2519 lb
0 lb
0 lb
0 lb
1440 lb
258 lb
0 lb
0 lb
8 lb
6 lb
0 lb

6212 lb

Structure Notes: .
1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-315 F/C RWRA)
4. ADMIXTURE = XYPEX C-500 NF RED.
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total:

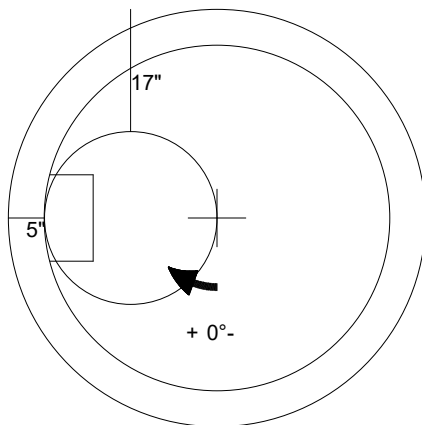

48" - ECC XYPEX CONE w/ 24" HOLE - 30" - (P2)

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 30"

Weight (Net): 1981 lb
Volume (Net): 0.51cu.yd
