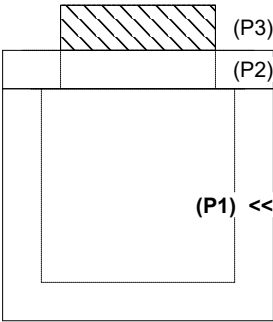
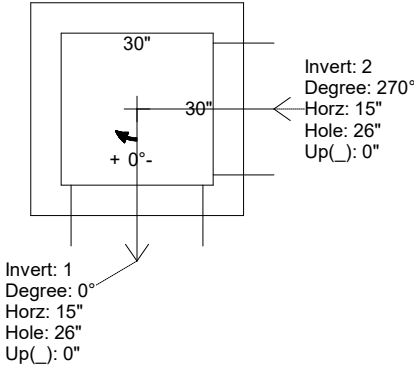
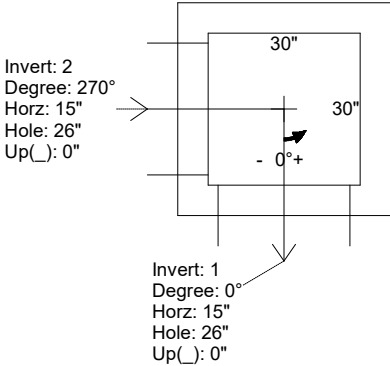
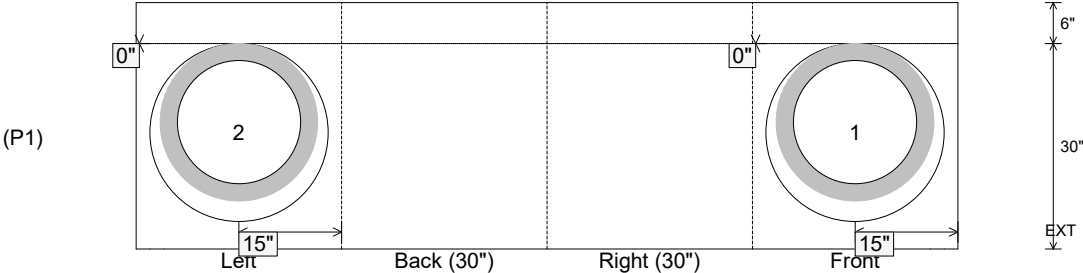


Job Name: 26-2358 - Sidewalk Lighting and Expansion - North Gibson School Corp		Plant: 100	Tech: Jared - F							
Job Location: Princeton, IN Contractor: Hahn Excavating, Inc.		7/14/2026 11:22:52 AM	PC: E. Bradley							
Structure ID: Str. 2 ST-JB										
P1 BX3030-06VH		BOX BASE 6inW, 6inF F/n								
P3) 24" - CASTING HEIGHT - 7" P2) 30" x 30" - CB FLAT TOP 6"W w/24"Hole F/F - 6" P1) 30" x 30" - BOX BASE 6inW, 6inF F/n - 30" 1) CASTING - HOE MC-315 F/C Storm 1) 30" x 30" - Conseal CS-102 1.00" 1) 24" - Conseal CS-102 1.00" 2) Hole - 26		0 lb 660 lb 2529 lb 258 lb 0 lb 0 lb 0 lb ----- Structure Total: 3447 lb Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE MC-315 F/C STORM). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W. - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.								
Rim: 492.6'		Rim to Invert: 3.34'	Slack: -0.42"	Sump: 2.5"	Step Position:					
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	489.26'	0°	21"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"
Invert 2	489.26'	270°	21"	18" RCP B WALL	23"	Hole 26	26"	26"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
		RIGHT-SIDE UP VIEW (int. dimensions)		UPSIDE-DOWN VIEW (int. dimenions)						
										
		INSIDE WALL DIMENSIONS								
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 30" Height (Ext): 36"		Weight (Net): 2529 lb Volume (Net): 0.65cu.yd		
