

Contractor: Hahn Excavating, Inc.

TECH: Jared - F

Plant: 100



Size: 30" x 30"

Rim to Invert: 3.34'

Floor Height: 6"


Slack: -0.42"

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.



0 lb
660 lb
2529 lb
258 lb
0 lb
0 lb
0 lb

Structure Total: 3447 lb

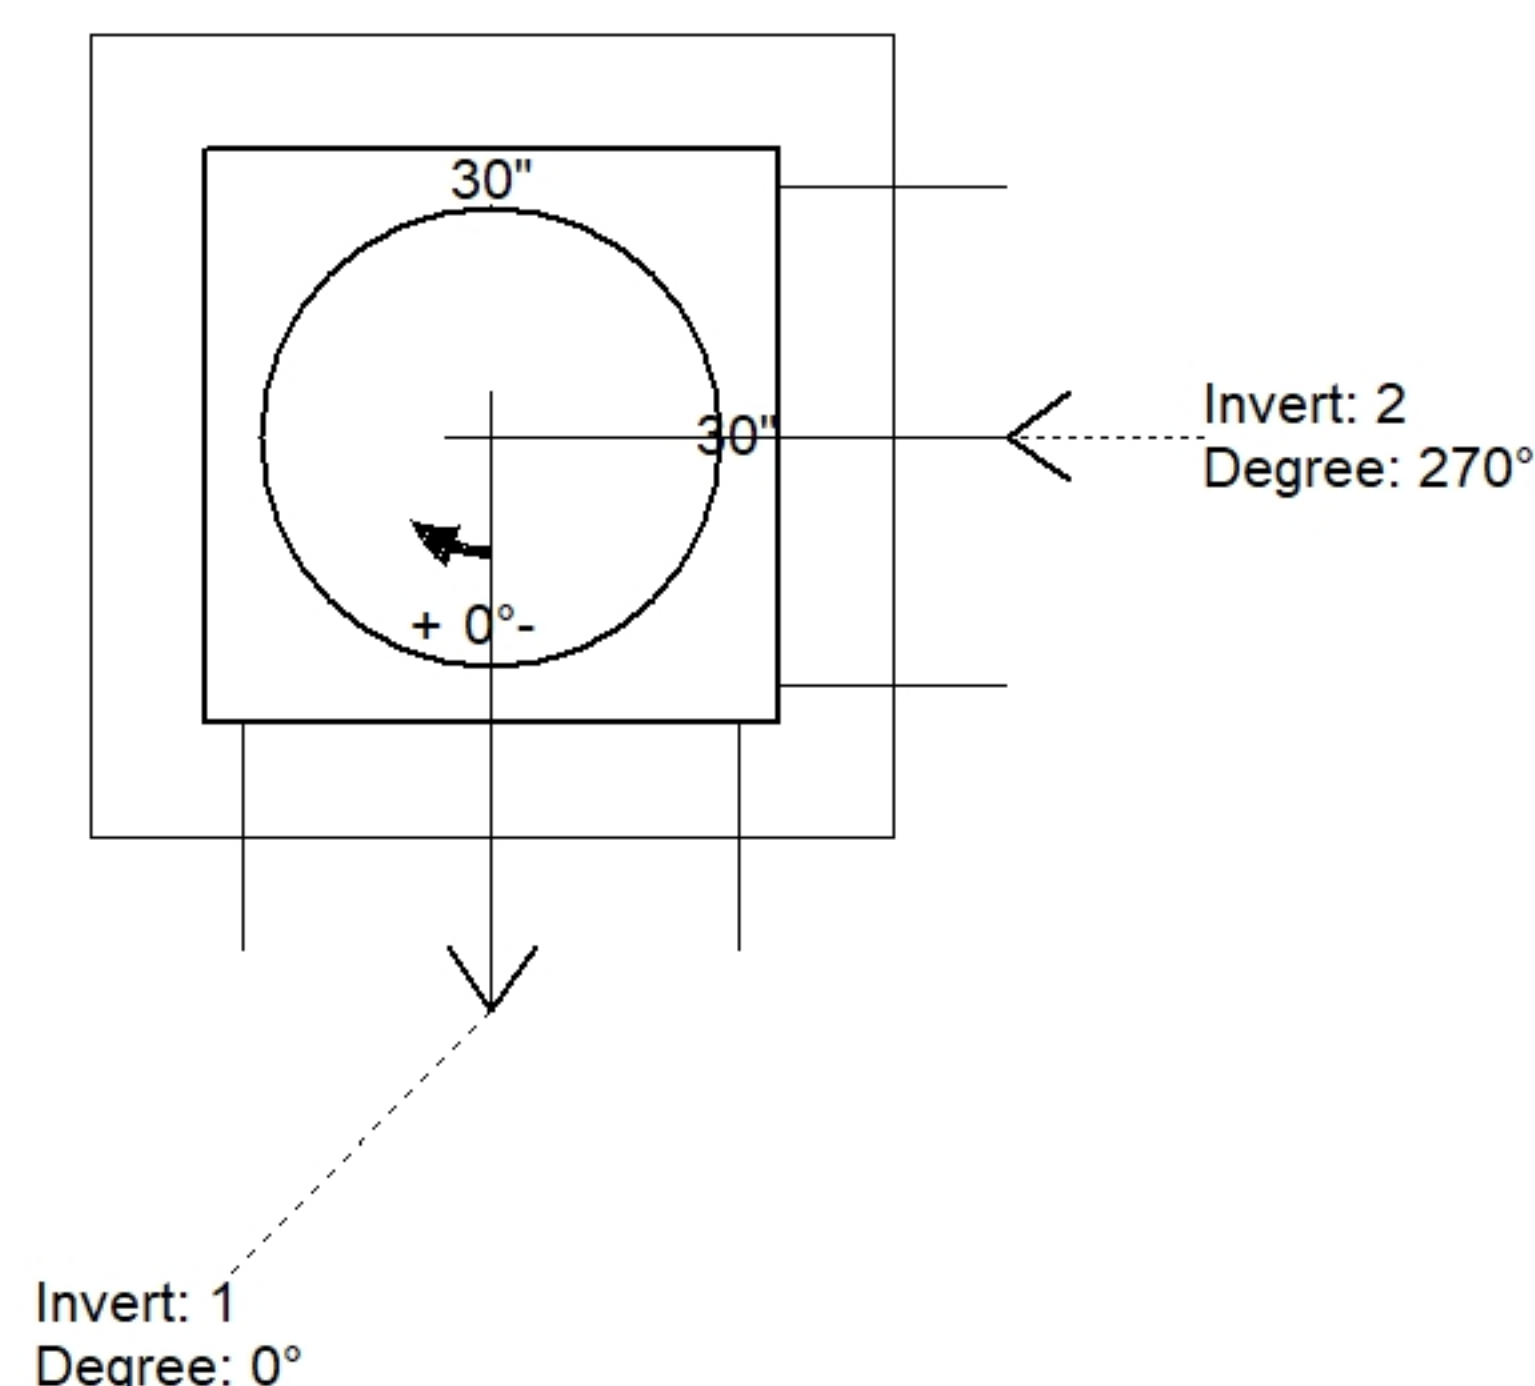

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	492.6'							
Reducer								
Invert 1	489.26'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	489.26'	270°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

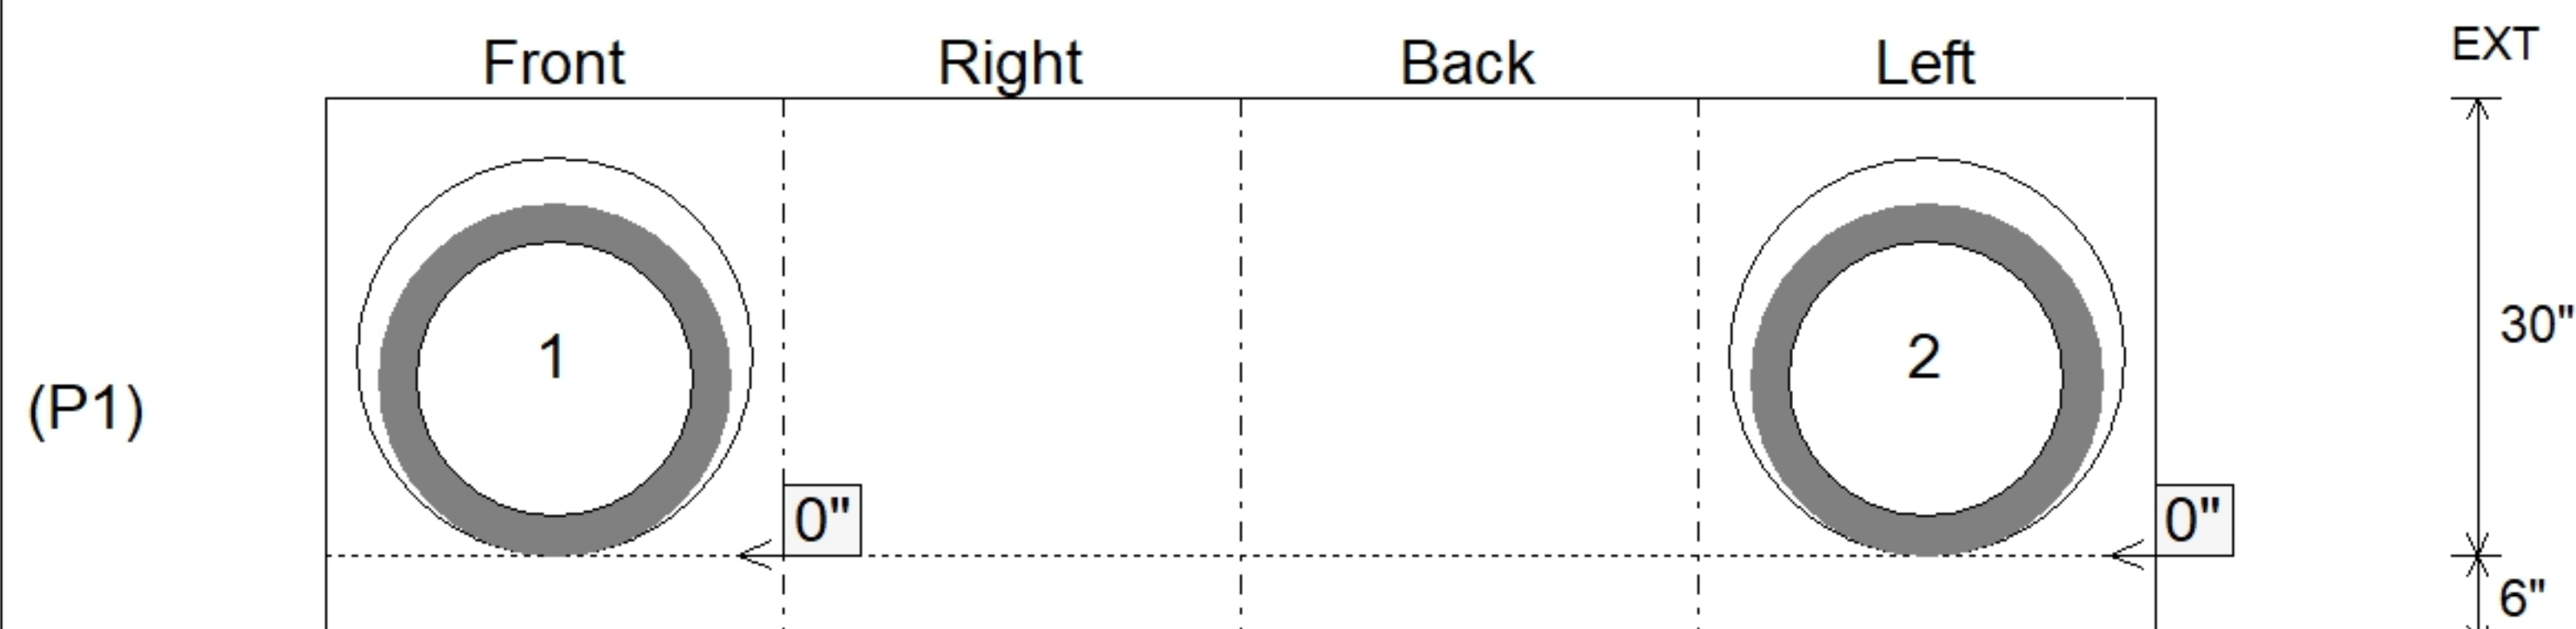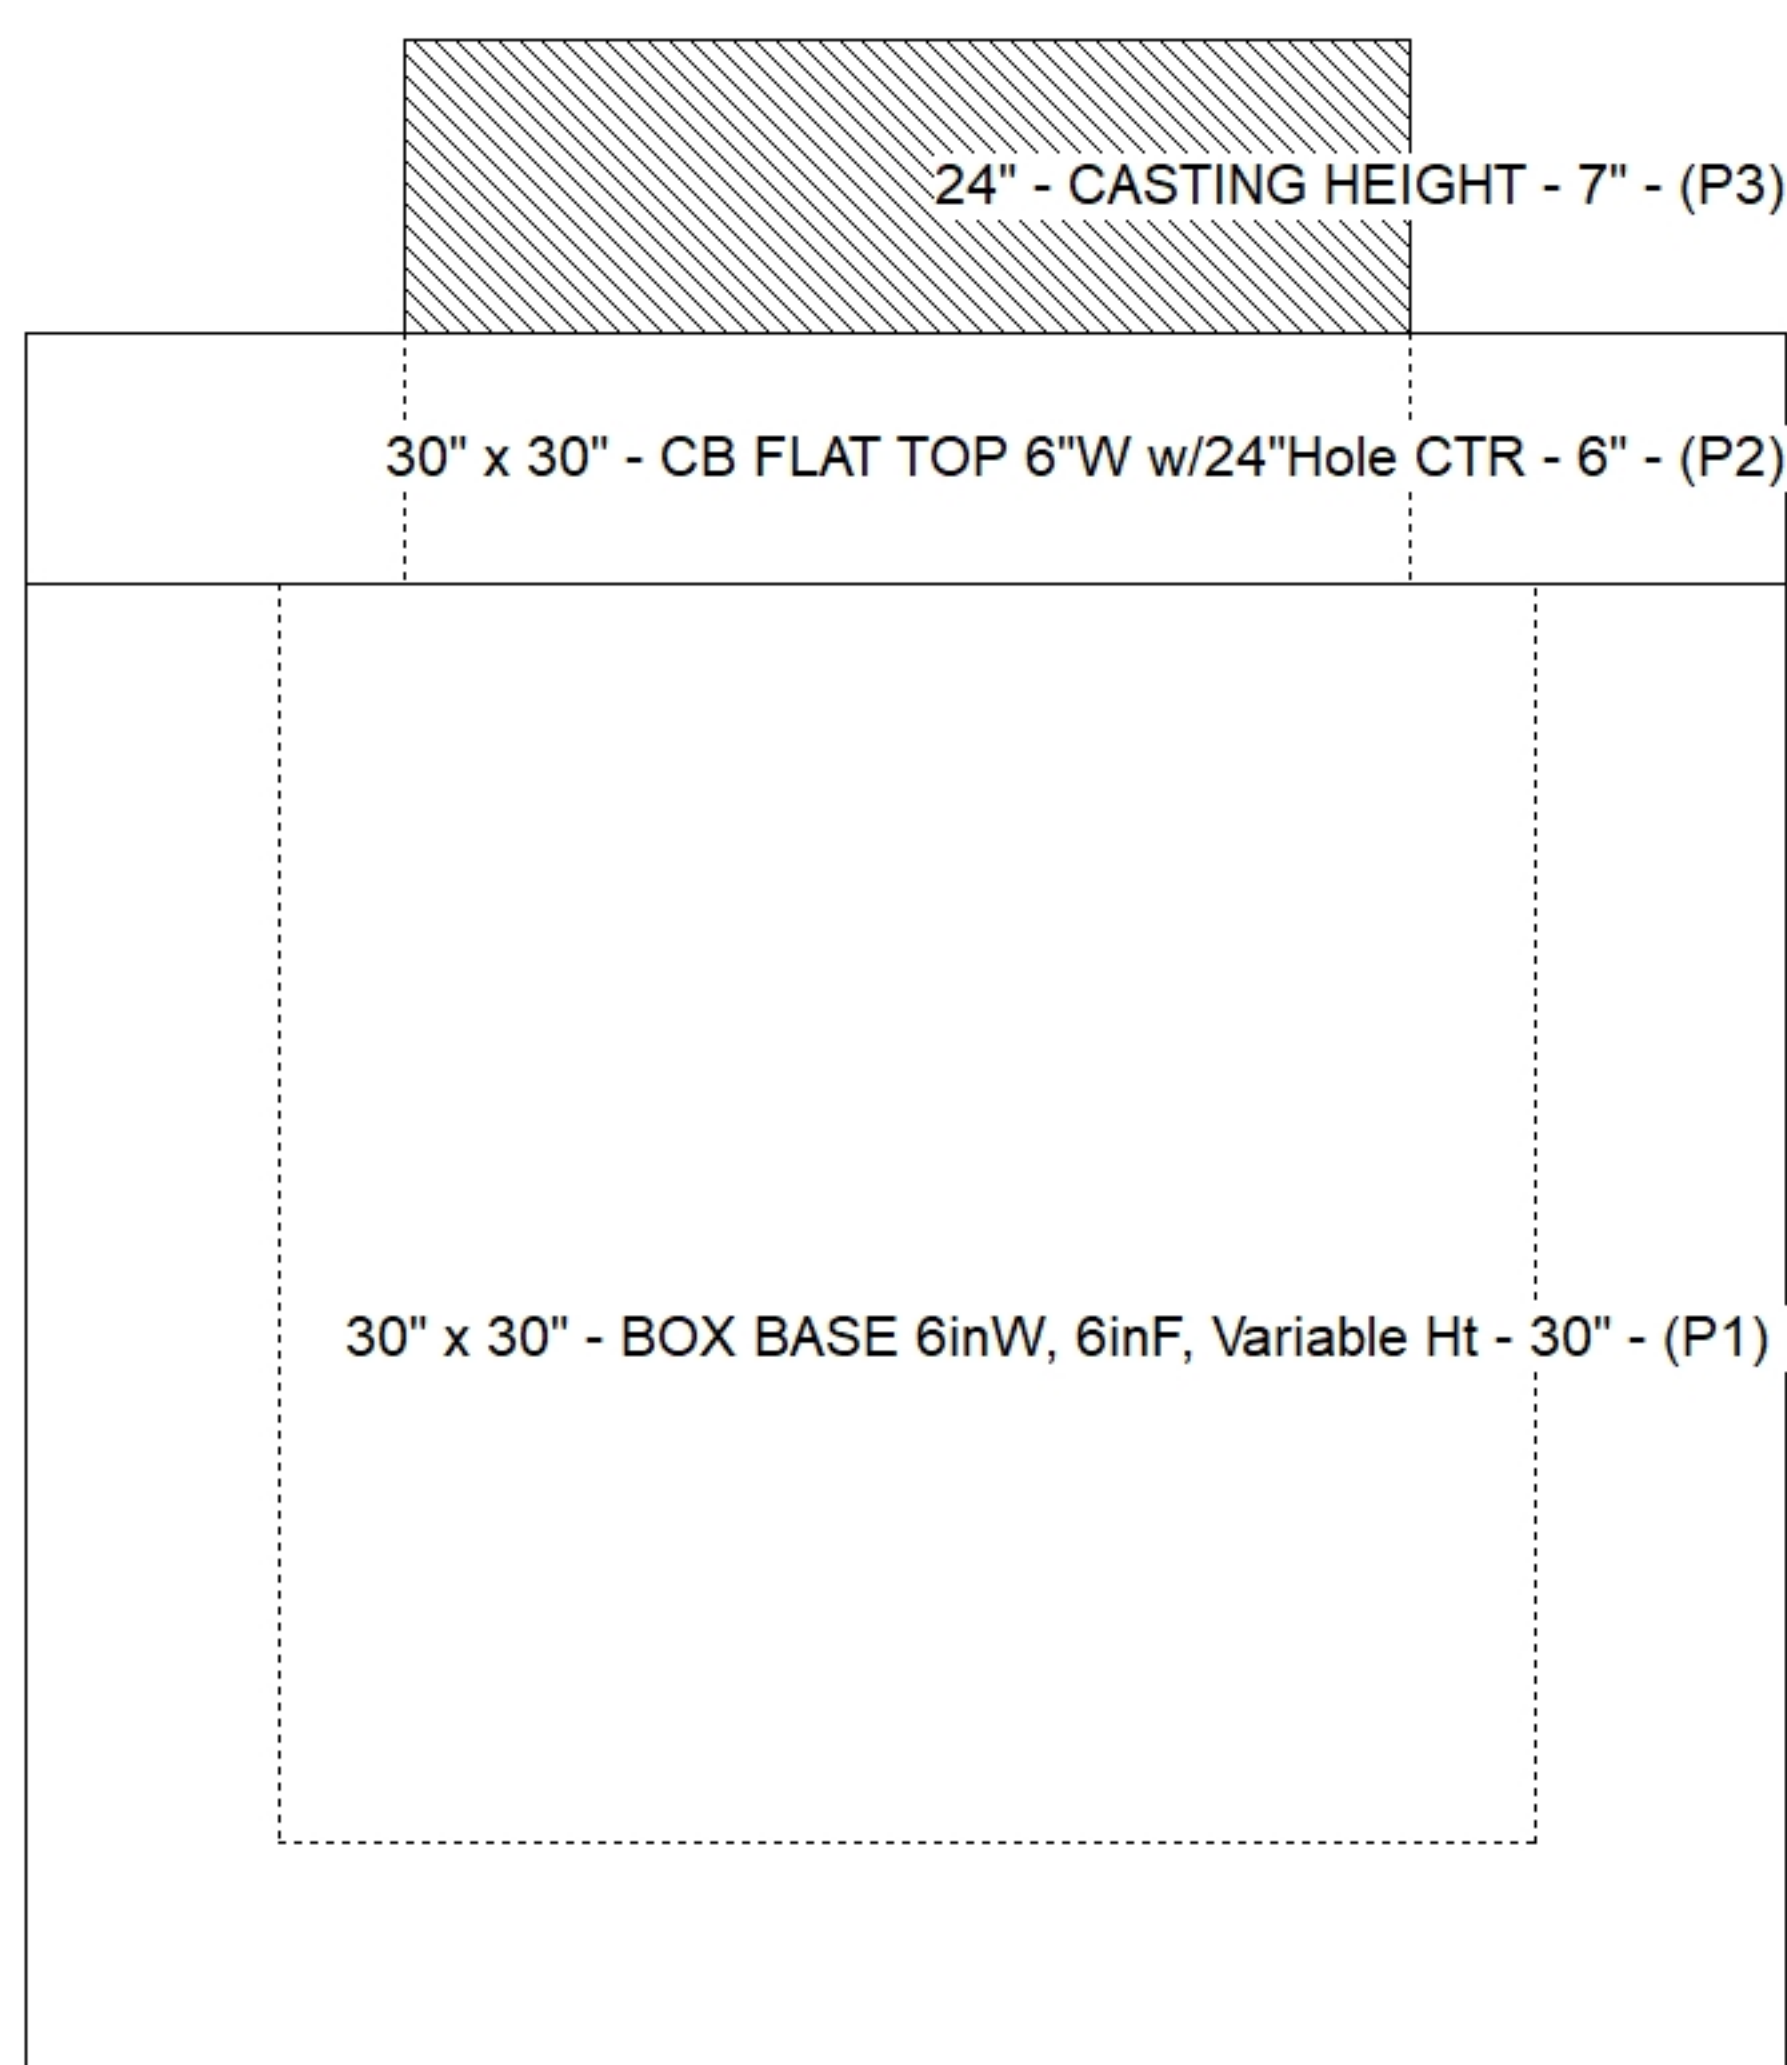

Submittal Drawing
7/15/2026 10:25:05 AM

SUBMITTAL
APPROVED BY:
