

Job Name: 26-2370 - Greystone Subd.
Job Location: Madisonville, KY
Contractor: Steve Pleasant Excavating, LLC

Plant: 100
5/26/2026 12:09:36 PM

Tech: Jared - F
PC: E. Bradley



Structure ID: 5 SS-MH


P3 GR4

GRADE RING

- P4) 24" - CASTING HEIGHT - 7"
P3) 24" - GRADE RING - 4"
P2) 48" - ECC CONE w/ 24" HOLE - 42"
P1) 48" - MH BASE - 30"
1) 48" - MH INVERT CHANNEL - FULL HEIGHT
1) JOINT WRAP - 12" WD x 048" MAC WRAP
1) Inflow Dish FOR MC-315
1) CASTING - HOE MC-315 F/C Sanitary
1) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 12-08 NYLO
2) PSX - 12-06 NYLO
6) MH Step ML-10-TDS-NCR - 10"

0 lb	Structure Notes:
270 lb	1. PER ASTM C478 SPECIFICATIONS.
3200 lb	2. CONCRETE = 4,000 PSI AT 28 DAYS.
3234 lb	3. CASTING BY ICAST (HOE MC-315 F/C "SANITARY").
1440 lb	
0 lb	REINFORCING PER ASTM A615 (GRADE 60).
2 lb	- CONE (As .12)
258 lb	- RISER/WALLS (As .12)
0 lb	- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.
0 lb	
16 lb	
16 lb	
0 lb	


Structure Total:	8436 lb

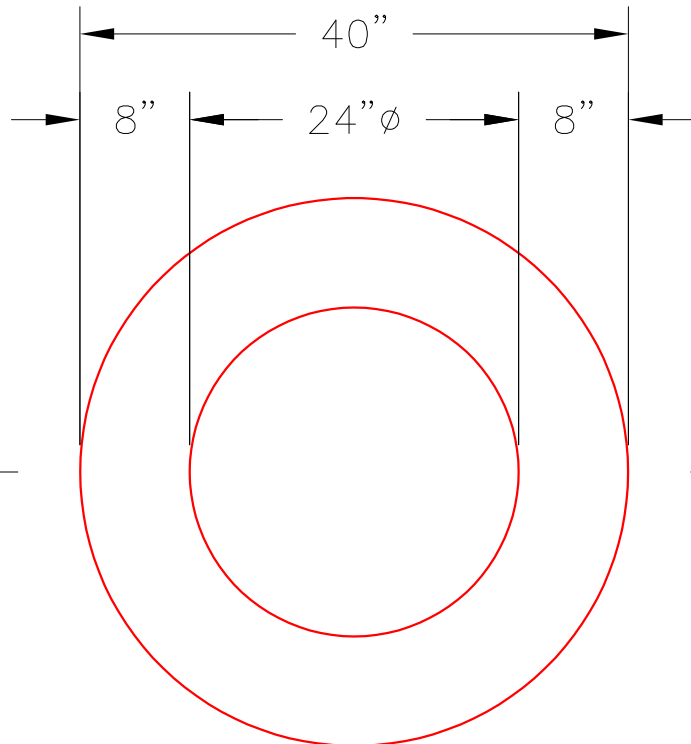


PLAN VIEW

NOTES:

- GRADE RINGS MEET OR EXCEED THE FOLLOWING SPECIFICATIONS:
 - CONCRETE: 4,000 PSI @ 28 DAYS.
 - REINFORCING: (1) #3 HOOP CENTERED (GRADE 60)



SECTION A-A

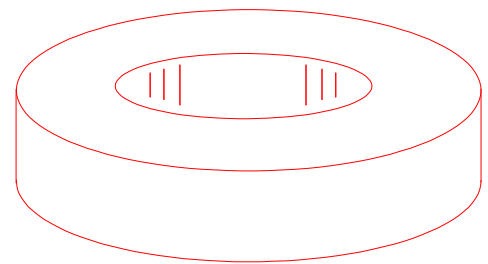

ISOMETRIC VIEW

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 4"

Weight (Net): 270 lb
Volume (Net): 0.07cu.yd
