

Contractor: Hahn Excavating, Inc.

TECH: Jared - F

Plant: 100



Slack: 0.1"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P4) 34" x 34" - CASTING HEIGHT - 3"
P3) 48" - MH FLAT TOP w/34"x34" Hole - 12"
P2) 48" - MH RISER - 12"
P1) 48" - MH BASE Custom Ht - 63"
1) CASTING - HOE 595 F/G
2) 48" - Conseal CS-102 1.00"
2) Hole - 26
1) Hole - 12
5) MH Step ML-10-TDS-NCR - 10"

0 lb
1194 lb
838 lb
5217 lb
376 lb
0 lb
0 lb
0 lb
0 lb


Structure Total: 7625 lb

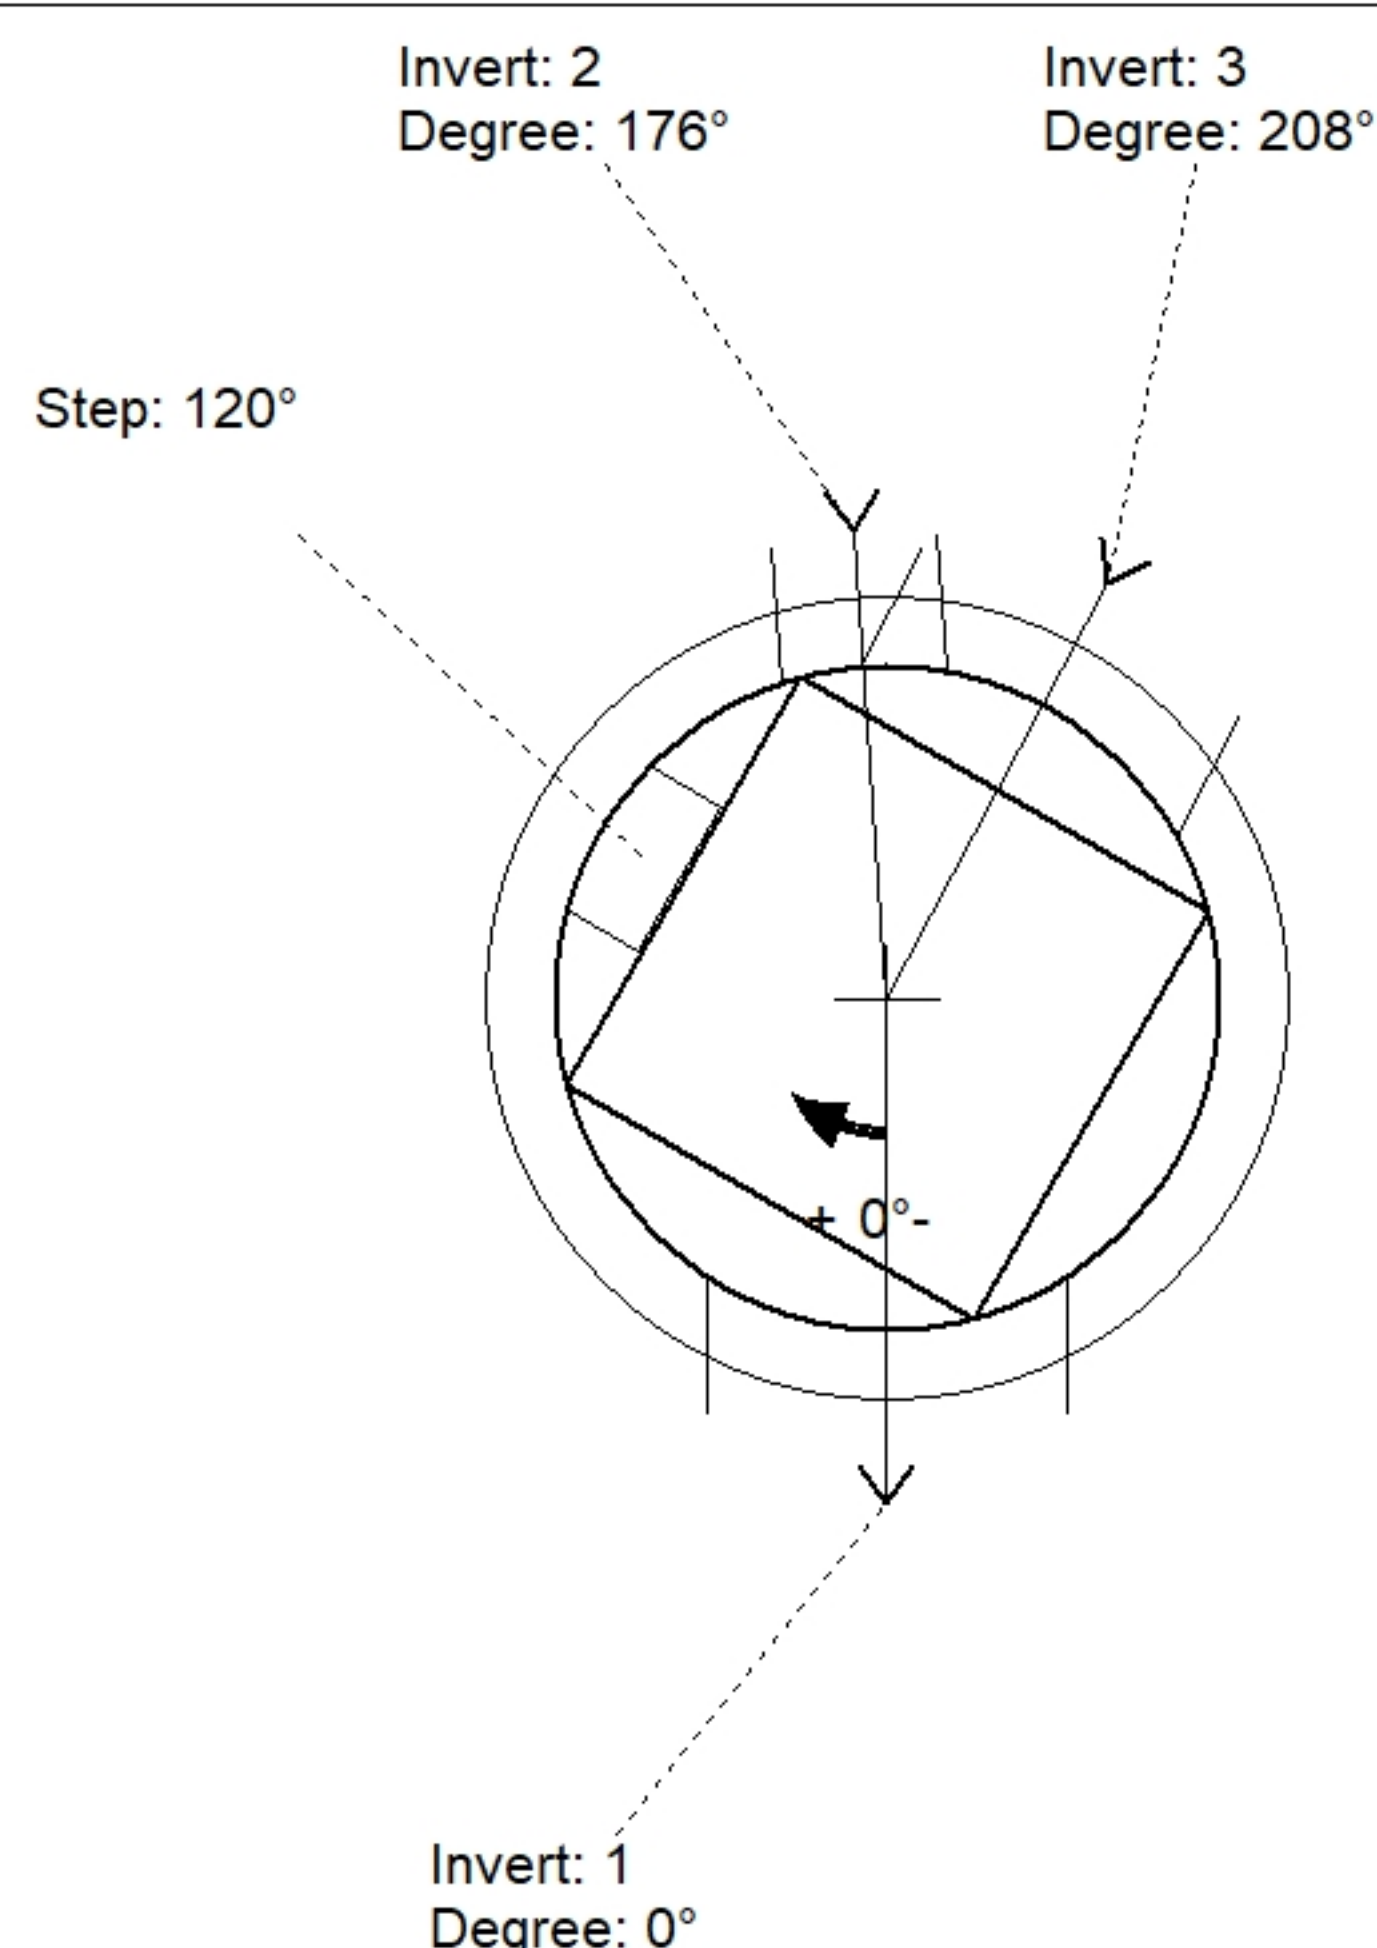

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	380.13'							
Reducer								
Invert 1	372.83'	0°	18" RCP B WALL	23"	26"	Hole 26	0"	P1
Invert 2	372.83'	176°	8" VCP	9.8"	12"	Hole 12	1.515"	P1
Invert 3	375.38'	208°	18" RCP B WALL	23"	26"	Hole 26	30.6"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

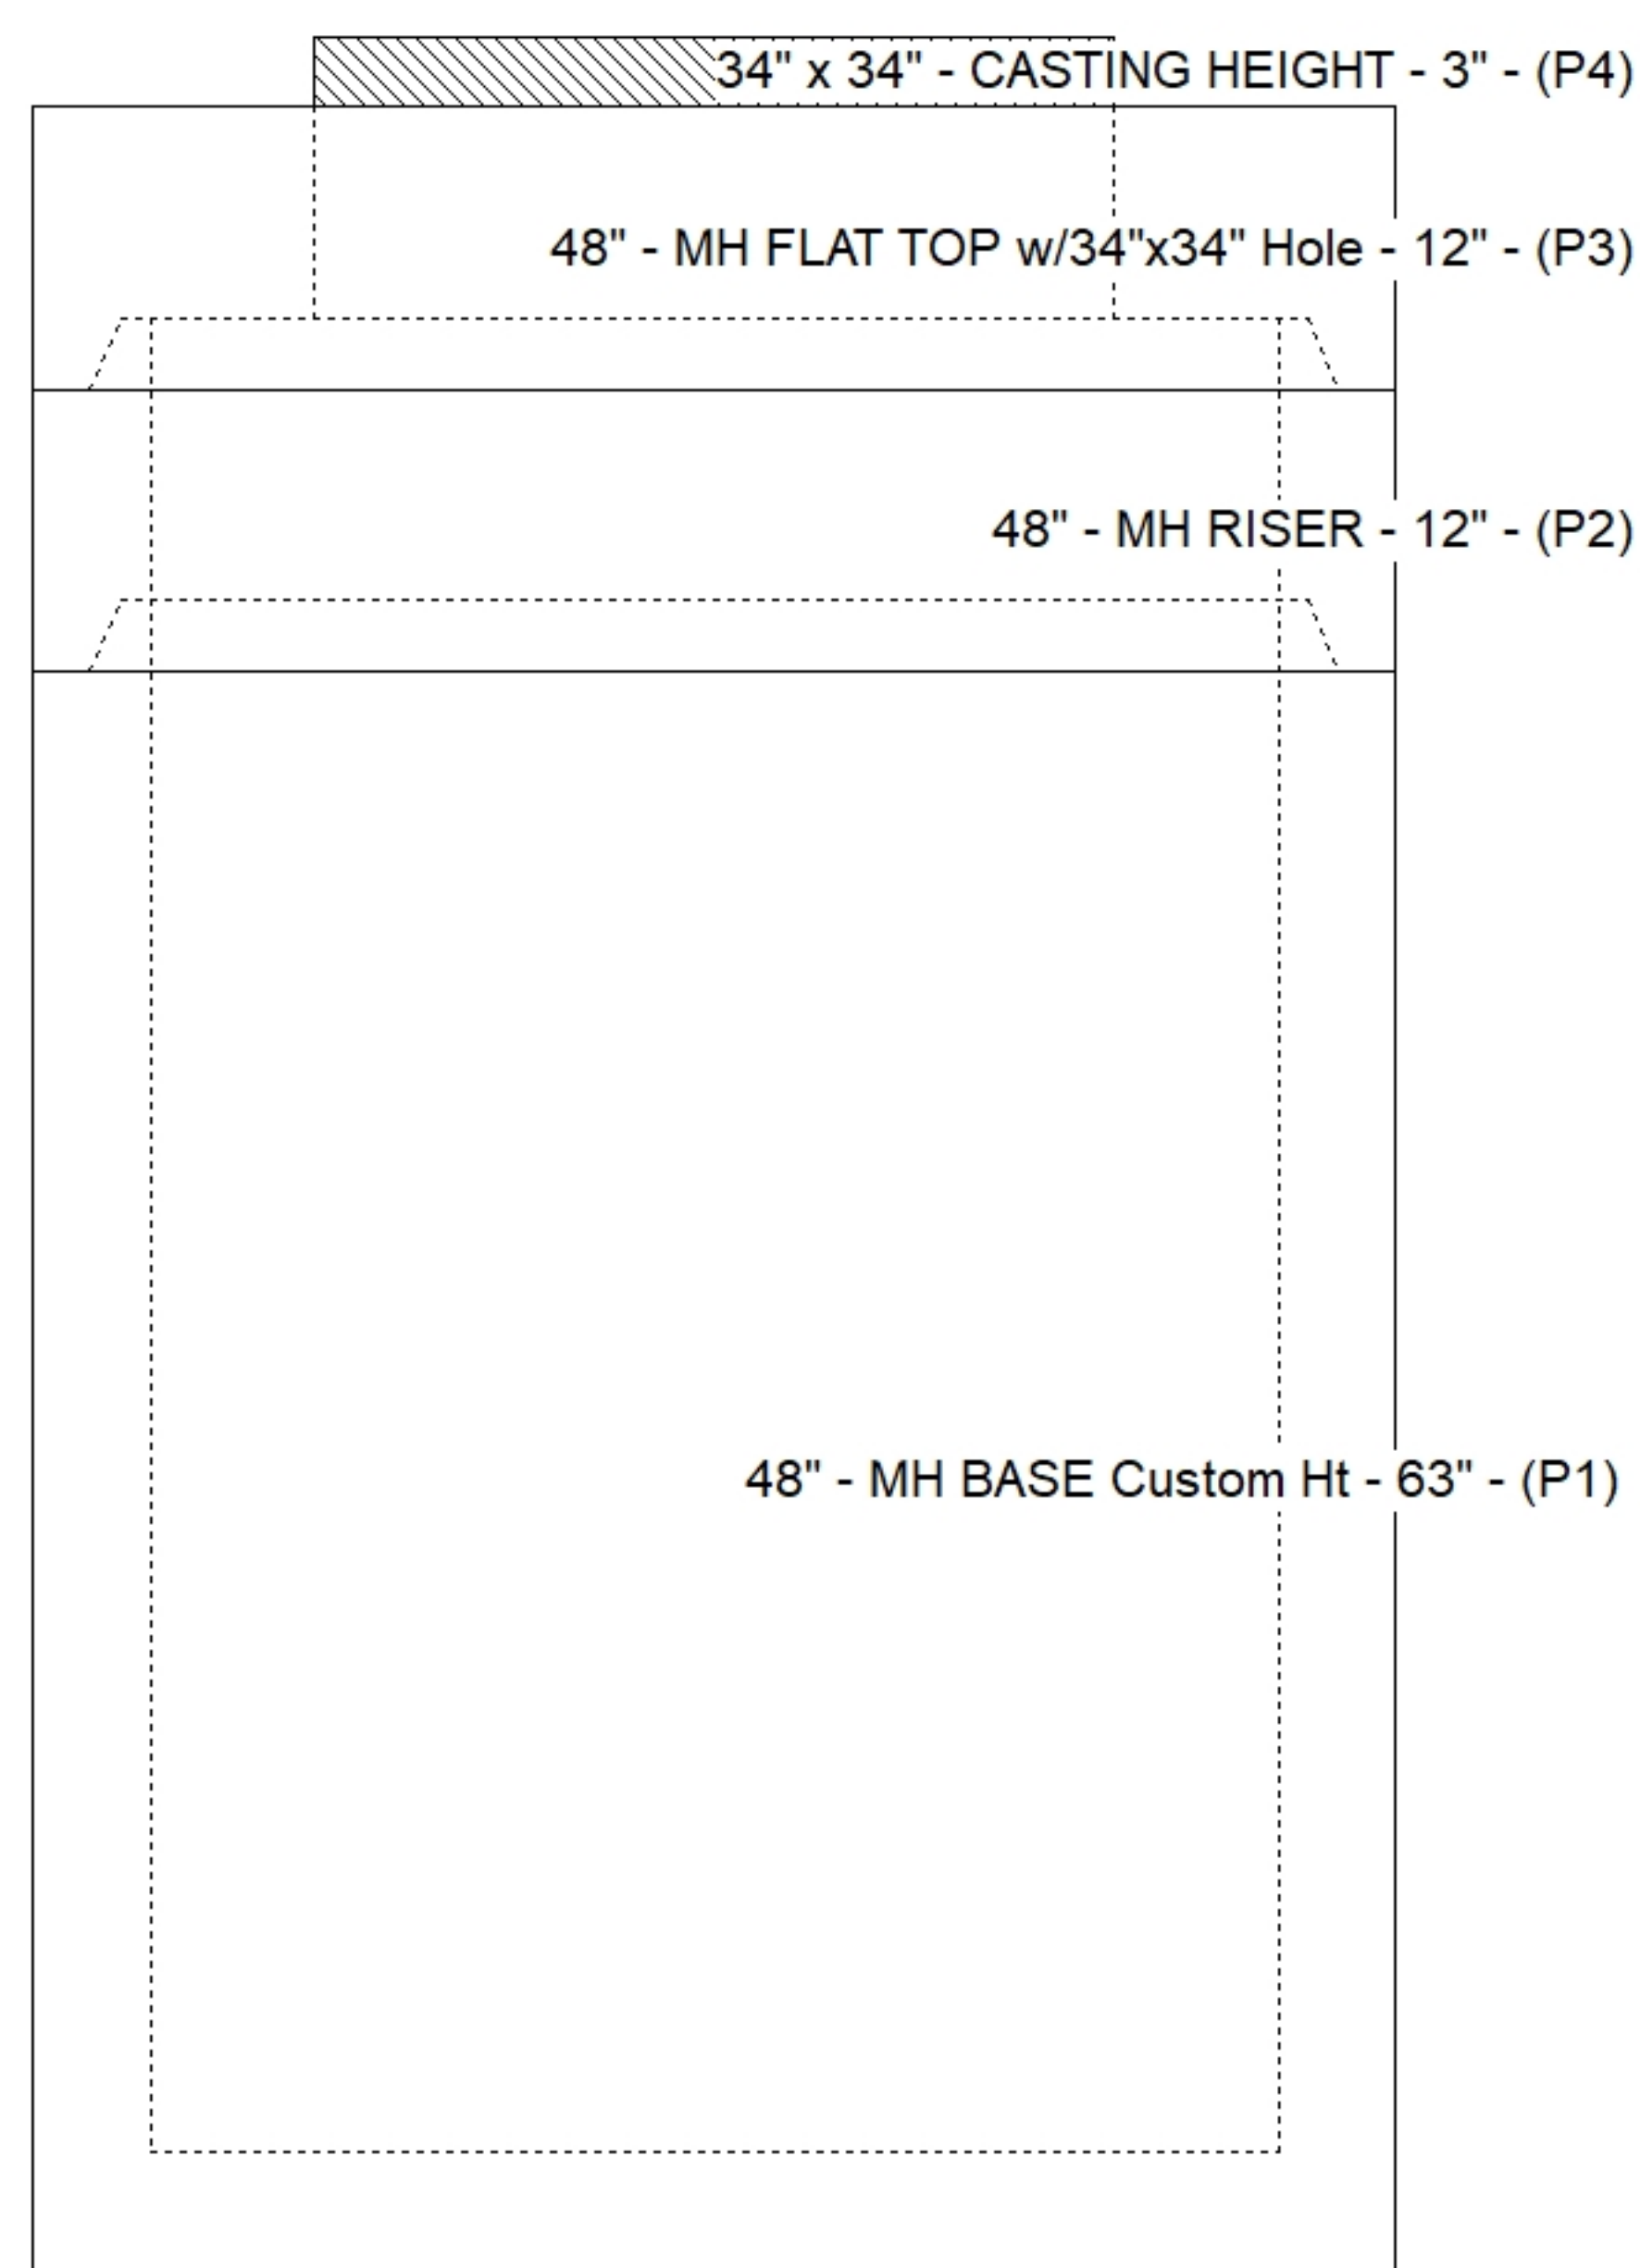

Default - Interior Dimensions

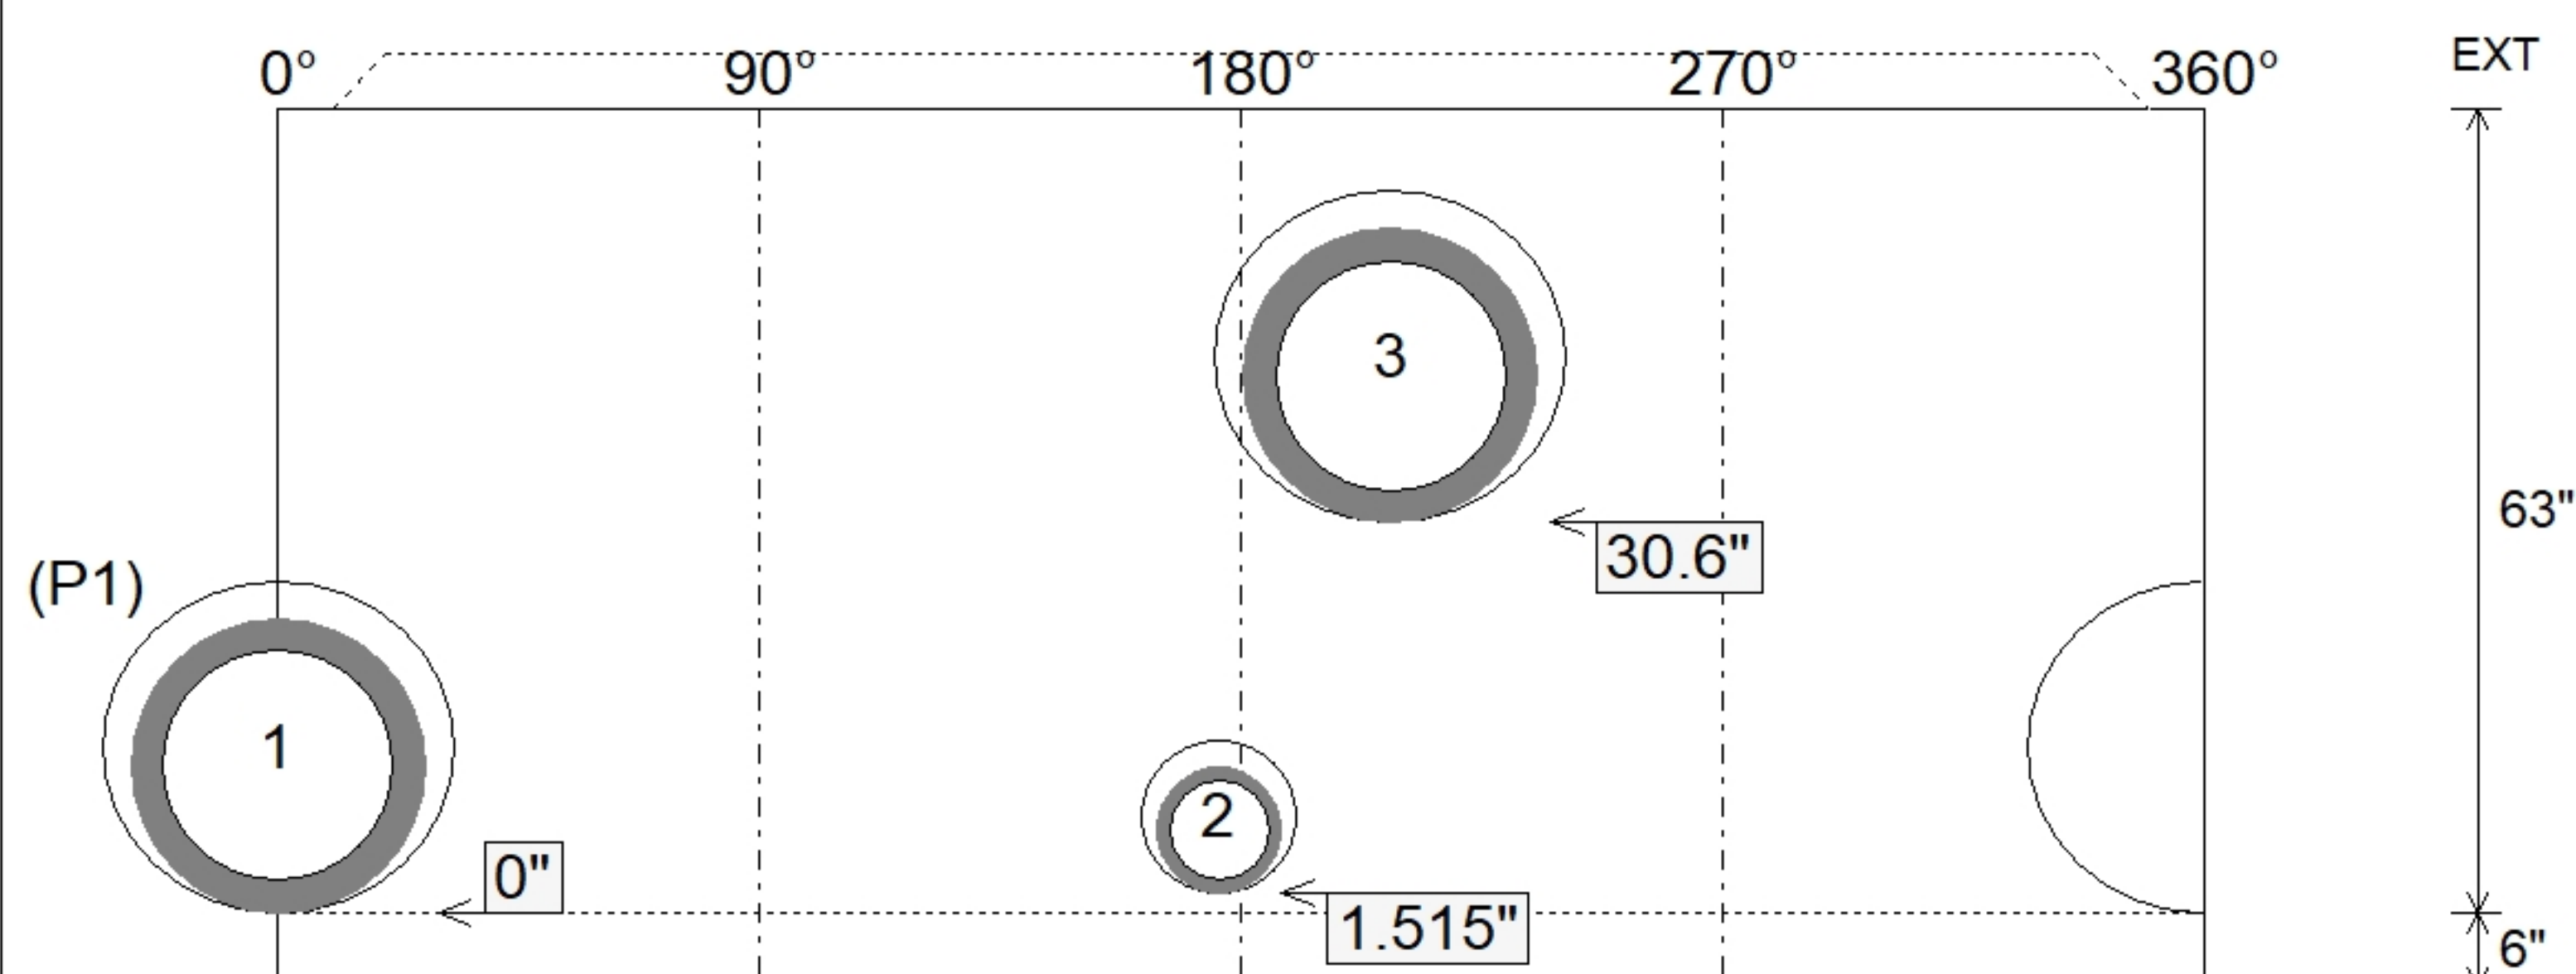

Submittal Drawing
10/9/2026 12:57:16 PM

SUBMITTAL
APPROVED BY:
