

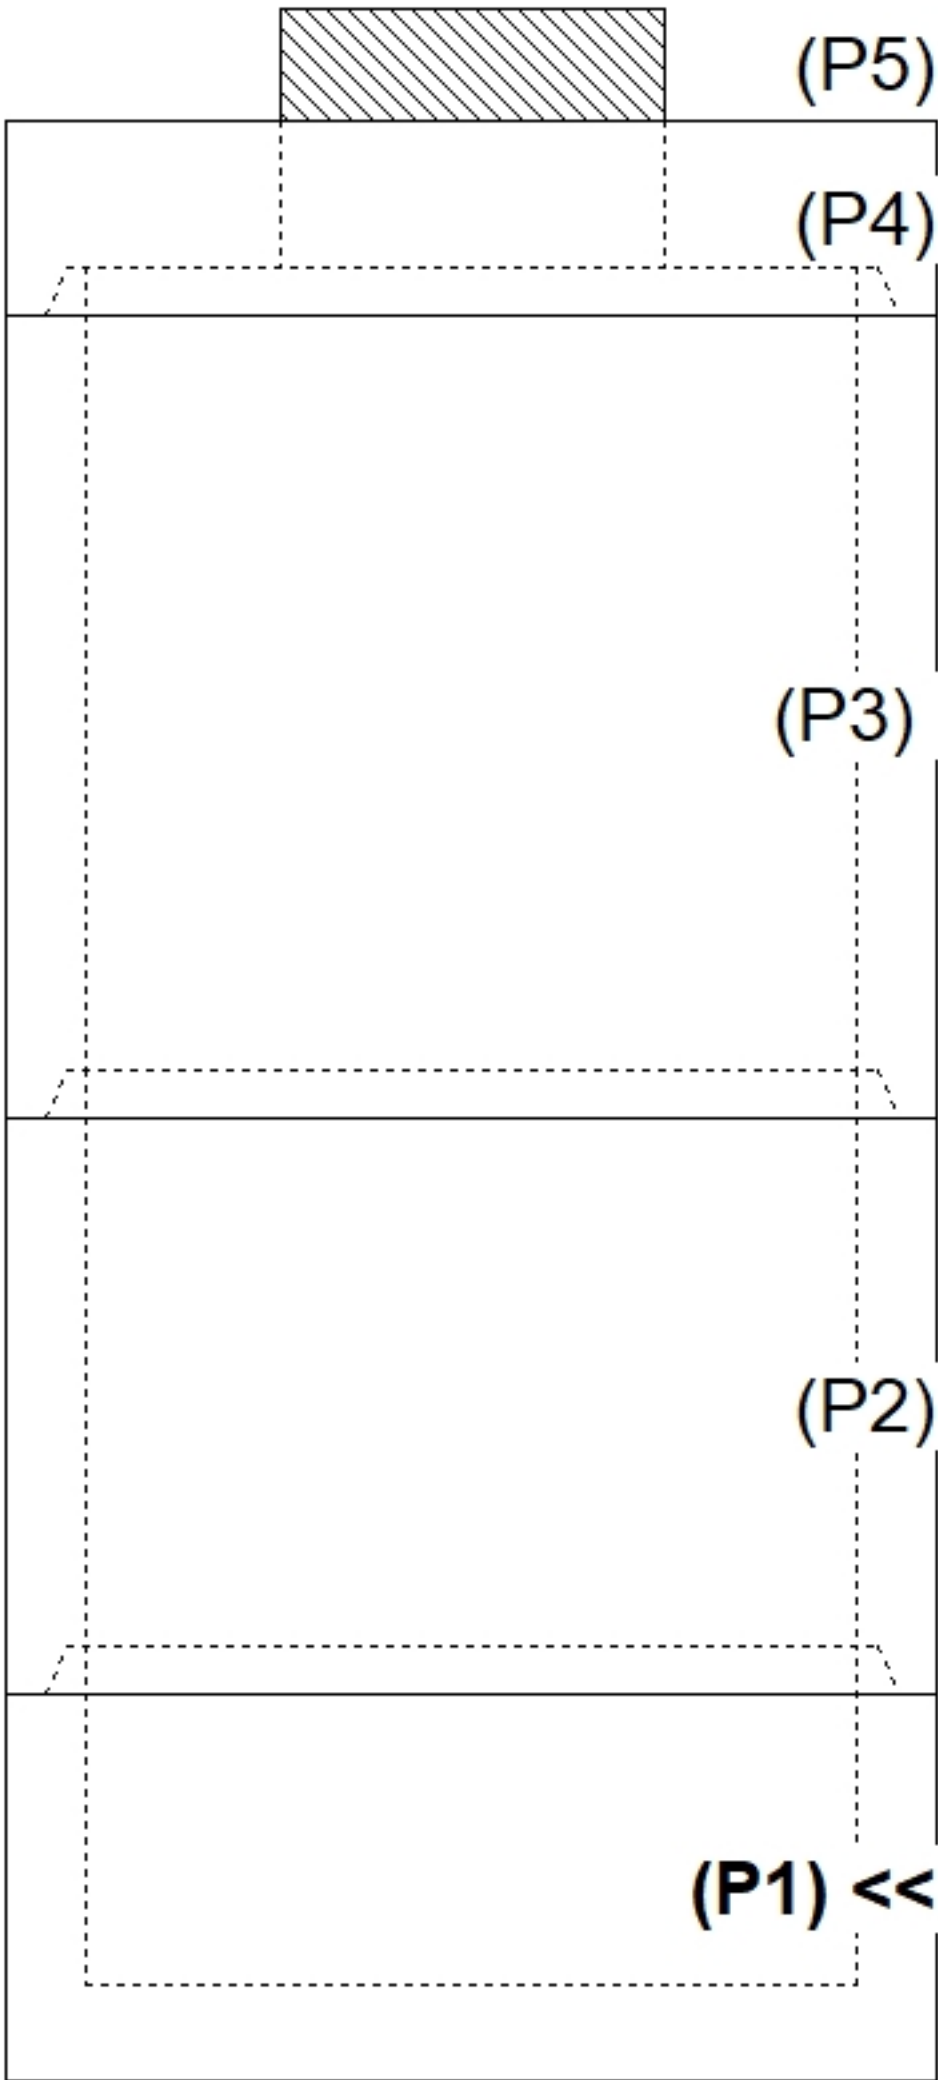
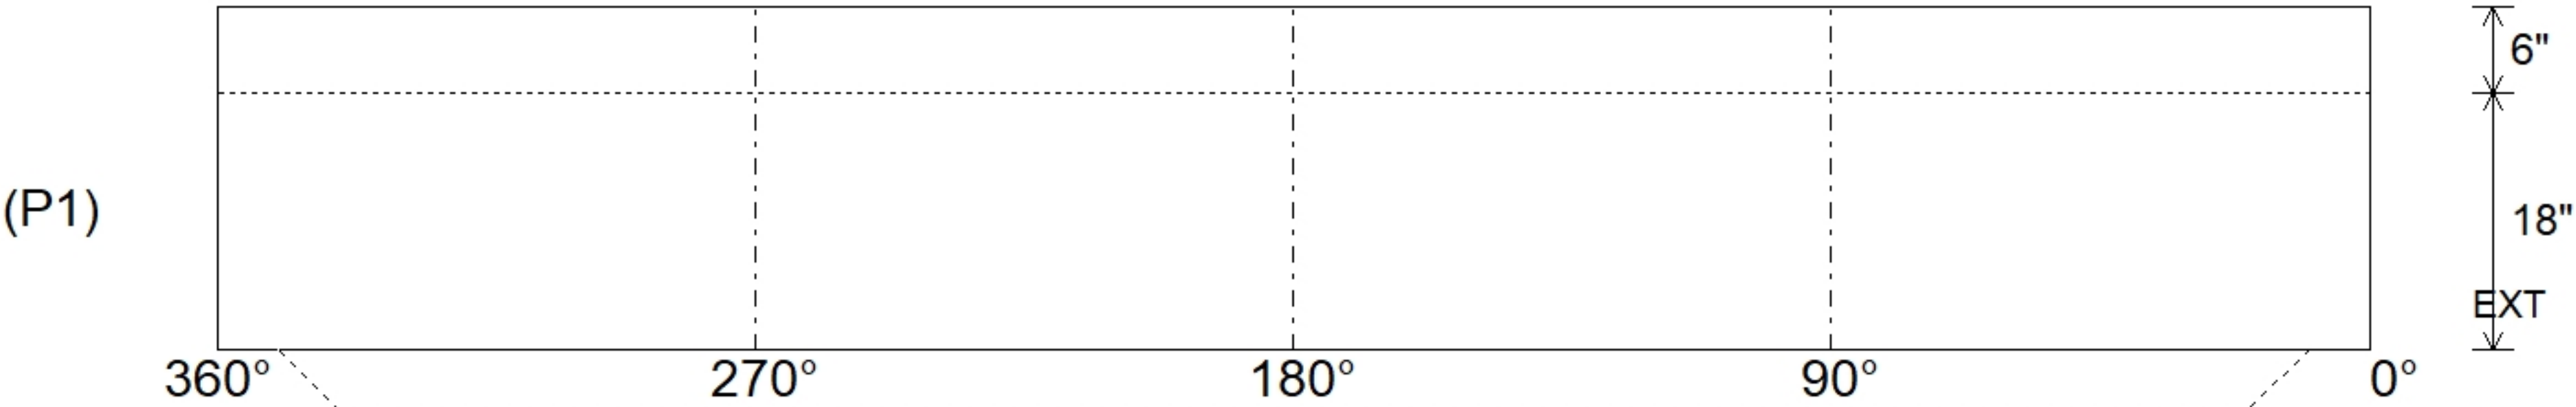


Job Name: 26-2447 ADS West Wilson Middle Job Location: Mt Juliet, TN Contractor: ADS Advanced Drainage Systems, Inc.				Plant: Beaver Dam 6/4/2026 9:27:15 AM		Tech: S. Felletter PC: T. Ryan						
Structure ID: QL1												
P1		MH048BA18		MH BASE T/n								
P5) 24" - CASTING HEIGHT - 7" P4) 48" - MH FLAT LID w/24" Center Hole F/G - 12" P3) 48" - MH RISER Custom Ht T/G - 50" P2) 48" - MH RISER T/G - 36" P1) 48" - MH BASE T/n - 18" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) ASSEMBLY REQUIRED 1) CASTING - HOE MC-375 F/C Storm 3) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) Hole - 20						0 lb 1580 lb 3222 lb 2515 lb 2588 lb 0 lb 0 lb 0 lb 271 lb 0 lb 0 lb 0 lb ----- 10176 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-375 F/C "STORM"). 4. LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE. 5. P2 & P3 RISERS TO BE MECHANICALLY ATTACHED BEFORE INTERNAL INSTALLATION/DELIVERY. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 553.9'		Rim to Invert: 3.55'		Slack: 0.6"		Sump: 81"		Step Position: 0°				
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset		
Invert 1												
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												
RIGHT-SIDE UP VIEW (int. dimensions)  UPSIDE-DOWN VIEW (int. dimenions) 												
 INSIDE WALL DIMENSIONS 												
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 5" Floor Height: 6"		Height (Int): 18" Height (Ext): 24"		Weight (Net): 2588 lb Volume (Net): 0.66cu.yd			
