




Job Name: 26-2478 - Marcelina Site Improvements (Storm) Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam, KY 10/8/2026 8:24:34 AM		Tech: J. Coppage PC: T. Lewis			
Structure ID: S0 ST-CI										
P1 MH048BAVF		MH BASE Custom Ht								
P3) 24" x 34" - CASTING HEIGHT - 6.5" P2) 48" - MH FLAT TOP w/24"x34" Hole - 12" P1) 48" - MH BASE Custom Ht - 64" 1) 48" - Conseal CS-102 1.00" 1) 24" x 34" - Conseal CS-102 1.00" 1) Hole - 24 1) Hole - 12 5) MH Step ML-10-TDS-NCR - 10"					0 lb 1839 lb 5603 lb 0 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 7442 lb		Structure Notes: . 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: - FLAT LID: #5 BAR @ 6" C.C. E.W. (GRADE 60) - BASE: PER ASTM A615 4. NO INVERT CHANNEL 5. STEPS AT 90 DEGREES 6. 6.5" CASTING SUPPLIED BY OTHERS			
Rim: 517.72' Rim to Invert: 7.05' Slack: 2.1" Sump: 0" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	510.67'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	-1.6"	0"
Invert 2	510.67'	180°	91.106"	8" HDPE	9.1"	Hole 12	12"	12.129"	-0.55"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

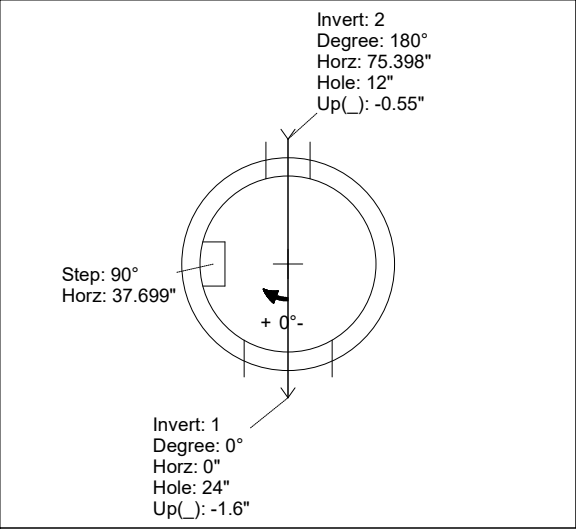

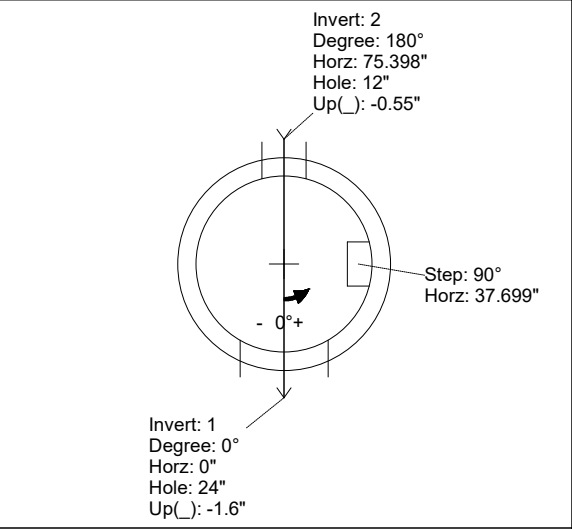

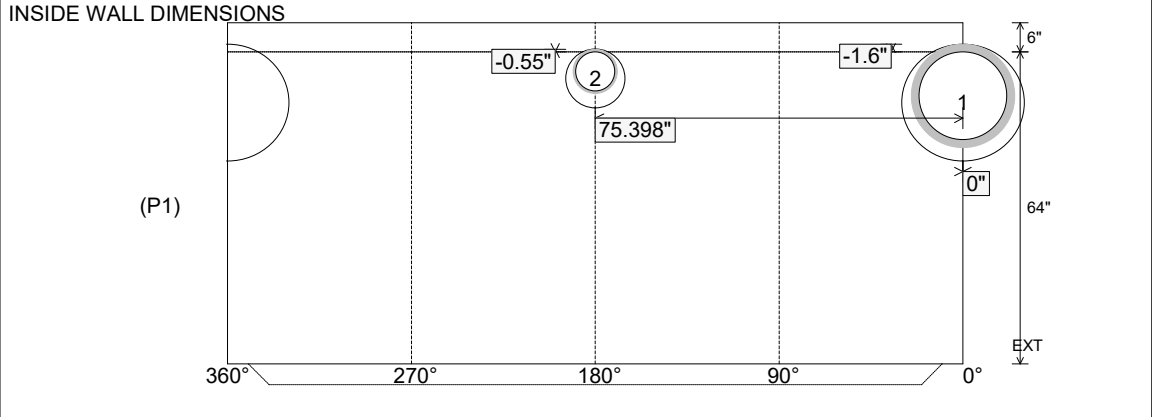

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 64" Height (Ext): 70"	Weight (Net): 5603 lb Volume (Net): 1.43cu.yd
----------------------------------	---------------------------------	--	--	--
