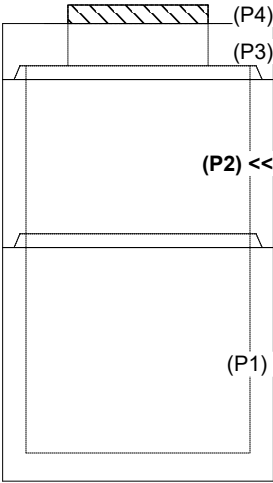




Job Name: 26-2478 - Marcelina Site Improvements (Storm) Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam, KY 10/8/2026 8:36:12 AM		Tech: J. Coppage PC: T. Lewis				
Structure ID: S14 ST-AD											
P2		MH048RS36		MH RISER							
P4) 30" x 30" - CASTING HEIGHT - 4" P3) 48" - MH FLAT TOP w/30"x30" Hole - 12" P2) 48" - MH RISER - 36" P1) 48" - MH BASE Custom Ht - 44" 2) 48" - Conseal CS-102 1.00" 1) 30" x 30" - Conseal CS-102 1.00" 1) Hole - 24 7) MH Step ML-10-TDS-NCR - 10"						0 lb 1350 lb 2515 lb 4207 lb 0 lb 0 lb 0 lb 0 lb ----- 8072 lb		Structure Notes: . 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: - FLAT LID: #5 BAR @ 6" C.C. E.W. (GRADE 60) - BASE & RISER: PER ASTM A615 4. NO INVERT CHANNEL 5. STEPS AT 260 DEGREES 6. 4" CASTING SUPPLIED BY OTHERS			
Rim: 506.69' Rim to Invert: 8.19' Slack: 2.28" Sump: 0" Step Position: 260°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 36" Height (Ext): 36"		Weight (Net): 2515 lb Volume (Net): 0.64cu.yd		
