




Job Name: 26-2478 - Marcelina Site Improvements (Storm) Job Location: Clarksville, TN 37043 Contractor: Core & Main LP				Plant: Beaver Dam, KY 10/8/2026 8:24:38 AM		Tech: J. Coppage PC: T. Lewis				
Structure ID: S8 ST-AD										
P1 MH048BAVF			MH BASE Custom Ht							
P3) 30" x 30" - CASTING HEIGHT - 4" P2) 48" - MH FLAT TOP w/30"x30" Hole - 12" P1) 48" - MH BASE Custom Ht - 56" 1) 48" - Conseal CS-102 1.00" 1) 30" x 30" - Conseal CS-102 1.00" 2) Hole - 30 5) MH Step ML-10-TDS-NCR - 10" Structure Total: 5960 lb						Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: - FLAT LID: #5 BAR @ 6" C.C. E.W. (GRADE 60) - BASE: PER ASTM A615 4. NO INVERT CHANNEL 5. STEPS AT 90 DEGREES 6. 4" CASTING SUPPLIED BY OTHERS				
Rim: 511.9'		Rim to Invert: 6'		Slack: 1.9"		Sump: 1.9"		Step Position: 90°		
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	505.9'	0°	0"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"
Invert 2	505.9'	270°	136.659"	24" HDPE	27.8"	Hole 30	30"	32.406"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

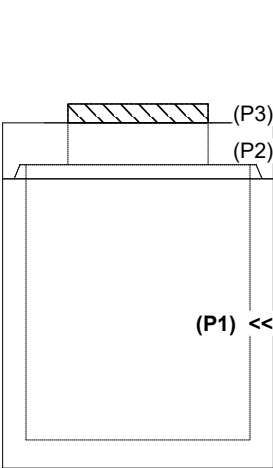

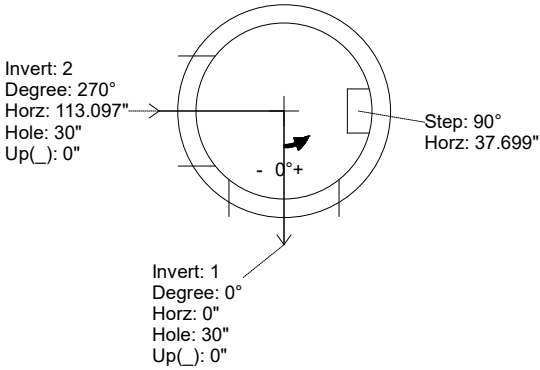

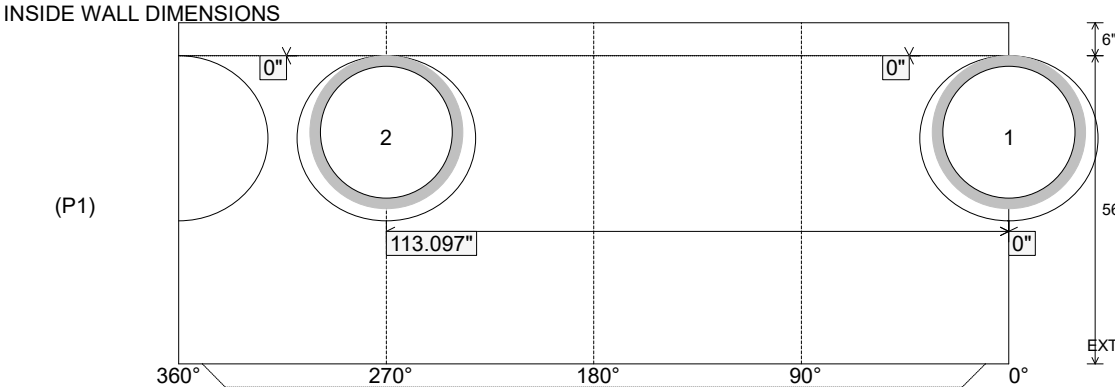

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 56" Height (Ext): 62"	Weight (Net): 4610 lb Volume (Net): 1.18cu.yd
----------------------------------	---------------------------------	--	--	--
