



Job Name: 26-2478 - Marcelina Site Improvements (Storm) Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam, KY 10/8/2026 8:24:50 AM		Tech: J. Coppage PC: T. Lewis				
Structure ID: T2 ST-CI											
P1 MH060BA60		MH BASE									
P3) 24" x 34" - CASTING HEIGHT - 6.5" P2) 60" - MH FLAT TOP w/24"x34" Hole - 13" P1) 60" - MH BASE - 60" 1) 60" - Conseal CS-102 1.00" 1) 24" x 34" - Conseal CS-102 1.00" 2) Hole - 44" 5) MH Step ML-10-TDS-NCR - 10" Structure Total: 9592 lb						0 lb 2279 lb 7314 lb 0 lb 0 lb 0 lb 0 lb ----- 9592 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: - FLAT LID: #5 BAR @ 6" C.C. E.W. (GRADE 60) - BASE: PER ASTM A615 4. NO INVERT CHANNEL 5. STEPS AT 270 DEGREES 6. 6.5" CASTING SUPPLIED BY OTHERS			
Rim: 513.8'		Rim to Invert: 6.59'		Slack: 2.43"		Sump: 2.85"		Step Position: 270°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	507.21'	0°	0"	36" HDPE	41.7"	Hole 44	44"	49.393"	0"	0"	
Invert 2	507.21'	138°	86.708"	36" HDPE	41.7"	Hole 44	44"	49.393"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

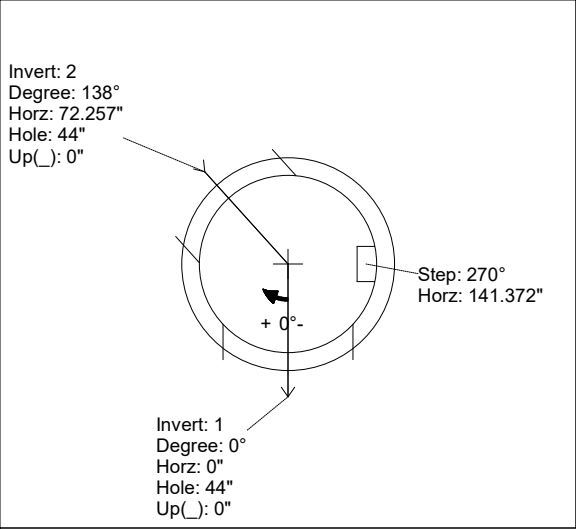

UPSIDE-DOWN VIEW (int. dimensions)

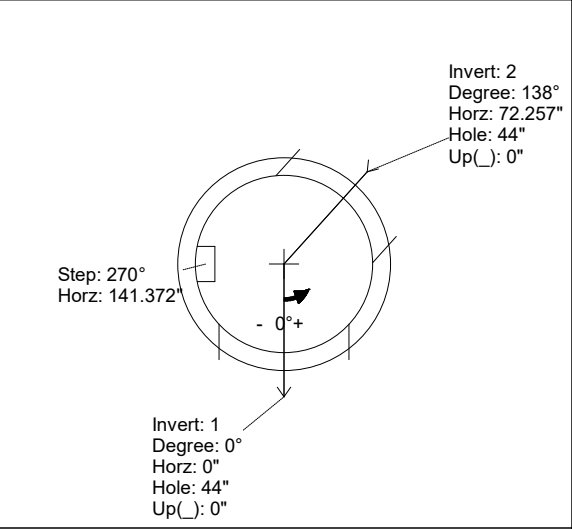

INSIDE WALL DIMENSIONS

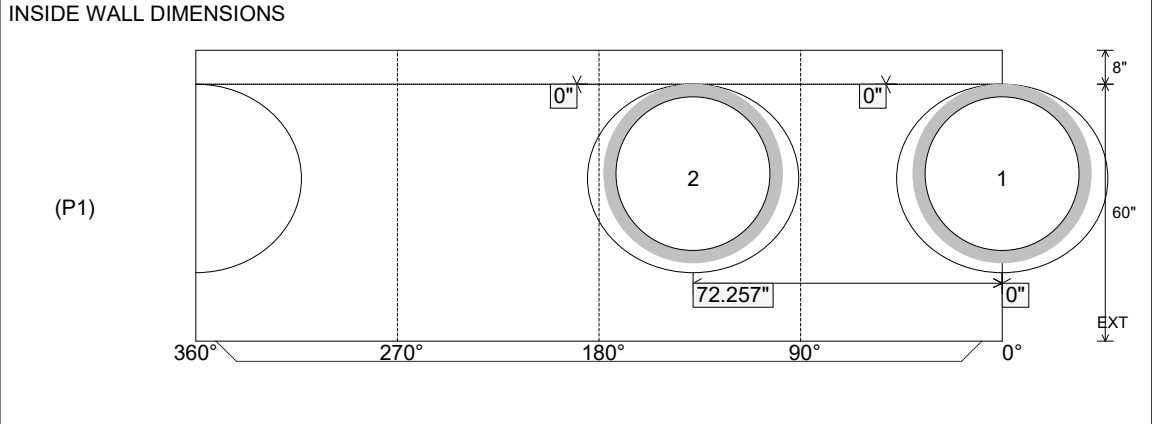

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 60" Height (Ext): 68"	Weight (Net): 7314 lb Volume (Net): 1.87cu.yd
----------------------------------	---------------------------------	--	--	--
