


Job Name: 26-2478B - Marcelina Site Improvements San.
Job Location: Clarksville, TN 37043
Contractor: Core & Main LP

Plant: Beaver Dam

Tech: J. Coppage

9/14/2026 4:53:43 PM

PC: T. Lewis



Structure ID: FS6 SS-MH

P3 GR3CDARED

GRADE RING w/ConBlock-CDA Red F/F


- P4) 24" - CASTING HEIGHT - 6"
P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3"
P2) 48" - ECC CONE w/ 24" HOLE, w/ConBlock-CDA Red F/G - 42"
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT
1) 48" - Conseal CS-102 1.00" (Double)
2) 24" - Conseal CS-102 1.00" (Double)
2) PSX - 16Y NYLO
6) MH Step ML-10-TDS-NCR - 10"

Structure Total:


0 lb
202 lb
3116 lb
3255 lb
0 lb
0 lb
1440 lb
0 lb
0 lb
16 lb
0 lb
8029 lb

Structure Notes:


1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: (1) #3 HOOP CENTERED (GRADE 60)
4. CONBLOCK CDA RED ADMIXTURE REQUIRED

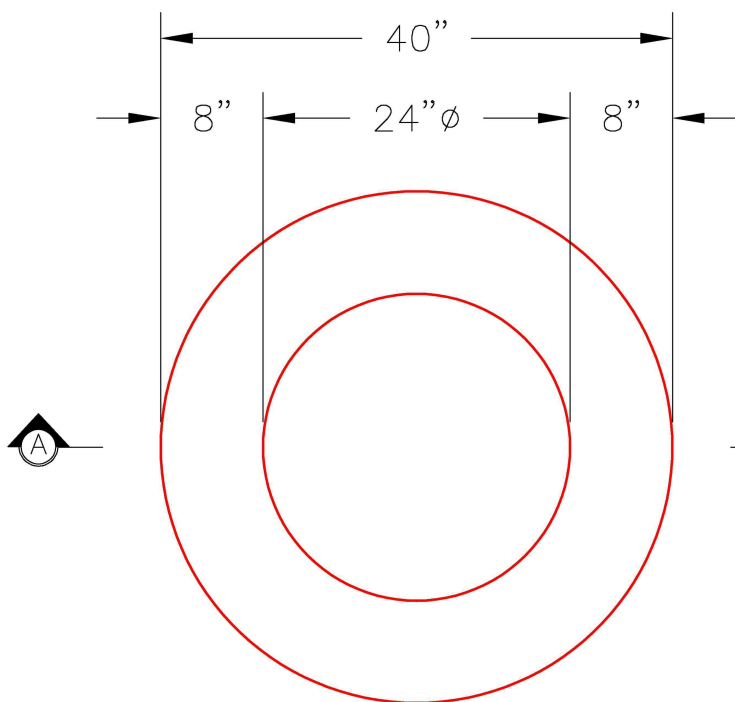

PLAN VIEW



ISOMETRIC VIEW

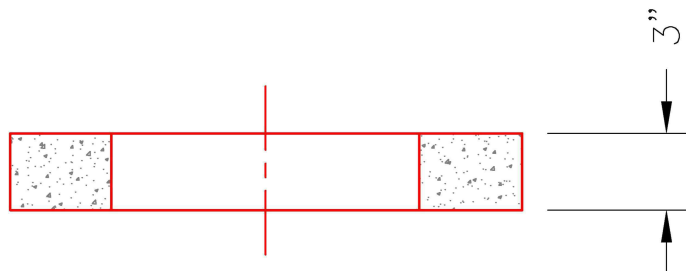

SECTION A-A

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 3"

Weight (Net): 202 lb
Volume (Net): 0.05cu.yd
