



Job Name: 26-2478B - Marcelina Site Improvements San. Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam 9/14/2026 4:50:06 PM		Tech: J. Coppage PC: T. Lewis				
Structure ID: FS8 SS-MH											
P2 MH060RS48CDARED					MH RISER w/ConBlock-CDA Red T/G						
P5) 24" - CASTING HEIGHT - 6" P4) 60" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 13" P3) 60" - MH RISER w/ConBlock-CDA Red T/G - 48" P2) 60" - MH RISER w/ConBlock-CDA Red T/G - 48" P1) 60" - MH BASE Custom Ht, w/ConBlock-CDA Red T/n - 26" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 60" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16Y NYLO 10) MH Step ML-10-TDS-NCR - 10"					0 lb 2800 lb 5011 lb 5011 lb 5243 lb 0 lb 0 lb 2962 lb 0 lb 0 lb 16 lb 0 lb		Structure Notes: . 1. (6" TALL CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60).				
Rim: 487.3' Rim to Invert: 11.5' Slack: 0" Sump: 3" Step Position: 97°					Structure Total: 21043 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

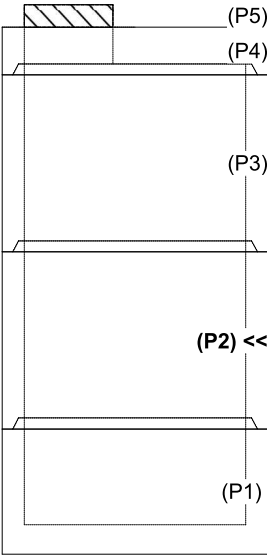


(P5)
(P4)
(P3)
(P2) <<
(P1)

RIGHT-SIDE UP VIEW (int. dimensions)



Step: 97°
Horz: 50.75"

INSIDE WALL DIMENSIONS

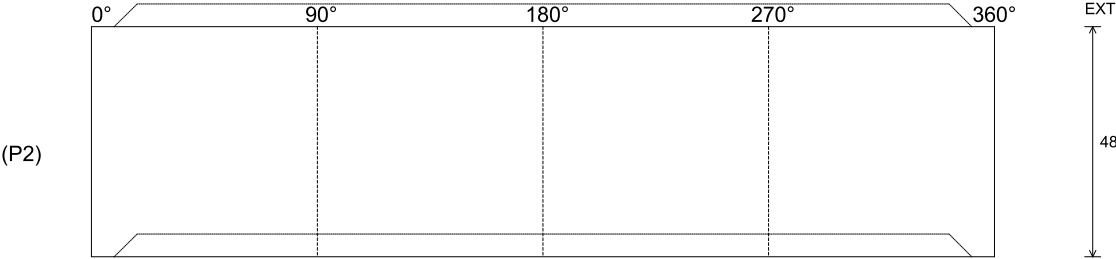

(P2)

0° 90° 180° 270° 360°

EXT 48"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 48" Height (Ext): 48"	Weight (Net): 5011 lb Volume (Net): 1.28cu.yd
----------------------------------	------------------------------------	--	--	--
