



Job Name: 26-2478B - Marcelina Site Improvements San. Job Location: Clarksville, TN 37043 Contractor: Core & Main LP					Plant: Beaver Dam 9/14/2026 4:50:08 PM		Tech: J. Coppage PC: T. Lewis				
Structure ID: FS9 SS-MH											
P3 MH060RS72CDARED					MH RISER w/ConBlock-CDA Red T/G						
P6) 24" - CASTING HEIGHT - 6" P5) 24" - GRADE RING w/ConBlock-CDA Red F/F - 6" P4) 60" - MH FLAT TOP w/24" Hole ECC w/ConBlock-CDA Red F/G - 13" P3) 60" - MH RISER w/ConBlock-CDA Red T/G - 72" P2) 60" - MH RISER w/ConBlock-CDA Red T/G - 60" P1) 60" - MH BASE Custom Ht. w/ConBlock-CDA Red T/n - 32" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 3) 60" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 16Y NYLO 1) PSX - 12-08 NYLO 13) MH Step ML-10-TDS-NCR - 10"					0 lb 405 lb 2800 lb 7459 lb 6264 lb 5869 lb 0 lb 0 lb 2962 lb 0 lb 0 lb 16 lb 8 lb 0 lb		Structure Notes: . 1. (6" TALL CASTING PROVIDED BY OTHERS) 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. ADMIXTURE = CONBLOCK CDA RED. 5. REINFORCING PER ASTM A615 (GRADE 60). 6. INTERNAL DROP PROVIDED BY OTHERS - ICAST TO SUPPLY OPENINGS & BOOTS				
Rim: 493.6' Rim to Invert: 15.6' Slack: 1.2' Sump: 3' Step Position: 74°					Structure Total: 25783 lb						
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (⌋)	Offset	
Invert 1											
Invert 2											
Invert 3	486.54'	265°	166.5"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.081"	6.75"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

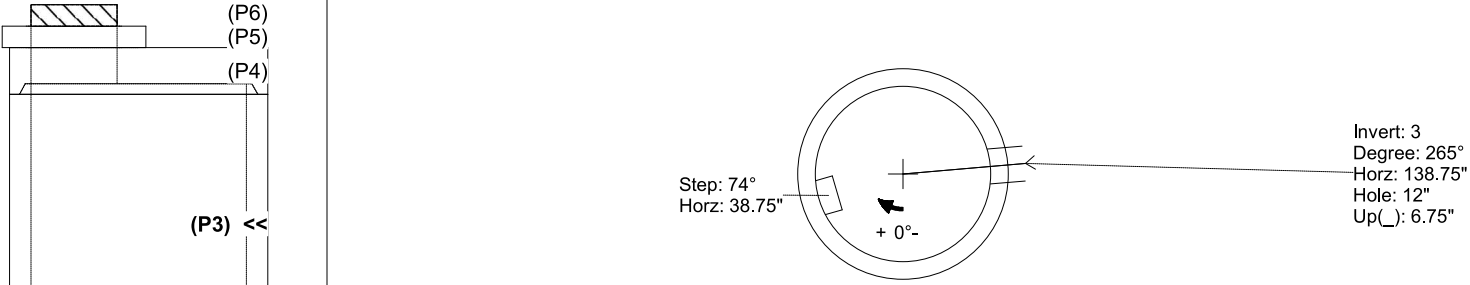

INSIDE WALL DIMENSIONS

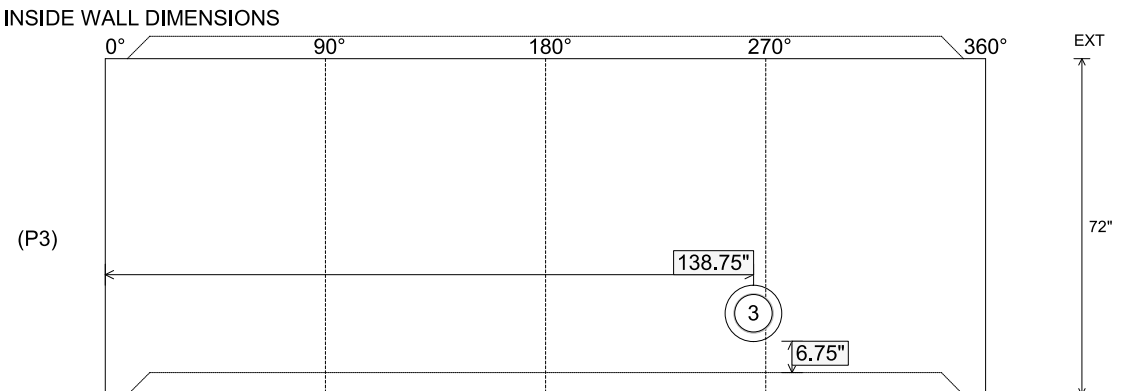

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 6" Floor Height: 0"	Height (Int): 72" Height (Ext): 72"	Weight (Net): 7459 lb Volume (Net): 1.9cu.yd
----------------------------------	------------------------------------	--	--	---
